Formcraft
DESIGN & CONSTRUCTION

FOUNDERS' GUIDE · VERSION 1.0

The Formcraft Command Centre

The system that runs Formcraft: what it is, why we built it, how every part works, how to use it every day, and the plan to finish it.

Formcraft Studio · Formcraft Construction · Formcraft Concrete · Formcraft Stores

For Emlyn Atochon, Peter Isingoma and Esther Ahumuza
Formcraft Design and Construction · Kampala · 30 October 2026
Confidential: for the founders

How to read this guide

This guide is for the three of us. It teaches you the Command Centre from nothing, and it also holds the whole logic behind it, so anyone we hire, or any AI we connect, can learn from the same book. Read Parts 1 to 3 in one sitting (about an hour). Use Parts 4 to 8 as a reference when you open a page for the first time.

Plain text

What a part is for and why it matters. Written for someone who has never seen the app.

Do this

1. Numbered steps
2. are how to use it.

Under the hood

The technical logic: which data it stores, which rules and automations drive it. For whoever builds or fixes it.

About the screenshots. Every screenshot is the real Command Centre, taken on 30 October 2026. To make the screens readable they show a small set of **example data** (the Okello quote, a clinic lead, a sketch of a house). The live system does not hold that data. Entering our real business is the first job (Part 3).

Contents

How to read this guide 2

1 One system that runs Formcraft 6

- What it does for each founder 6
- The goal it serves 6
- By the numbers 7
- Why it makes the plan more likely 7

2 The big picture 9

- Four principles 9
- The work loop: how a job gets done 11
- The cheapest path: six levels 12
- AI models, agents and memory 13
- The eight agents 13
- Memory: why switching AI loses nothing 14
- The AI workforce 15
- Approvals, roles and who uses what 16
- Where the data lives 17

How the data is kept safe 17

3 A tour of the screen 19

Your first week: put the real business in 20

The routine 20

Logging by hand and talking to the AI 20

4.1 Main menu 22

4.2 Business pages 33

4.3 Build and AI pages 49

4.4 Registers 60

4.5 Control pages 62

5 Lead to cash 68

Client onboarding, step by step (Studio design) 68

Sketch to building 70

The content factory 71

Events 71

Standards bank 55

Professionals directory 72

The money cycle 73

How AI work becomes scripts 73

6 The automation catalogue 75

The first ten to switch on 76

7 Where we are 78

The roadmap 78

The 90-day focus rule 79

Foundation sprint, week by week 79

The Formcraft Hub for Windows 80

Revit, voice and the rules for building 82

A simpler Revit plugin 82

Voice 82

Rules for building 82

8 The gaps, ranked 84

Real, but not plan-stopping 84

The next 30 days 85

Decisions we need from the founders 85

A Appendix: glossary and technical reference 86

Where everything is 86

Design studio keys 87

PART 1

The pitch

Why Formcraft needs one system, what it does for each of us, and how it serves the five-year goal: the top design and construction firm in East Africa.

Formcraft
DESIGN & CONSTRUCTION

1 One system that runs Formcraft

Formcraft is three founders running five businesses at once: Studio (design), Construction, Concrete, Stores and Formcraft Tools for Revit. Each one has clients, money, deadlines, suppliers, content and compliance. Kept in heads, WhatsApp chats and spreadsheets, that work grows faster than three people can carry it. The Command Centre is the answer: **one place where the whole business lives, where AI agents do the routine work, and where the founders decide and check.**

The problem

- Leads arrive by website, WhatsApp, calls and events, and some are never answered within a day.
- Quotes take days; prices are guessed instead of tied to the plan.
- Money, tax dates and cash runway are checked only when there is a problem.
- Content, the YouTube channel and the website need daily work nobody has time for.
- Everything depends on what each founder remembers.

The answer

- Every lead, quote, project, shilling, task and document in one database.
- A morning brief that tells each founder what needs them today.
- AI agents and scripts that draft, chase, price, post and log, with nothing applied until a founder approves.
- The company's rules and memory written down, so any model, and any new hire, continues from them.
- Built to grow into a fully automated business.

What it does for each founder

Founder	Runs and approves	What the Command Centre takes off them
Emlyn Atochon Design, BIM, software, admin	Revit and model jobs, automations, connections, AI settings, releases of Formcraft Tools and the website	The design studio, family factory, tutorials, development room and the main hub on his PC
Peter Isingoma Projects, Concrete, real estate, finance	Site and project jobs, purchase orders, supplier payments, contracts (jointly with Emlyn), finance agent work	Site diaries, project flags, price book, supplier price calls, payroll, tax calendar, cash forecast
Esther Ahumuza Marketing, sales, interiors	Social posts, newsletters, enquiries and quotes, website content, sales agent work	Auto-quotes, follow-ups, the content plan, events, the professionals directory and campaigns

Roles as proposed in the pitch deck; to be confirmed by the founders (Part 8).

The goal it serves

The feasibility study sets the target: **the top design and construction firm in East Africa within five years**, which in numbers means about **USD 1 million of revenue a year by 2031**, on the way to a much longer journey (Formcraft Tools sold worldwide). The Command Centre tracks that journey in six phases.

1
P0 · Foundation sprint
Nov 2026 to Jan 2027
Core coding done, IP and shareholders' agreement signed, USD 15,000 buffer

2
P1 · Prove the model
2027
About USD 46,000 revenue, 20 then 50 leads a month, 2,000 YouTube subscribers

3
P2 · Kampala leader
2028 to 2029
The firm people in Kampala name first

4
P3 · East Africa
to 2031
Offices and partners across the region; about USD 1M a year

5
P4 · Africa
after 2031
Formcraft Tools and services across Africa

6
P5 · Global software
long term
Formcraft Tools as a global product

By the numbers

67
pages in the app

128
automations planned in 13 groups

28
AI staff roles, one per planned hire

8
AI agents with their own rulebooks

78
business systems mapped to the value chain

7
service lines with client on and offboarding

173
templates in the master register

5
AI tiers: scripts, offline, DeepSeek, Claude, Grok

Why it makes the plan more likely

The simulations behind the feasibility study are honest about software: on its own, a system adds only a little to the odds. What moves the odds is **cash discipline, steady sales, deposits and stage payments, and signed legal papers**. The Command Centre earns its place by making those things happen every day without relying on memory: the cash buffer is watched, every quote is priced to the plan, every lead gets a next step, every tax date is on the calendar, and every AI hour is spent on the cheapest tool that can do the job.

> **Where it stands today (30 October 2026).** The app is built and running, but it holds almost no real business yet: no deals, no projects, no ledger entries and no logged numbers. None of the 128 automations is live yet; they are designed, with recipes, and waiting to be built. The system becomes valuable the day we put the real business into it. Part 8 lists the honest gaps and the next 30 days.

PART 2

How the system works

The big picture, the four principles, the work loop, the AI ladder, who approves what, and where the data lives.

Formcraft
DESIGN & CONSTRUCTION

2 The big picture

Read the picture from top to bottom: people use the Command Centre, the Command Centre keeps everything in one database, AI and scripts propose work, founders approve it, and approved work goes out through the connections.

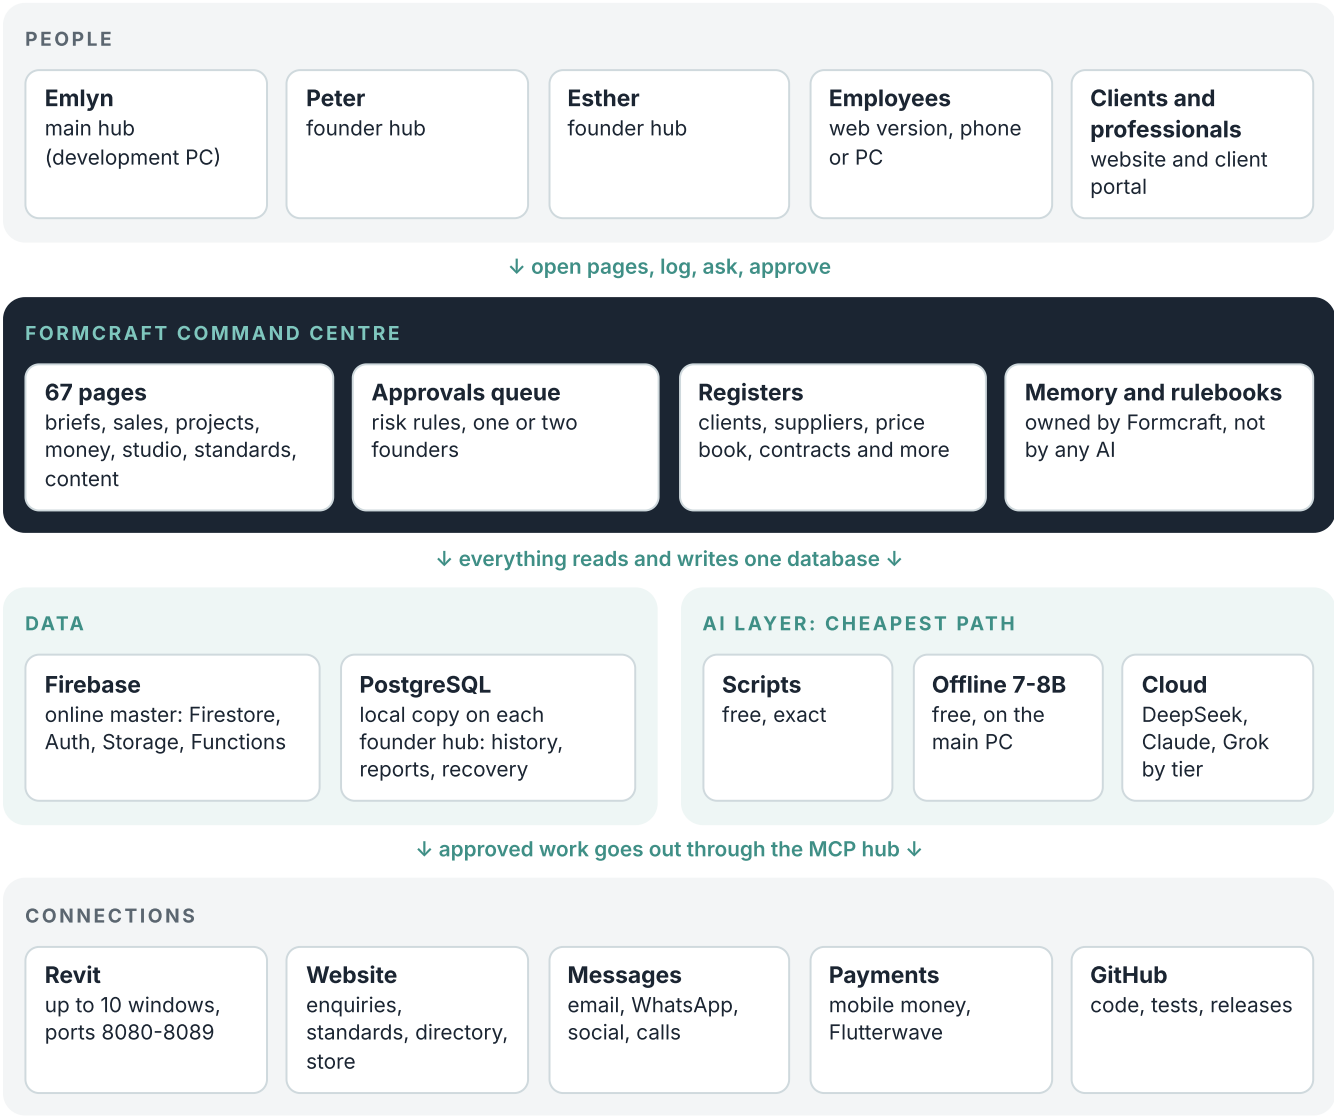

Four principles

1. Rules before automation

Every job is first written as a rulebook recipe: what to do, what to check, who approves. Only then is it scripted or handed to AI. A recipe that is not written does not get automated.

2. Scripts first, AI as the bridge

A script beats a model; a small offline model beats a large one; the large cloud models are kept for reasoning, development and review. AI uses scripts as its tools.

3. Nothing applied without approval

Agents propose; founders decide. Low-risk work runs and is logged, medium needs one founder, money over USD 500, contracts and releases need two.

4. The memory belongs to Formcraft

Memory, rulebooks and data live in our database, not inside any AI. We can switch Claude for Grok, DeepSeek or an offline model at any time and the new one continues from the same place.

The work loop: how a job gets done

Every piece of work, whether a reminder to chase an invoice or a new wall layout, goes through the same loop. This is the logic of the whole system on one page.

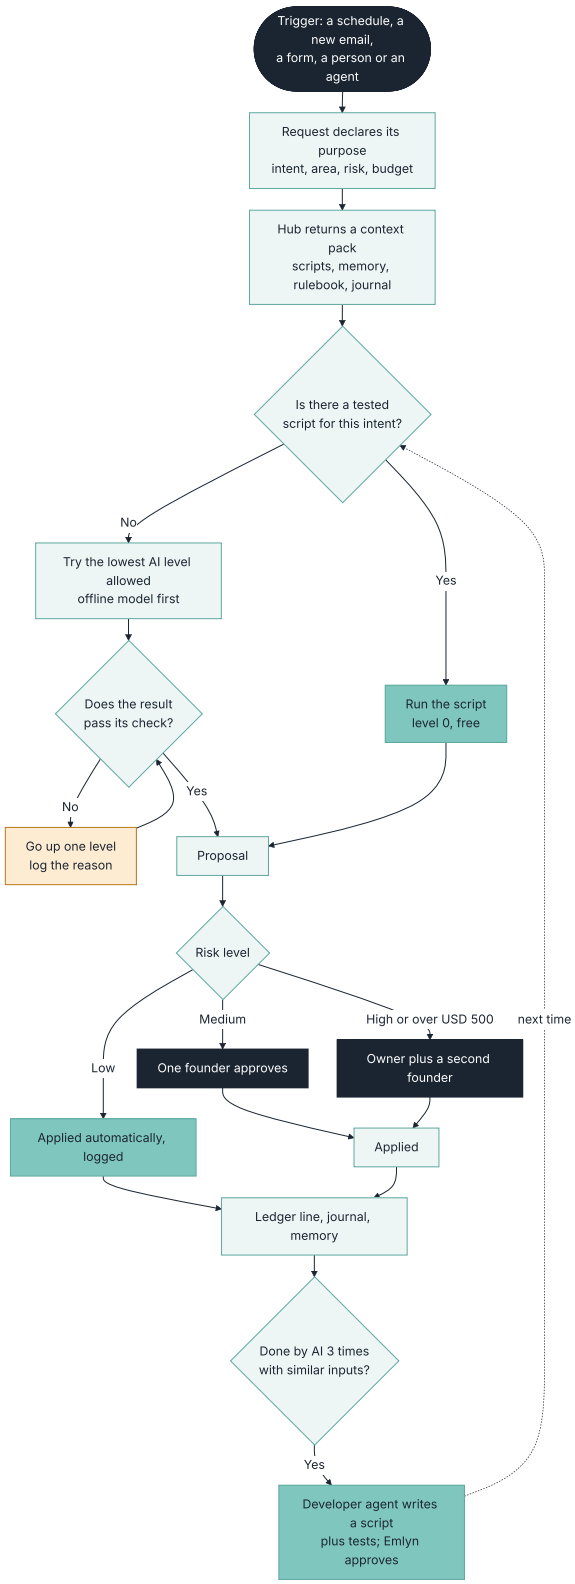

Figure 2.1 · The work loop. Teal boxes are free or automatic; dark boxes need a founder.

The cheapest path: six levels

For every task we use the cheapest thing that can do it correctly. Work starts at the bottom of the ladder and climbs one level only when a check fails. Every climb is logged with its reason, so we know which script to write next.

Level 5	**Chief, developer, reviewer** Planning, writing scripts and tests, development, hard reasoning, reviewing	Top cloud model (Claude)	**Highest**
Level 4	**Senior agents** Client-facing writing, multi-step reasoning, what level 3 failed	Mid cloud model (DeepSeek, Grok)	**Low**
Level 3	**Area agents** Drafts, summaries, simple tool chains, first-line replies	Offline 7-8B model	**Free**
Level 2	**Worker bots** Sorting, tagging, extracting fields, filling script inputs; output must pass a schema	Offline 3-4B model	**Free**
Level 1	**Rules and lookups** Routing, matching, filling templates: tables, formulas, regex	Code	**Free**
Level 0	**Scripts and tools** Anything already scripted and tested	Code	**Free**

How a job is routed

1. Look up the intent in the script table. If a tested script exists, run it.
2. Otherwise start at the lowest level allowed for that intent and check the result.
3. On a failed check go up one level, up to the maximum allowed. Log why.
4. If the budget runs out, stop and ask the owning founder. Never overspend silently.

How AI work becomes free

When the same intent has been done by AI three times with similar inputs, the developer agent (level 5) writes a script and its tests from those runs. Emlyn approves it; it joins level 0. If a promoted script later fails a check it is paused and the job goes back to AI until it is fixed.

Target: 50% of runs done by scripts by month 6, 80% by month 18.

UNDER THE HOOD

Every call carries a **purpose** (purpose, intent, area, started_by, agent, project, risk, budget_usd). The hub answers with a **context pack** (task id, scripts, tools, memory lines, rulebook link, journal, level, limits) holding references and short extracts, never data dumps. When the task ends the hub writes a journal note, any lesson to memory, and a ledger line (purpose, intent, level used, escalations, cost, time, result). Answers are cached by a hash of intent, inputs and context version. At 80% of a monthly budget, routing drops one level except for high-risk work. Spec: `docs/windows-hub-plan.md §15`.

AI models, agents and memory

We use three cloud families and one offline model, each for what it does best. Changing a model is a setting, not a rebuild.

Tier	Default model	Used for	Cost
Offline	7-8B model through Ollama on the main PC (3-4B for the quick jobs)	Sorting, tagging, drafts, summaries when Revit is not busy; works without internet	Free
Quick	DeepSeek	Cheap cloud work: extraction, standards summaries, simple replies	Lowest
Default	Claude	Daily agent work, client-facing writing, the morning brief	Medium
Complex	Claude (top model)	Design assistant, planning, development, reviewing	Highest
Second opinion	Grok	Reviewing another model's work: nobody grades their own work	Medium

The eight agents

Agent	Looks after
Chief of staff (general)	The whole business: keeps the founders accountable to the plan, joins up the other agents, runs the morning brief and the weekly review, decides which agent acts
Finance	Money, budget, cash forecast, payroll (PAYE, NSSF), tax calendar, invoices, receipts, debts, pricing. Never moves money; prepares and proposes
Sales and marketing	Leads, enquiries and auto-quotes, follow-ups, email list and campaigns, content, SEO, global reach
Projects and site	Projects, building playbook, drawings, RFIs, variations, site diary, defects, permits, quality
Design and BIM	Design studio, models, families, templates, standards checks
Software and automation	Formcraft Tools, the MCP server, automations, recipes, tests
People and admin	Staff, hiring, leave, training, the AI workforce scorecards
Legal and risk	Contracts, compliance calendar, data protection, risk register

Memory: why switching AI loses nothing

Short-term

Every exchange with the AI is kept for 7 days in the AI log.

Long-term

Once a week the AI consolidates what mattered into long-term memory: decisions, client preferences, lessons. Founders can pin lines.

Rulebooks

Each agent's written rules (`rulebooks/agents/*.md`). Errors become new rules so they never repeat.

A **handover pack** (JSON or Markdown) holds memory, rules and the current state. Give it to any AI tool and it continues where the last one stopped. The same pack is how an AI staff member hands its role to a new human hire.

UNDER THE HOOD

Collections `memory` , `ailog` , `aistaff` , `aiuse` , `pending` . The Formcraft MCP server (`mcp-server/server.js` , Node, stdio JSON-RPC) gives any outside AI the same tools: `get_brief, read_data, query_register, propose_actions, list_pending, apply_approved, reject_pending, remember, recall, log_exchange, handover_pack, log_metric` . `propose_actions` validates every action against a schema; nothing is written until `apply_approved` . API keys never go into the shared database: they stay on each PC (Windows Credential Manager or the browser's local storage).

The AI workforce

Every role in the hiring plan has an AI version working now, reporting to the founder who owns that department. Each starts on probation, suggesting only, with a USD 10 monthly AI budget, and earns autonomy through its scorecard. When we hire a person for the role, the AI hands over its journal, scripts and memory and becomes that person's assistant.

Emlyn Atochon

Design, BIM and software

STUDIO AND BIM

Architectural designer	standard
Architectural designer (housing)	standard
BIM modeller	standard
BIM modeller (families)	quick
Render and visualisation artist	quick

SOFTWARE (FORMCRAFT TOOLS)

Software developer	deep
Web developer	standard
Software tester and code reviewer	standard
Tools customer support	quick
Product manager (Formcraft Tools)	deep

Peter Isingoma

Engineering, construction, concrete, finance

ENGINEERING

Structural engineer	deep
MEP designer	standard
Quantity surveyor	standard

CONSTRUCTION

Project manager	standard
Site engineer	standard
Site engineer (second site)	standard
Site supervisor	quick
Health and safety officer	quick

CONCRETE AND STORES

Procurement and stores officer	quick
Concrete production lead	standard
Quality and lab technician	quick

FINANCE AND ADMIN

Accountant	standard
HR and admin officer	quick

Esther Ahumuza

Sales, marketing and stores

CONCRETE AND STORES

Stores sales lead	quick

SALES AND MARKETING

Sales and business development	standard
Content producer	standard
Video editor and designer	quick
Receptionist and customer service	quick

28 roles. The small label is the model size each role uses by default: quick (offline or DeepSeek), standard (Claude), deep (top Claude model).

Approvals, roles and who uses what

Risk	Examples	Needs
Low	Tags, summaries, internal tasks, drafts	Runs automatically and is logged
Medium	Posting to social media, client emails, register changes	One approval from the owning founder
High	Money out, contracts, prices, website releases, Revit model changes	The owner, plus a second founder for money over USD 500 and for every contract

Checking. Each founder reviews a sample of the AI's finished work in their area every week (10% to start). The share with a serious error is a KPI with a target under 2%. If an agent is above target, its autonomy drops one level until it recovers.

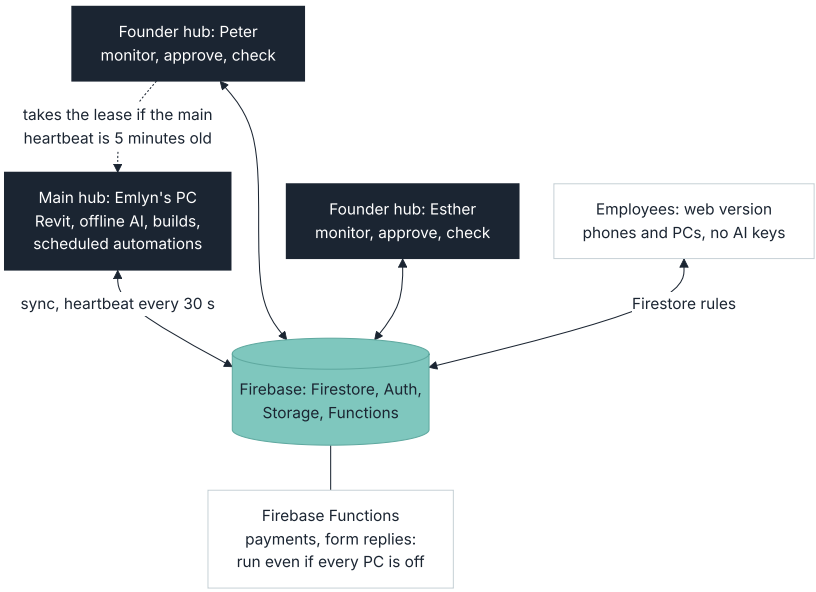

Figure 2.2 · Three founder hubs and the employees' web version share one online database.

	Founders (3)	Employees
App	Formcraft Hub for Windows (planned; today the Command Centre in claude.ai)	The web version on phone or PC
Sees	Everything their role allows; Emlyn chooses which tabs Peter and Esther see	Only their role's pages, tasks and registers
AI	Through the hub's router	Never holds an AI key: each request becomes a job the main hub runs within the role's budget
Does	Approving, checking, development, clients, strategy	Their tasks, site logs and photos, what automations cannot do; exceptions go up

Where the data lives

Everything is in one database, organised as collections (think: one sheet per kind of record). The Data explorer page shows every one of them. Money, payroll, contracts, investors and candidates are locked to admins by the database itself, whatever a person's role says.

Area	Collections
Daily work	`todos` tasks · `notices` · `meetings` · `chat` · `events` calendar · `deadlines` · `log` numbers · `targets` · `wins`
Sales and clients	`deals` · `enq` enquiries · `onb` journeys · `campaigns` · `reg_clients` · `reg_prospects` · `reg_subscribers`
Projects and design	`projects` · `boards`, `bel`, `brev` design studio · `reg_models` · `reg_drawings` · `reg_rfis` · `reg_variations` · `reg_sitediary` · `reg_defects` · `reg_permits`
Money (admin)	`ledger` · `invoices` · `budget` · `staff` · `payruns` · `hires` · `lic` · `reg_accounts` · `reg_debts` · `reg_contracts` · `reg_lenders`
Knowledge	`std_clauses` standards · `appr_auth`, `appr_rep` approvals · `pros`, `pro_reviews`, `referrals`, `contrib` directory · `reg_pricebook` · `reg_knowledge`
AI and systems	`memory` · `ailog` · `pending` approvals · `aistaff` · `aiuse` AI cost · `autos` · `issues` · `learn` · `decisions` · `risks`
Content	`cplan` content plan · `xevents` events · `seokw` · `files`, `assets` · `reach` · `impact`

How the data is kept safe

- **Today:** the database lives with the Command Centre in claude.ai, under Emlyn's account. A full backup (one JSON file) is one click on Team and access; restore is on the same page.
- **Next:** Firebase becomes the online master (the web version is already built for it: `command-centre/standalone`), and each founder hub keeps a full PostgreSQL copy with a change log and an outbox, so nothing is lost if one copy fails.
- **Rule:** a weekly backup and a restore drill every quarter. A backup that has never been restored is not a backup.

PART 3

Getting started

A tour of the screen, the first week, and the daily, weekly and monthly routine for each founder.

Formcraft
DESIGN & CONSTRUCTION

3 A tour of the screen

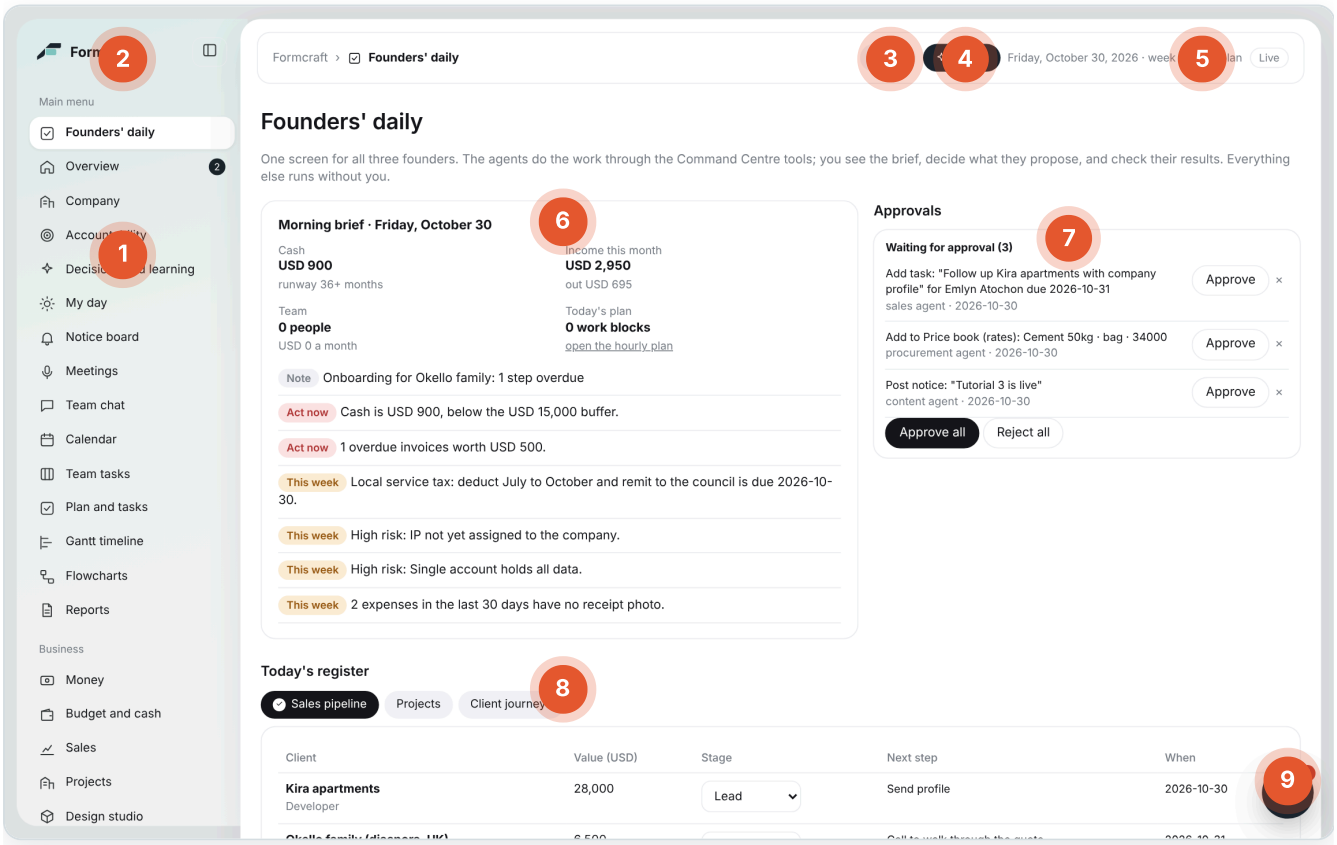

The Founders' daily page with the menu open. Example data.

1. **The menu.** Five groups: Main menu (daily work), Business (money, sales, projects, design, content), Build and AI (agents, automations, standards, tools), Registers (lists) and Control (targets, risk, access). You only see the pages your role allows. The button at the top folds it away.
2. **Where you are.** The page name. Every page has the same header.
3. **+ Log.** Log anything by hand from any page: a number, an expense, a task, a note. Marked as manual so you can always tell it from automation.
4. **Ask AI.** Ask a question about the page you are on. The AI reads the data you can see and proposes actions; you approve them.
5. **Date, week of the plan and Live.** 'Live' means you are connected and every change is saved for everyone at once.
6. **Morning brief.** Cash, income, team, today's plan, then alerts in order: Act now, This week, Note.
7. **Approvals.** What the agents propose. Approve, reject, or approve all.
8. **Today's register.** The pipeline, projects and client journeys you can change in place.
9. **The AI button.** Opens the agent chat from anywhere. The red number is how many approvals are waiting.

Your first week: put the real business in

The Command Centre is only as good as what is in it. Before anything else, these eight jobs give every page real numbers to work with. Each takes under an hour.

1. **Company** — Fill the Company page: URSB, TIN, NSSF, addresses. Upload certificates to Files.
2. **Cash and money** — Log cash in hand. Enter this month's income and expenses in Money. Add unpaid invoices.
3. **Pipeline** — Every live lead and quote into Sales, each with a next step and date.
4. **Projects** — Every running job, with budget, cost so far and due date.
5. **Registers** — Paste clients, suppliers and the price book from Excel.
6. **Numbers** — Log leads, subscribers and the other metrics on Log and deadlines.
7. **People and roles** — Founders confirm roles; Emlyn sets tabs on Team and access.
8. **Backup** — Download the first full backup on Team and access.

The routine

Every day · 10 minutes

1. Open Founders' daily.
2. Read the brief, red items first.
3. Decide every approval waiting for you.
4. Log anything that happened (+ Log).
5. Check My day.

Every week · 45 minutes, together

1. Weekly founders review meeting (Meetings).
2. Sales: every deal has a next step.
3. Cash: log cash, read the forecast.
4. Check a 10% sample of AI work.
5. Approve next week's content.
6. Download a backup.

Every month · 2 hours

1. Monthly management pack (Reports).
2. Live simulation: are we on plan?
3. Targets and Accountability.
4. Compliance calendar ticked.
5. AI cost: is the cheap path working?
6. Raise or lower each agent's autonomy.

Logging by hand and talking to the AI

You never have to wait for an automation. **+ Log** in the header records a number, an expense, a task or a note from any page, marked *manual*. **Ask AI** answers questions about the page you are on (for example on Sales: *"which deals have gone quiet for two weeks?"*) and can propose actions, which land in Approvals. On the AI hub page you can talk to one agent directly, for example the Finance agent about the cash forecast.

> Good questions are specific and name the outcome: *"Draft the follow-up for the Okello quote, friendly, mention the site visit slot on Tuesday"* works better than *"help with Okello"*.

PART 4

Every page, explained

All 67 pages in menu order: what each is for, how to use it, and the logic under it. Use this part as a reference.

Formcraft
DESIGN & CONSTRUCTION

4.1 Main menu

Daily work: the brief, your tasks, meetings, the calendar, the plan and reports.

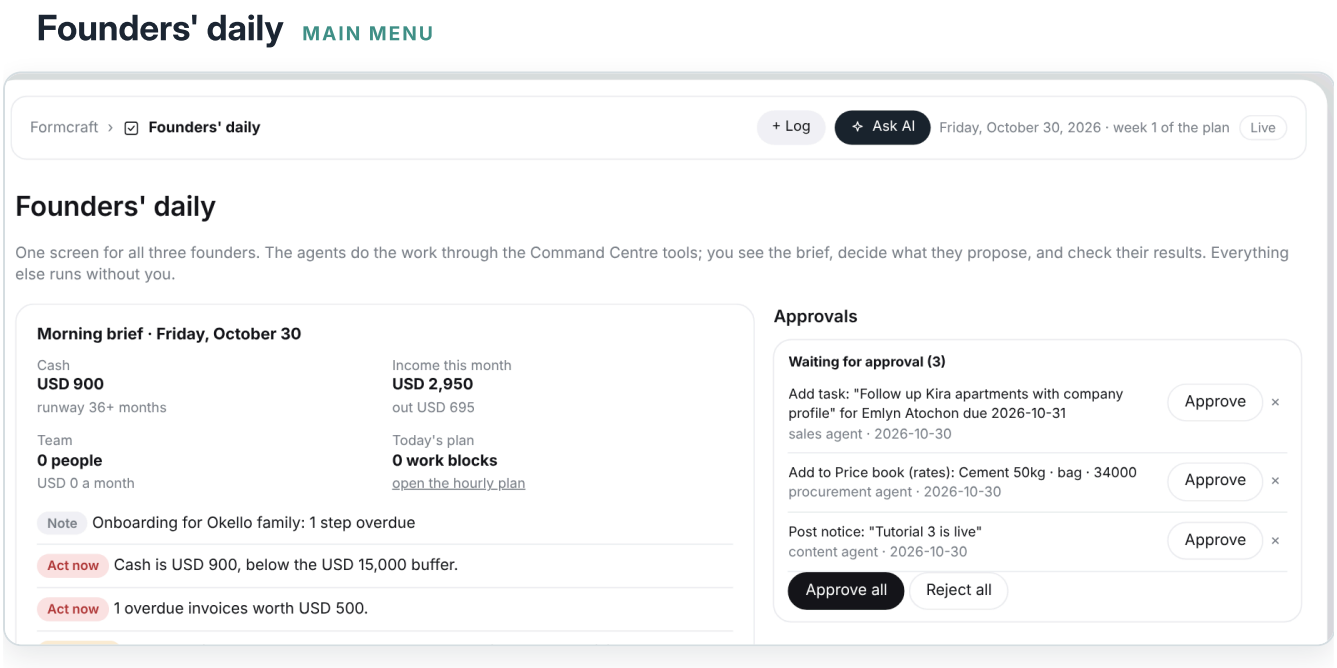

The founders' home screen. One page shows the morning brief (cash, income, team, today's plan and alerts ranked Act now / This week / Note), the approvals waiting for you, and today's register of deals, projects and client journeys. The idea: agents do the work, you decide what they propose and check their results.

HOW TO USE IT

1. Open it first thing every morning. Read the brief from the top: red 'Act now' items first.
2. Clear the Approvals box: Approve, reject (×), or Approve all if you have read them. Target: nothing waits more than 24 hours.
3. Use the tabs under Today's register (Sales pipeline, Projects, Client journeys) to change a stage or date in place.
4. Scroll down for the 60-day review check: it measures whether the founders keep pace with the agents.

UNDER THE HOOD

Brief = briefAlerts() reading ledger, invoices, deadlines, risks, onb, compliance calendar. Approvals = the shared 'pending' collection; each item holds the proposed action, the agent, and the time. Approving calls the same validated apply function the MCP server uses (apply_approved). The 60-day check measures decision time from the 'pending' timestamps: decide within 24 h, nothing older than 48 h. This is the gate before phase 4 of the Windows hub.

Overview MAIN MENU

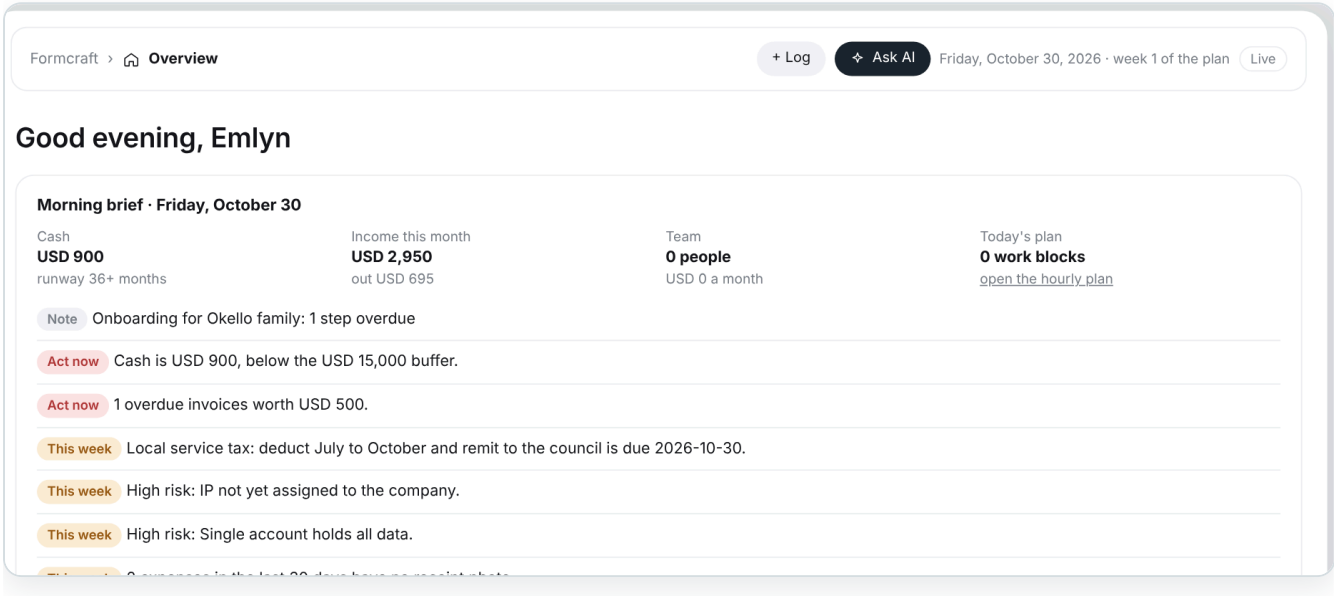

The Overview: the same morning brief plus the company dashboard. The badge on the menu shows how many 'Act now' alerts are open.

HOW TO USE IT

1. Use it when you want the whole company at a glance rather than your approvals.
2. Click any alert to jump to the page that fixes it.

UNDER THE HOOD

Shares briefAlerts() with Founders' daily. Alert levels: 2 = Act now, 1 = This week, 0 = Note. The menu badge counts level-2 alerts.

Company MAIN MENU

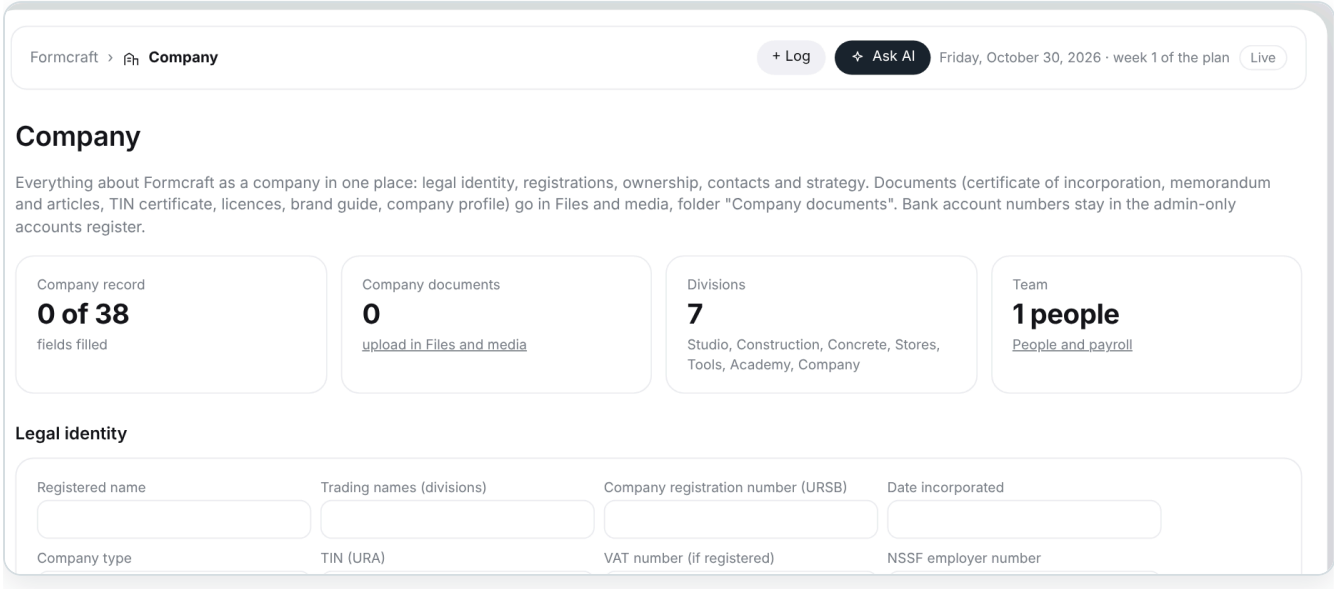

Everything about Formcraft as a legal company: registered name, URSB number, TIN, NSSF and EFRIS status, data-protection registration, addresses, ownership, divisions and strategy. 38 fields in all.

HOW TO USE IT

1. Fill every field once from the certificates (incorporation, TIN, trading licence).
2. Upload the documents themselves to Files and media, folder 'Company documents'.
3. Keep bank account numbers out of here: they belong in the admin-only Accounts register.

UNDER THE HOOD

Stored in settings.company. Counted as 'x of 38 fields filled' so the gap is visible. Other pages (Documents, Templates, invoices) read the company name, TIN and address from here, so filling it once brands every document.

Accountability MAIN MENU

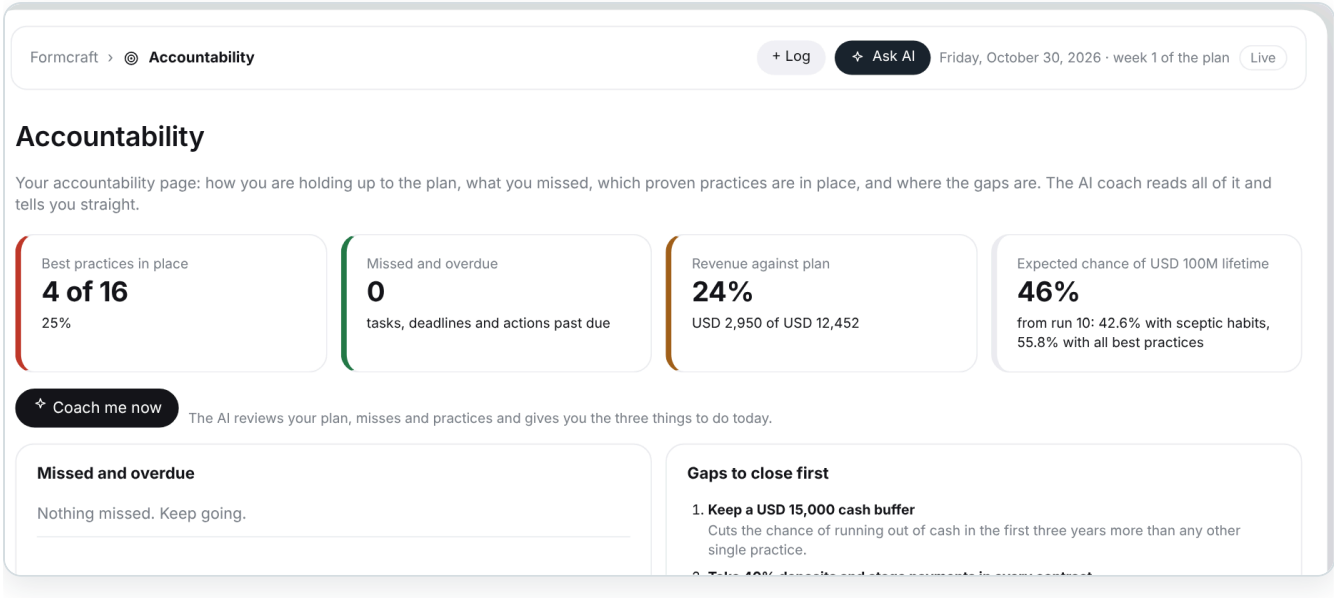

Your accountability page. It shows the best practices in place (out of 16), what you missed, revenue against plan, and the chance of the long-term goal from the simulations. 'Coach me now' asks the AI for the three things to do today.

HOW TO USE IT

1. Read 'Gaps to close first': each practice says why it matters (for example the USD 15,000 cash buffer, 40% deposits, IP assignment).
2. Tick a practice only when it is really in place.
3. Press Coach me now when you feel off-track; it reads your plan, misses and practices and answers straight.

UNDER THE HOOD

Practices and their effect sizes come from simulation run 10 (best practices 55.8% vs sceptic habits 42.6% for the USD 100M lifetime goal). Revenue against plan compares the ledger with the plan's monthly curve.

Decisions and learning MAIN MENU

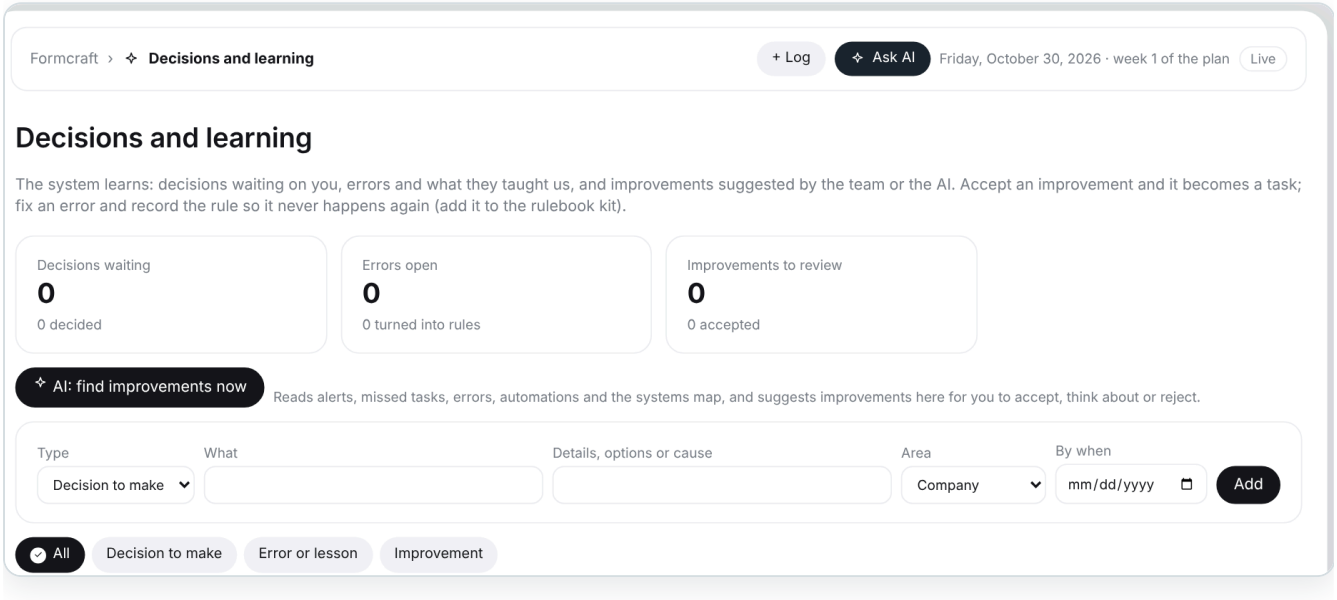

How the system learns. Three lists: decisions waiting on you, errors and what they taught us, and improvements suggested by the team or the AI. Accept an improvement and it becomes a task; fix an error and record the rule so it never happens again.

HOW TO USE IT

1. Add a decision, error or improvement with the form (type, area, by when).
2. Press 'AI: find improvements now' weekly: it reads alerts, missed tasks, errors and the systems map and proposes improvements.
3. When you close an error, write the rule, then add it to the rulebook.

UNDER THE HOOD

Collections: learn (kind = Decision / Error / Improvement) and decisions. Accepted improvements create todos. Rules feed rulebooks/agents/*.md so every AI model inherits them.

My day MAIN MENU

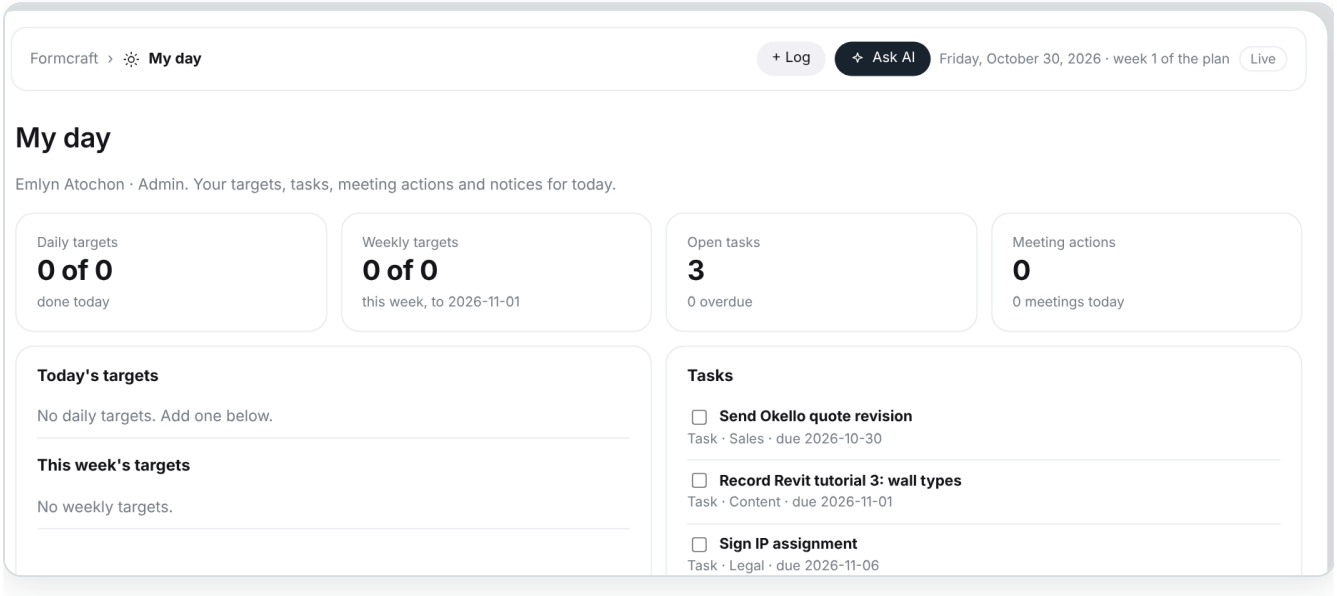

Your personal page: today's and this week's targets, your open tasks, meeting actions and notices. Each person sees their own.

HOW TO USE IT

1. Add a daily or weekly target for yourself.
2. Tick tasks as you finish them; overdue ones turn red.
3. Meeting actions assigned to you show here automatically after the minutes are written.

UNDER THE HOOD

Filters todos, meetings.actions and notices by the signed-in user (ME). Daily and weekly targets are todos of kind 'Daily target' / 'Weekly target'.

Notice board MAIN MENU

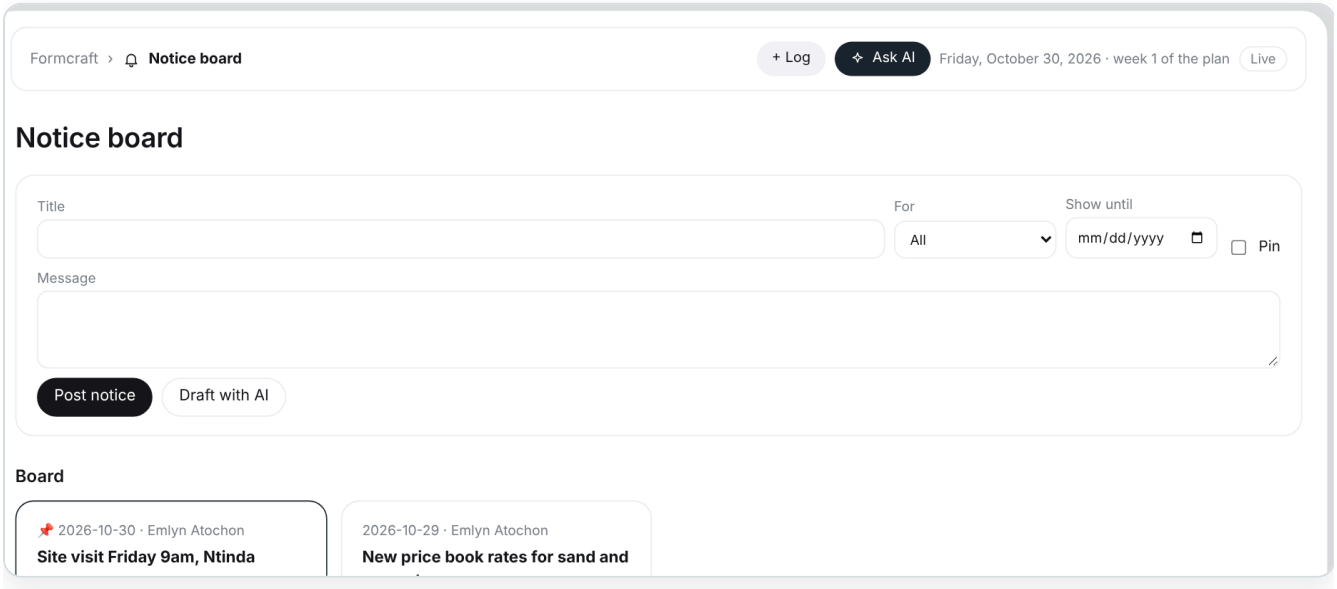

The company notice board. Post a notice to everyone or to one group (Manager, Finance, Design and BIM, Site, Sales and content, Staff, Partner), pin it, and give it an end date.

HOW TO USE IT

1. Write a title and message, choose who it is for, and post. 'Draft with AI' writes it from a short note.
2. Pin anything everyone must see this week.
3. Agents can also propose notices; they arrive in Approvals first.

UNDER THE HOOD

Collection: notices {title, body, aud, exp, pin, by, date, ai}. The AI action type post_notice writes here after approval.

Meetings MAIN MENU

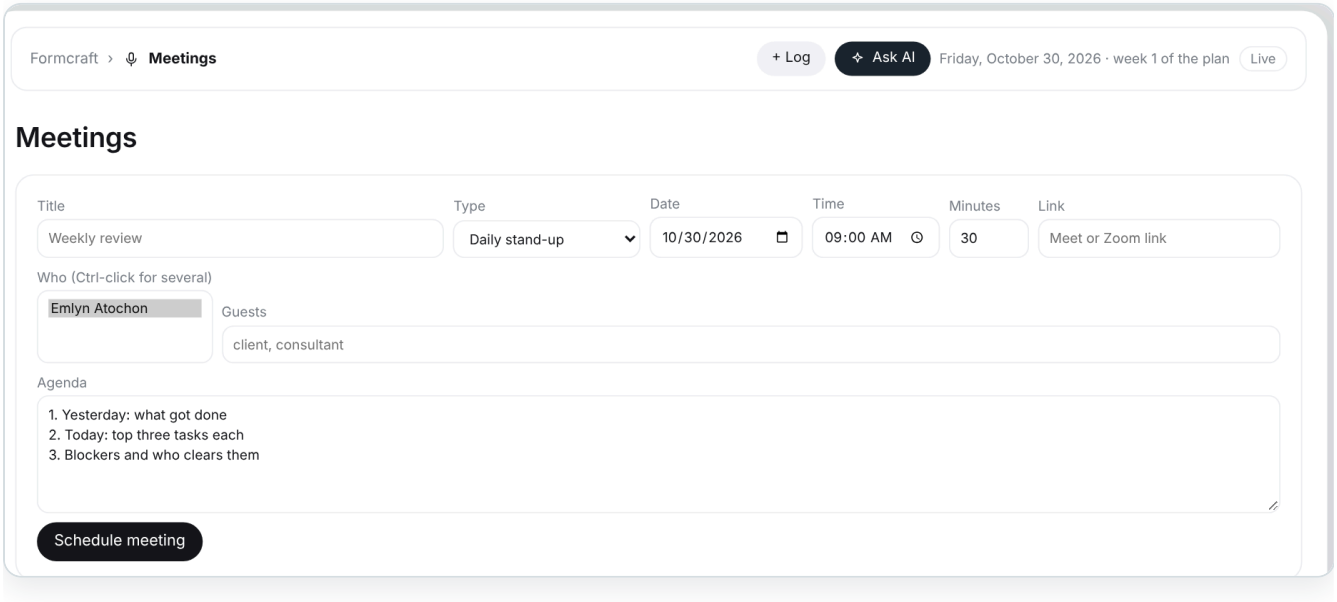

Schedule meetings by type (daily stand-up, weekly review, monthly management, site, client, quarterly board, design review), with an agenda template. After the meeting the AI writes the minutes, the decisions and the actions with owners and dates.

HOW TO USE IT

1. Pick a type: the agenda fills in from the template. Add people and guests.
2. During or after the meeting, paste notes or a transcript and press the minutes button.
3. Check the actions; they become tasks for their owners.

UNDER THE HOOD

Collection: meetings {title, type, date, time, att, agenda, notes, actions[], decisions[]}. AI minutes return JSON {summary, decisions, actions}; decisions are copied to the decisions collection with 'Meeting: title' as the reason.

Team chat MAIN MENU

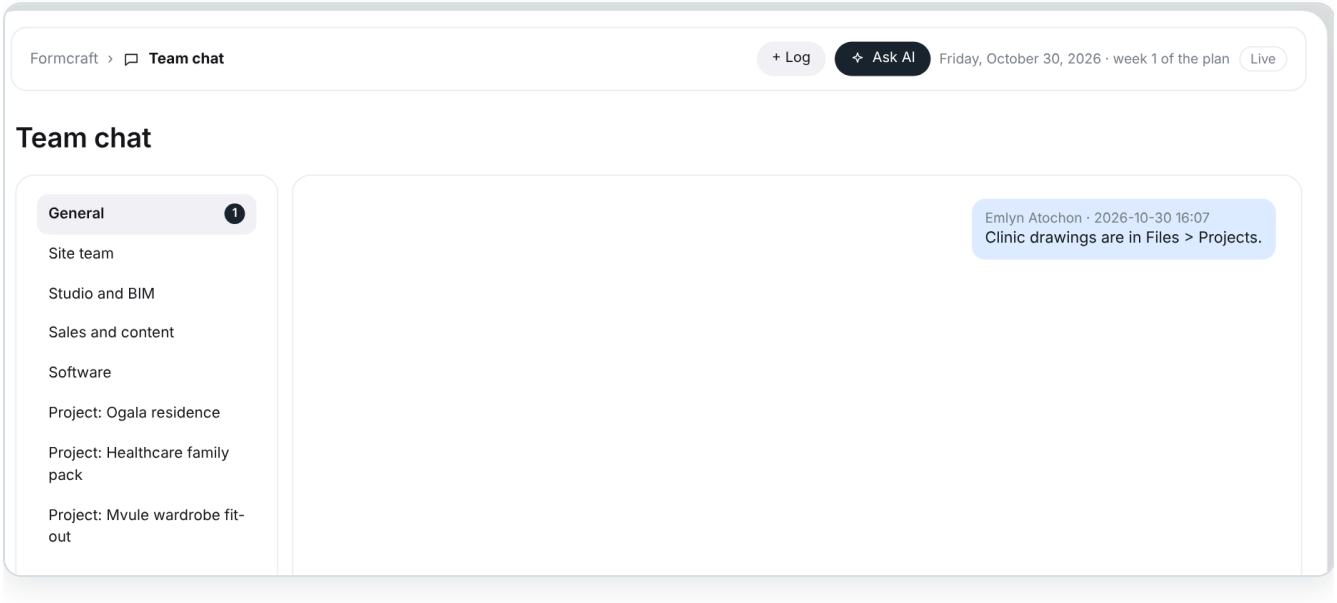

Team chat with rooms: General, Site team, Studio and BIM, Sales and content, Software, and one room per project. 'Send AI summary' condenses a busy room.

HOW TO USE IT

1. Pick the room, type, press Enter.
2. Use the project room for anything about that project so the history stays with it.

UNDER THE HOOD

Collection: chat {room, t, by, at}. Project rooms are generated from the projects collection.

Calendar MAIN MENU

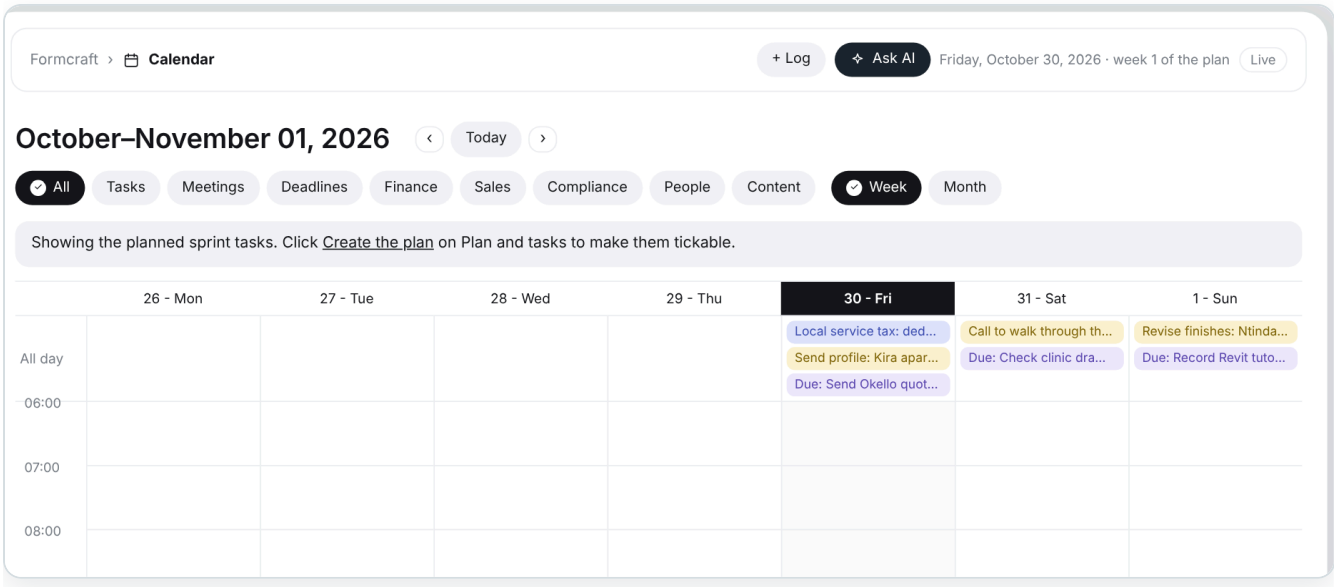

One calendar for tasks, meetings, deadlines, finance and compliance dates, sales follow-ups, people dates and content. Filter by type; switch week or month.

HOW TO USE IT

1. Use the filter chips to show only what you need.
2. Click a day to add an event.

UNDER THE HOOD

Reads events, todos, meetings, deadlines, the compliance calendar (OBLIG), deals.nextDate and cplan. Nothing is copied; the calendar is a view over the data.

Team tasks MAIN MENU

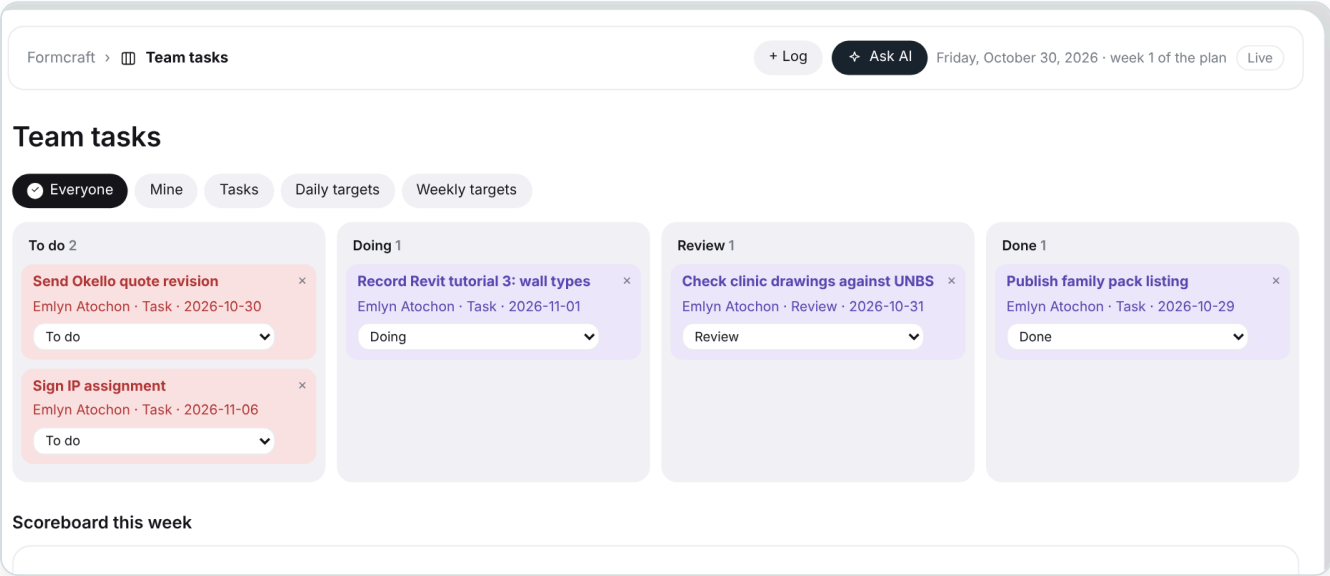

A Kanban board: To do, Doing, Review, Done. Everyone's tasks or only yours.

HOW TO USE IT

1. Move a card by choosing its new column on the card.
2. Use Review when someone else must check the work before it is Done.

UNDER THE HOOD

Collection: todos {t, kind, owner, due, area, pri, status}. AI-proposed tasks arrive through Approvals with ai: true.

Plan and tasks MAIN MENU

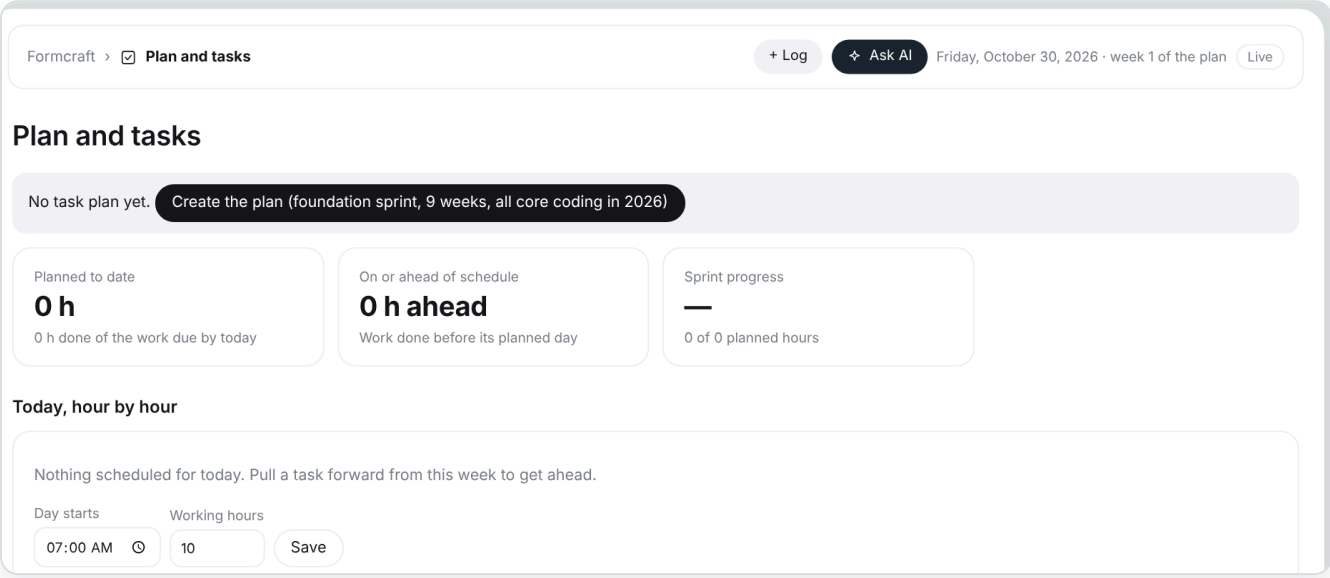

The work plan, hour by hour. It creates the foundation sprint (9 weeks of core build in 2026) and the journey phases with their milestones, then schedules today's work blocks inside your working hours.

HOW TO USE IT

1. Press 'Create the plan' once.
2. Set your day start and working hours.
3. Each day, do the blocks in order; pull a task forward from this week to get ahead.

UNDER THE HOOD

Phases P0 to P5 with milestones (P0 Foundation sprint, P1 Prove the model about USD 46,000 revenue, 2,000 subscribers, and so on). 'On or ahead of schedule' compares hours done with hours planned to date.

Gantt timeline MAIN MENU

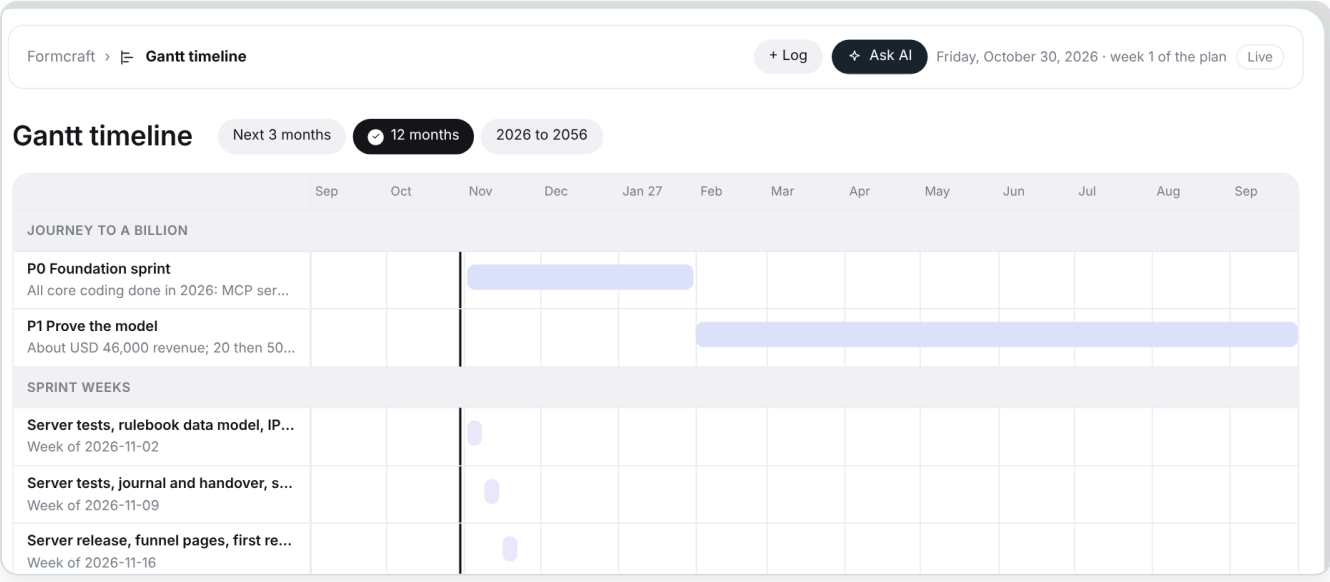

A timeline of the whole journey: phases, sprint weeks, projects, targets, systems to build, software releases and the hiring plan, from the next 3 months up to 2026-2056.

HOW TO USE IT

1. Switch between Next 3 months, 12 months and the full journey.
2. The darker fill is progress; red means behind; the black line is today.

UNDER THE HOOD

Drawn from the same collections as each section (projects, targets, systems, hires). No separate data.

Flowcharts MAIN MENU

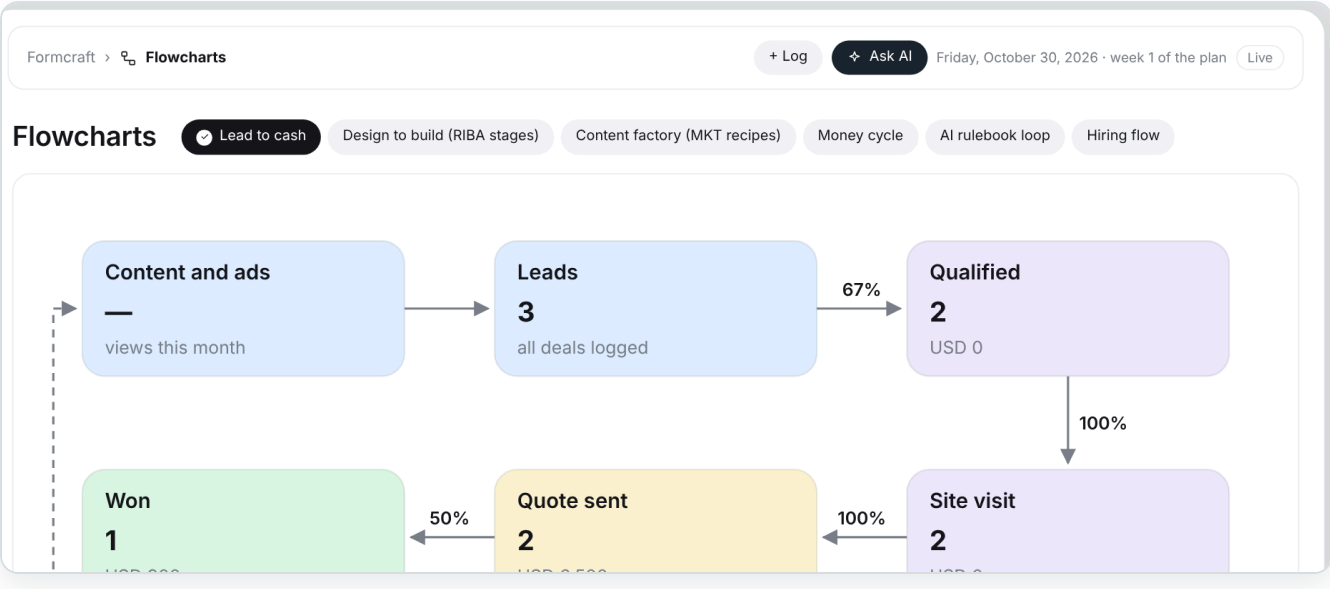

Live flowcharts of how the business moves: Lead to cash, Design to build (RIBA stages), Content factory, Money cycle, the AI rulebook loop and the Hiring flow. Numbers in each box come from your data; percentages are conversion between steps.

HOW TO USE IT

1. Use it in the weekly review: the weakest arrow is where to work this week.

UNDER THE HOOD

Lead to cash reads deals by stage, projects, invoices and ledger; conversion = next stage / this stage.

Reports MAIN MENU

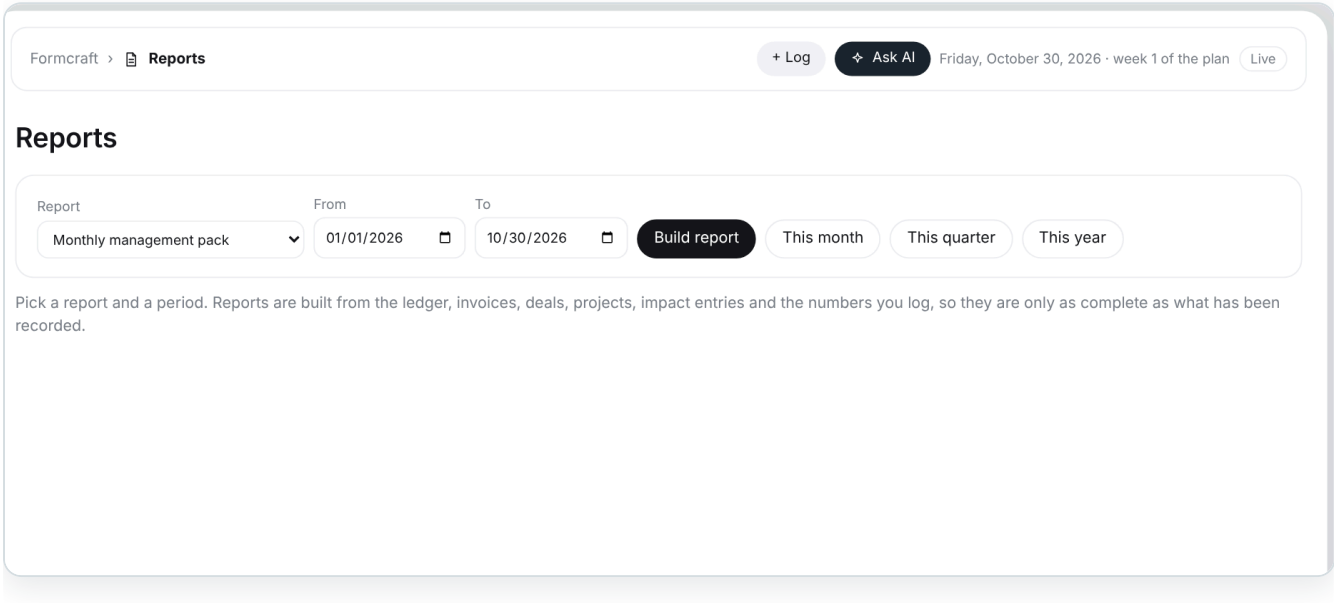

Ready-made reports for any period: profit and loss, cash flow by month, expenses by category and project, receivables, tax summary, sales, marketing, projects, impact, people and payroll, budget against actual, risk and compliance, Formcraft Tools, AI and systems, and the monthly management pack.

HOW TO USE IT

1. Pick a report and a period (this month, quarter, year, or dates).
2. Build, then download as Excel or Word.

UNDER THE HOOD

Built from ledger, invoices, deals, projects, impact and the log. A report is only as complete as what has been recorded, which is why entering real data is the first job.

4.2 Business pages

Running the five businesses: money, sales, projects, design, clients, content, pricing and growth.

Money BUSINESS

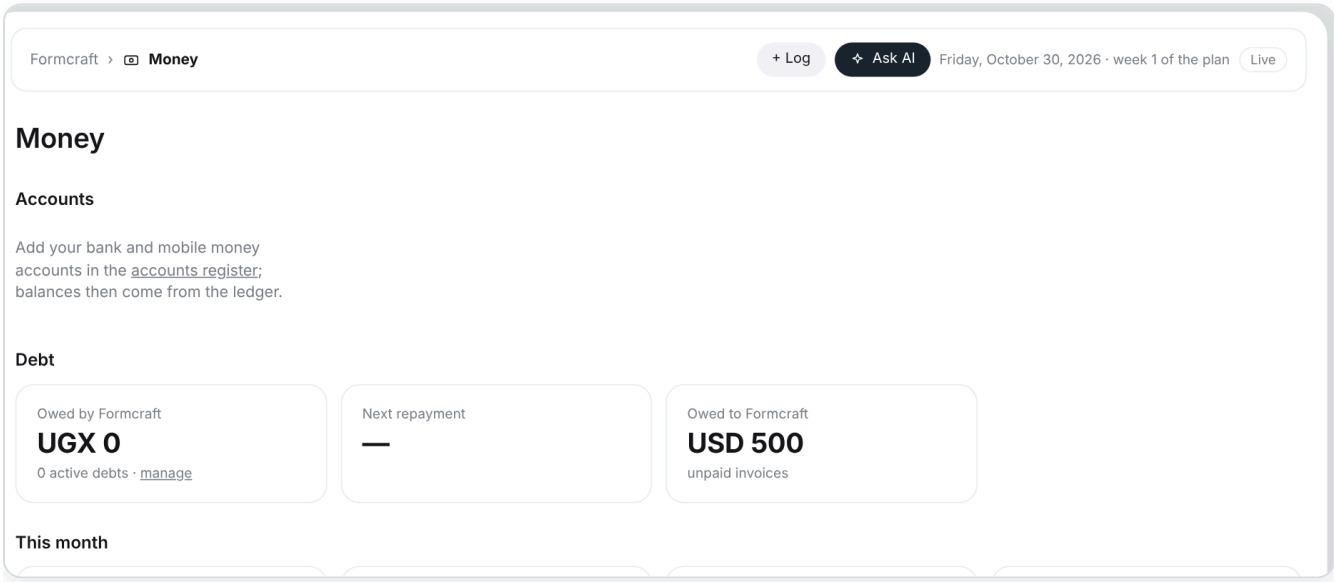

The ledger: every shilling and dollar in and out, with category, division, project and withholding tax. It also shows debts, money owed to Formcraft, this month and this year.

HOW TO USE IT

1. Add every income and expense the day it happens (or press + Log in the header from anywhere).
2. Attach a receipt photo; the brief flags expenses without one.
3. Set the exchange rate once in settings; amounts in UGX are converted to USD for the totals.

UNDER THE HOOD

Collections: ledger {date, type, category, amount, cur, amountUSD, division, project, wht}, invoices, reg_debts, reg_accounts. Admin-only in the database rules. All totals use usd(e), which reads amountUSD.

Budget and cash BUSINESS

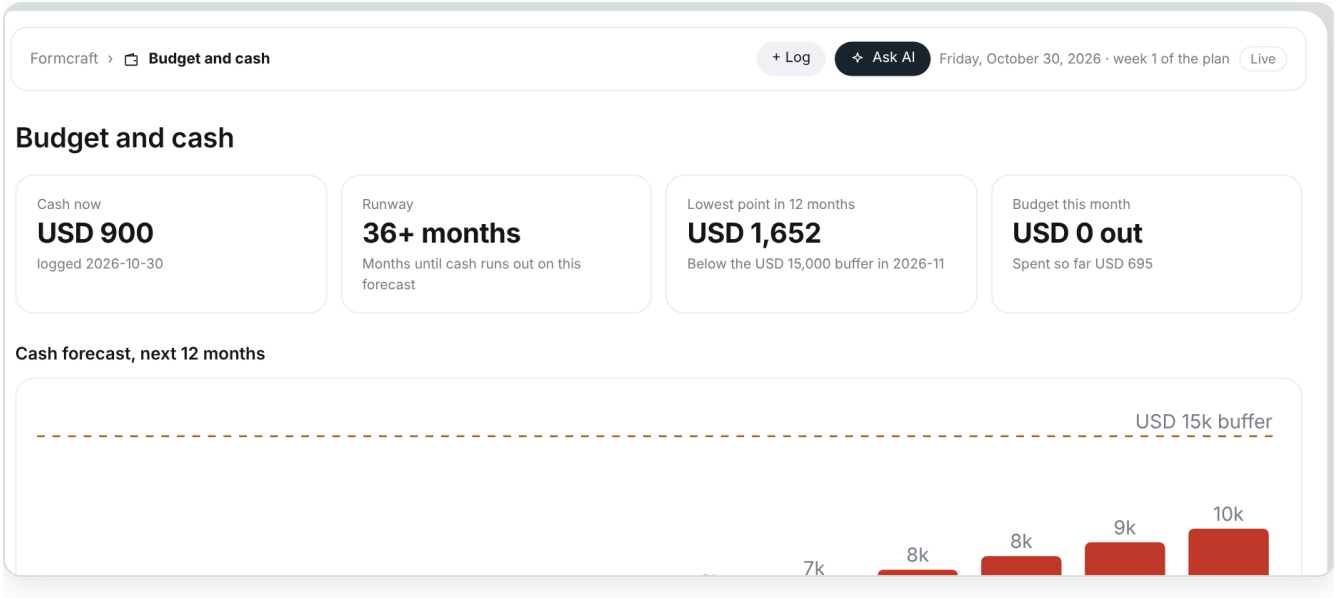

Cash now, runway, the lowest point in the next 12 months, and budget against actual by category. The forecast warns when cash will drop below the USD 15,000 buffer.

HOW TO USE IT

1. Log the real cash figure (Log: Cash in hand) at least weekly.
2. Set a monthly budget for each category.
3. Read the 12-month forecast: money in = your income budget or the last 90 days' average; money out = budget plus people cost, including planned hires.

UNDER THE HOOD

Collections: budget, log (metric cash), staff, hires. The buffer target is the plan's working-capital rule.

Sales BUSINESS

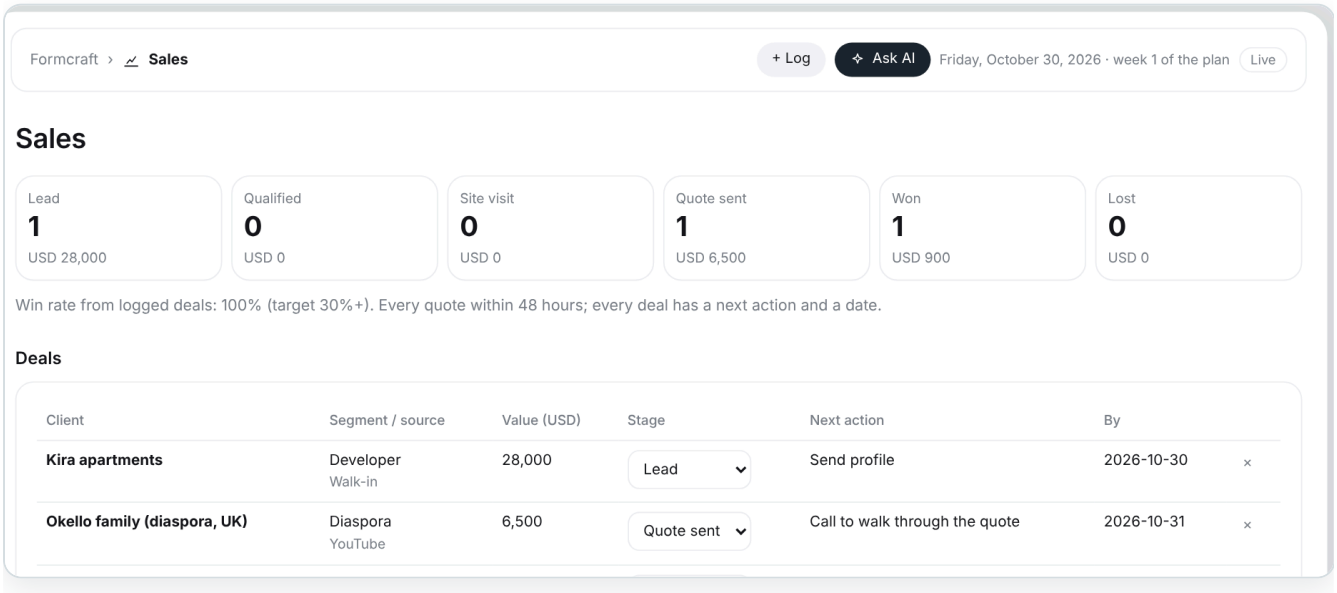

The pipeline: Lead, Qualified, Site visit, Quote sent, Won, Lost, with values and the win rate. Rule: every quote within 48 hours, every deal has a next action and a date.

HOW TO USE IT

1. Add each lead with its segment and source.
2. Move the stage as it progresses; always set the next action and date.
3. When a deal is Won, start its onboarding journey (Client on and offboarding offers it automatically).

UNDER THE HOOD

Collection: deals {client, segment, source, value, stage, next, nextDate}. Win rate = won / (won + lost); target 30% or more.

Projects BUSINESS

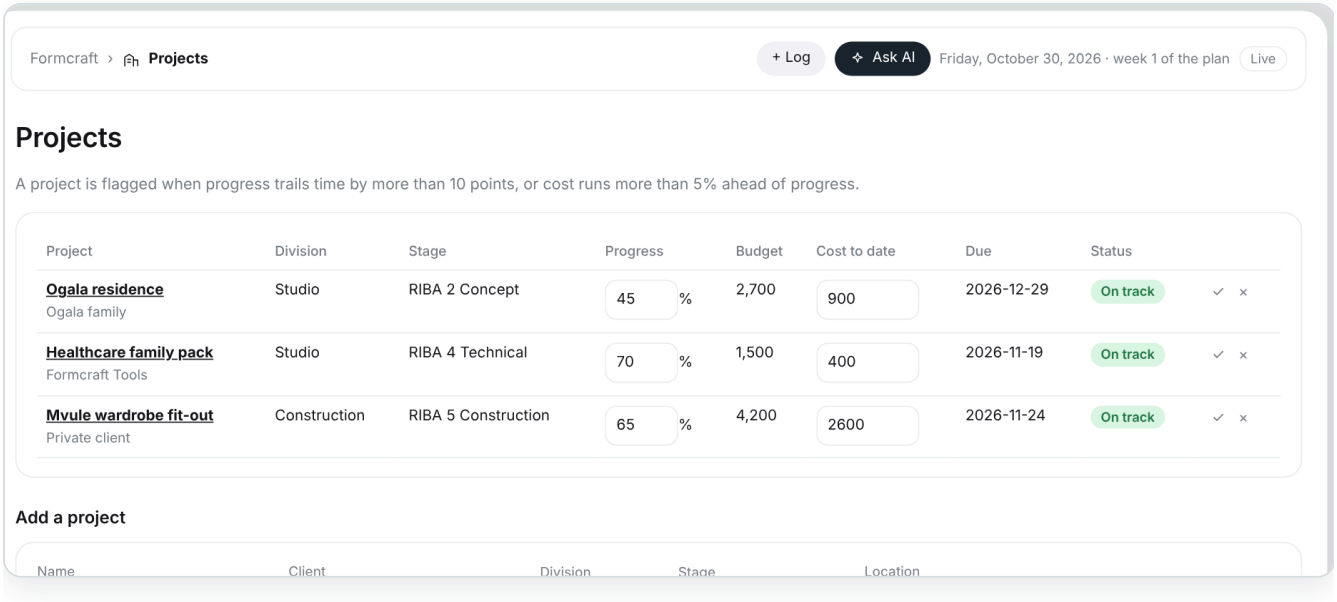

Every project with division, RIBA stage, progress, budget, cost to date and due date. A project is flagged when progress trails time by more than 10 points, or cost runs more than 5% ahead of progress.

HOW TO USE IT

1. Create the project when the deposit is paid.
2. Update progress and cost weekly (site diary and ledger feed it).

UNDER THE HOOD

Collection: projects {name, client, division, stage, budget, cost, pct, start, due, status}. Flags compare pct with time elapsed and cost/budget with pct.

Design studio BUSINESS

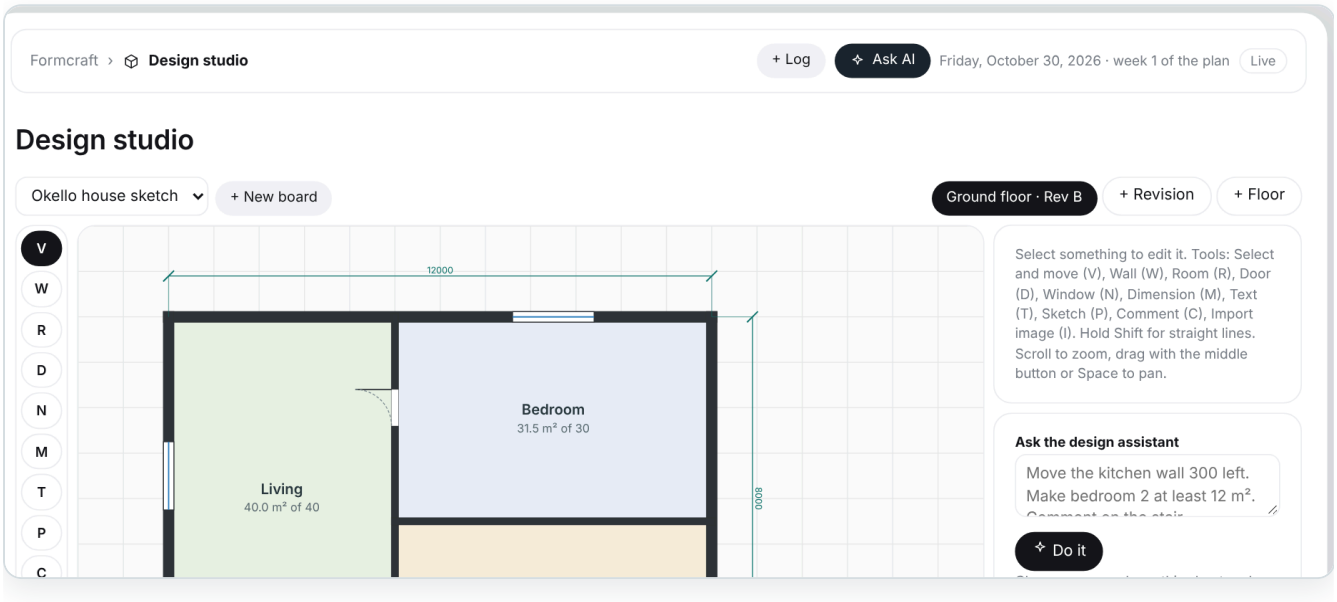

A fast 2D drawing board, like a light AutoCAD for sketch design: walls, rooms with live areas, doors, windows, dimensions, text, freehand sketch, comments and imported images on a giant canvas. Floors and revision sheets keep a history. The design assistant edits on command, for example 'move the kitchen wall 300 mm left'. The finished sheet hands off to Revit.

HOW TO USE IT

1. Make a board for the project; it starts with a Ground floor sheet at Rev A.
2. Draw with the keyboard tools: V select, W wall, R room, D door, N window, M dimension, T text, P sketch, C comment, I image. Hold Shift for straight lines; scroll to zoom; Space or the middle button to pan.
3. Give a room a target area: it turns red when the drawn area is more than 10% off.
4. Type an instruction for the design assistant and press Do it. Every change is logged and Undo reverses it.
5. Press + Revision before showing the client changes; + Floor copies the outer walls to a new level.
6. Share and hand over: export the sheet (SVG) or the hand-off file for Revit.

UNDER THE HOOD

Collections: boards {sheets[{id, name, level, elev, rev}]}, bel (one record per element: wall x1,y1,x2,y2,t; room pts[], use, target; door/window x,y,w,a), brev (revision log). Units are millimetres. AI edits return ops (move / set / add / delete / comment) that are applied through the same undo history. Hand-off format fmc-cis/0.2: outline_mm, walls, openings, decisions.

Client on and offboarding BUSINESS

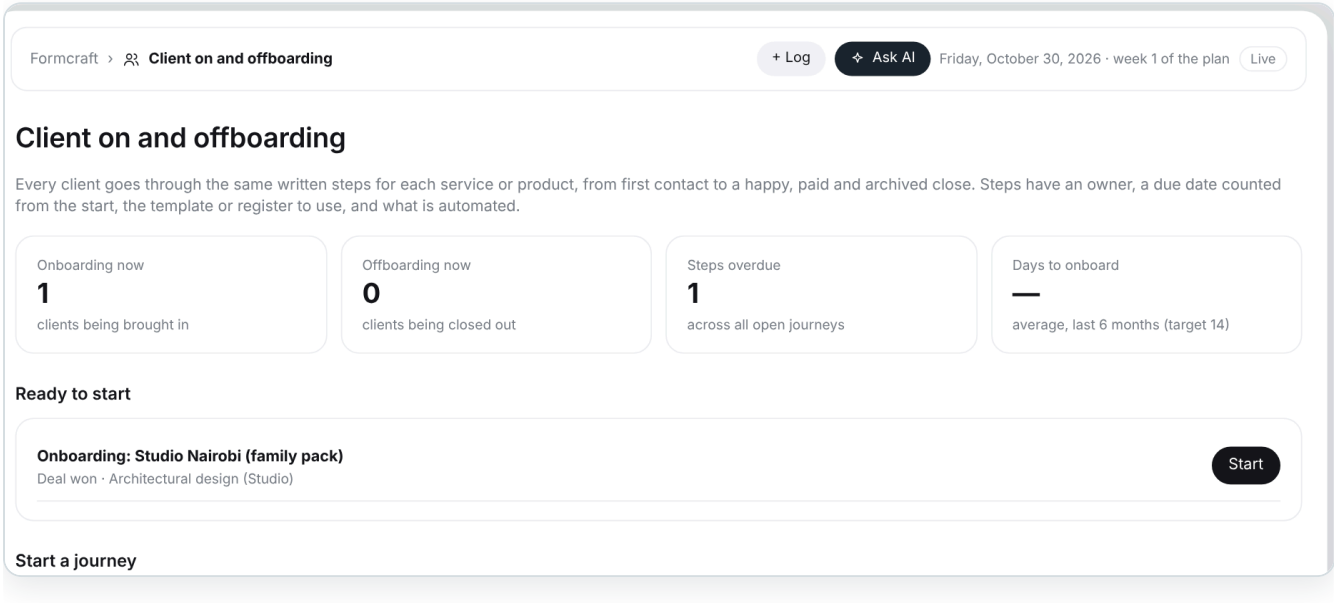

The written journey every client goes through, from first contact to a happy, paid and archived close, for each of the 7 service lines: Studio design, Construction and design-and-build, Concrete, Stores, BIM services and renders, Formcraft Tools and families, and Advisory. Each step has an owner, a due day counted from the start, the template or register to use, and what is automated.

HOW TO USE IT

1. When a deal is won it shows under 'Ready to start'. Press Start.
2. Tick steps as they are done; overdue steps go to the morning brief.
3. At the end of the job, start the Offboarding journey: final drawings, final invoice, review, referral ask, archive.

UNDER THE HOOD

Playbooks are the OBL table in the app (rulebooks/client-onboarding-offboarding.md in the repo). Collection: onb {client, line, kind, start, owner, done{step:true}, status}. Days to onboard: target 14.

Approvals and professionals BUSINESS

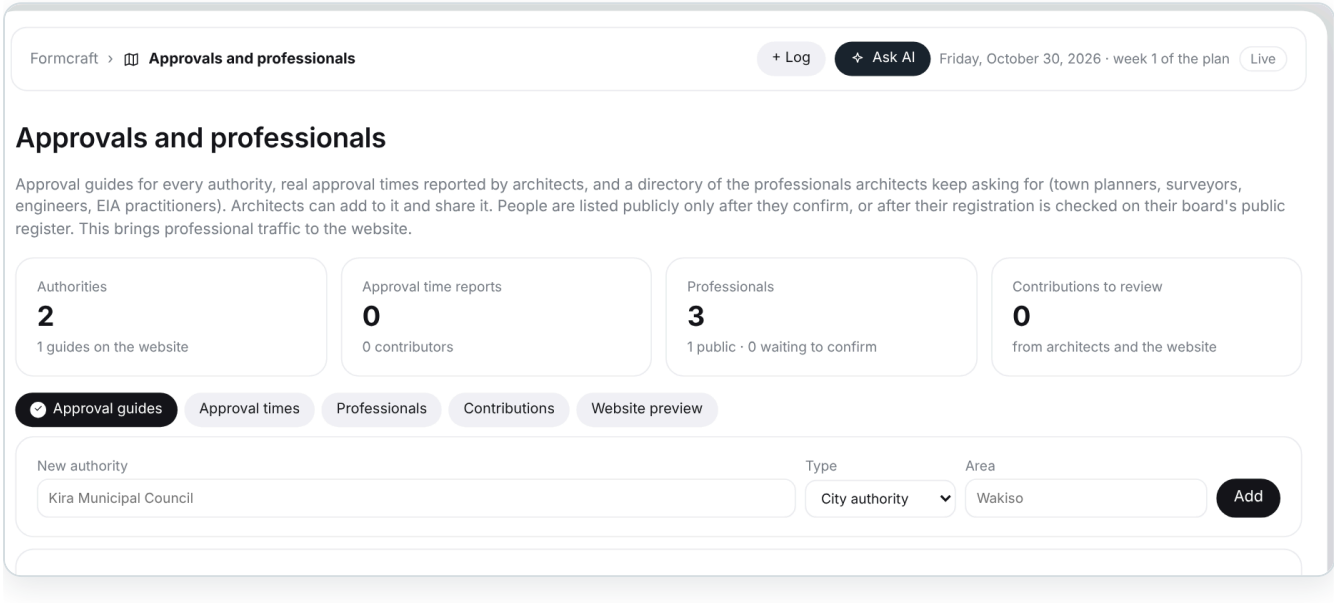

Two things architects need constantly: approval guides for every authority (steps, documents, fees, real approval times reported by architects) and a directory of the professionals they keep asking for (town planners, surveyors, engineers, EIA practitioners, trades and crafts). Architects can add to it. Nobody is shown publicly until they confirm. This brings professional traffic to the website.

HOW TO USE IT

1. Add an authority (for example Gulu City Council) and fill its guide; tick when checked.
2. Add professionals with their registration number; they stay Private.
3. Confirmation: a consent call or SMS, or their registration found on the board's public register. Then they become Public.
4. Use the finder: search by place (Gulu) and by trade or profession.
5. Review contributions from architects and the website before they go live.

UNDER THE HOOD

Collections: appr_auth, appr_rep (approval time reports, median days), pros {name, prof, regno, areas, status Private / Confirmed / Public, vouches}, contrib, pro_reviews, referrals. Ratings only come from clients who arrived through a referral link. Automations WS-05 to WS-08 send confirmations, publish data and follow up referrals.

Models and BIM BUSINESS

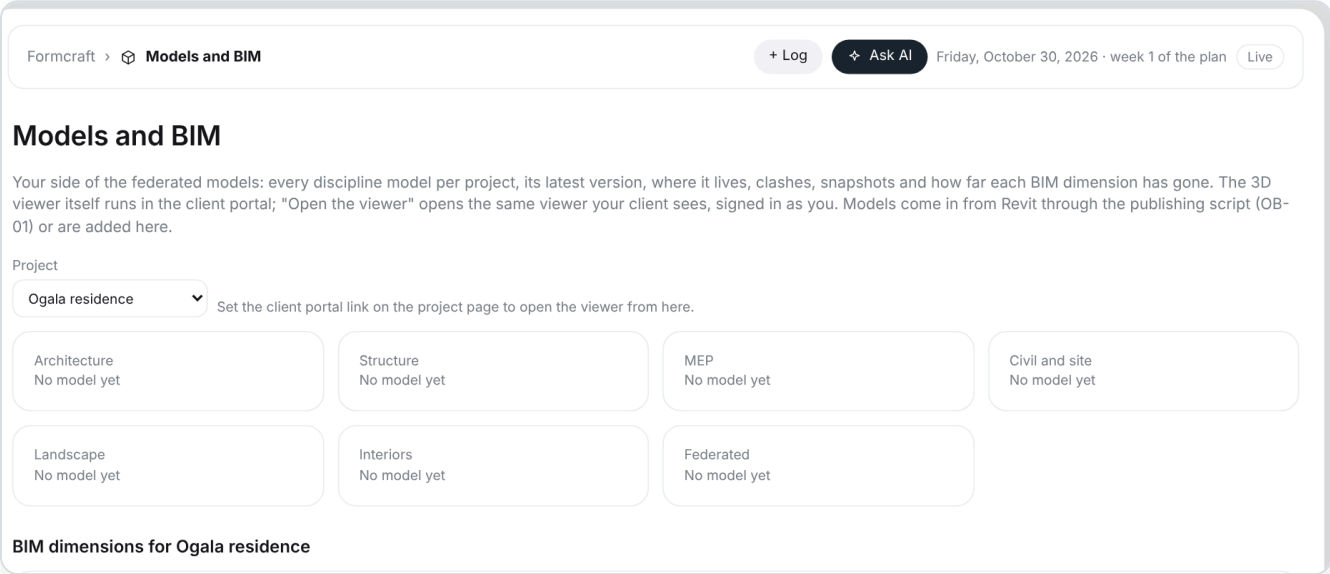

Your side of the federated BIM models: each discipline model per project (architecture, structure, MEP, civil, landscape, interiors, federated), its latest version, clashes, snapshots and how far each BIM dimension (3D to 7D) has gone. 'Open the viewer' opens the same 3D viewer the client sees in the portal.

HOW TO USE IT

1. Pick the project; check each discipline has a current model.
2. Models arrive from Revit through the publishing script (CP-01) or are added by hand.

UNDER THE HOOD

Collection: reg_models. 4D comes from the Gantt; 5D from quantities × the price book; 1D/2D live in the Drawings register.

People and payroll BUSINESS

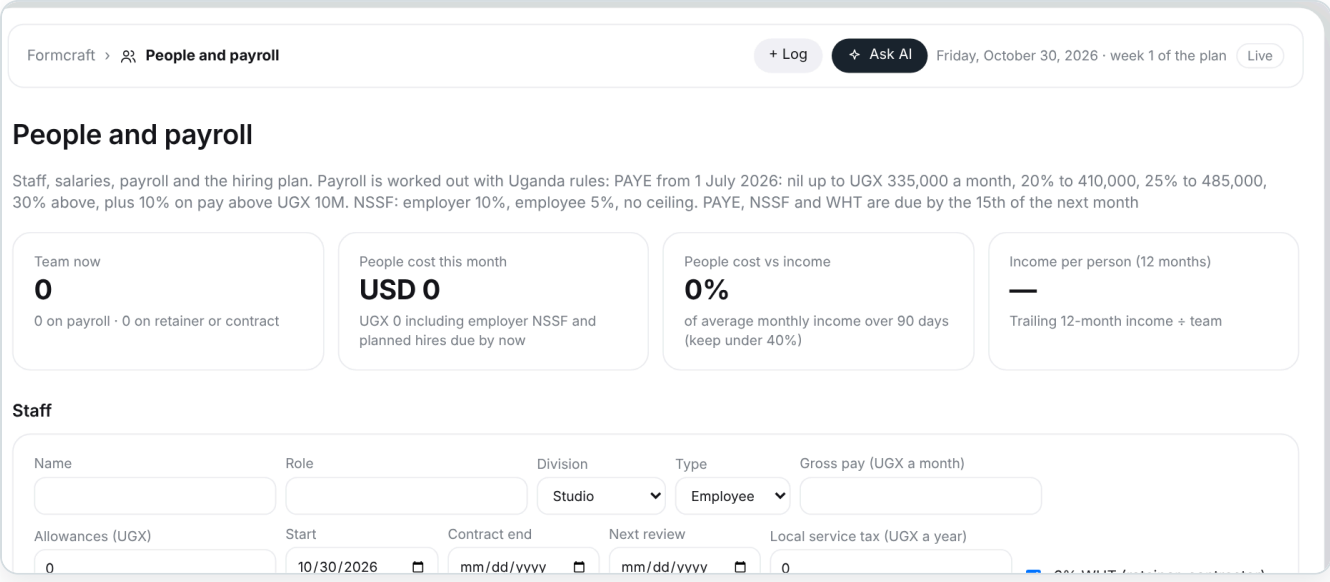

Staff, salaries, payroll and the hiring plan, with Uganda rules built in: PAYE bands from July 2026, NSSF 10% employer and 5% employee, local service tax, and 6% withholding for retainers and contractors.

HOW TO USE IT

1. Add each person with work details only (no ID numbers here, under the Data Protection and Privacy Act 2019).
2. Run payroll monthly; PAYE, NSSF and WHT are due by the 15th of the next month.
3. Keep people cost under 40% of income; the page shows the share.

UNDER THE HOOD

Collections: staff, payruns, hires (admin-only). The hiring plan has a revenue trigger per role; the AI workforce mirrors the same roles.

Formcraft Tools BUSINESS

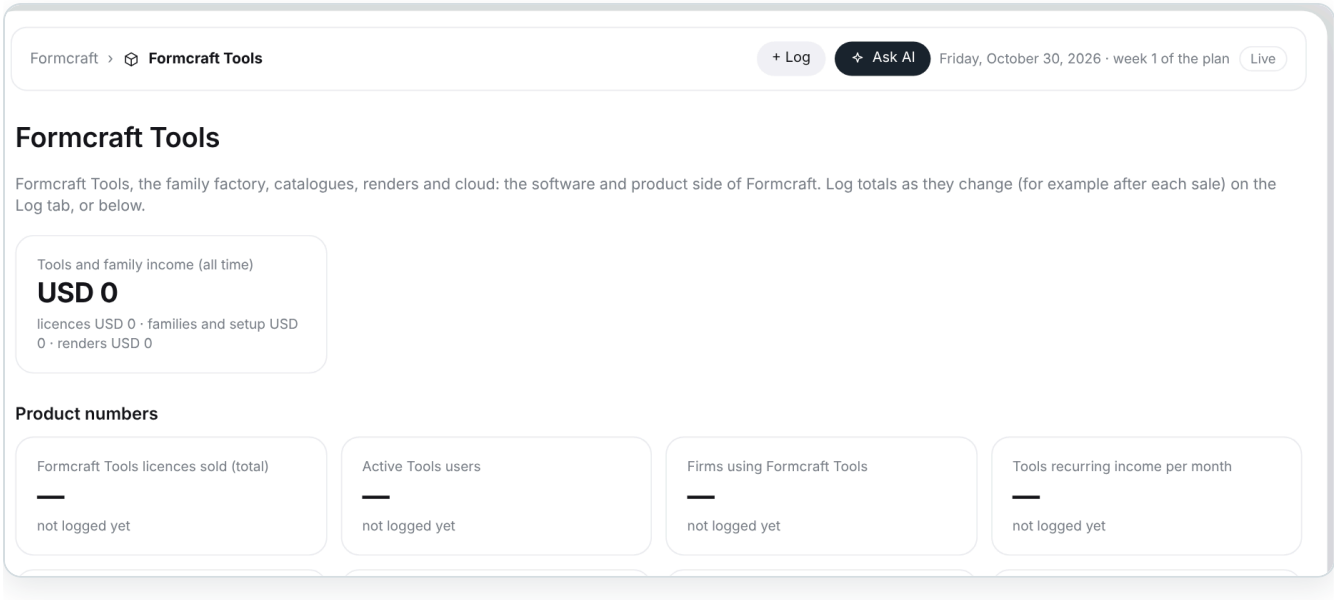

The software and product side: Formcraft Tools for Revit, the family factory, catalogues, renders and cloud seats. Income and the product numbers (licences, users, families sold, library size, tests passing).

HOW TO USE IT

1. Log totals as they change, for example after each sale.

UNDER THE HOOD

Product numbers are metrics in the log collection, so targets and the simulation can use them.

Content BUSINESS

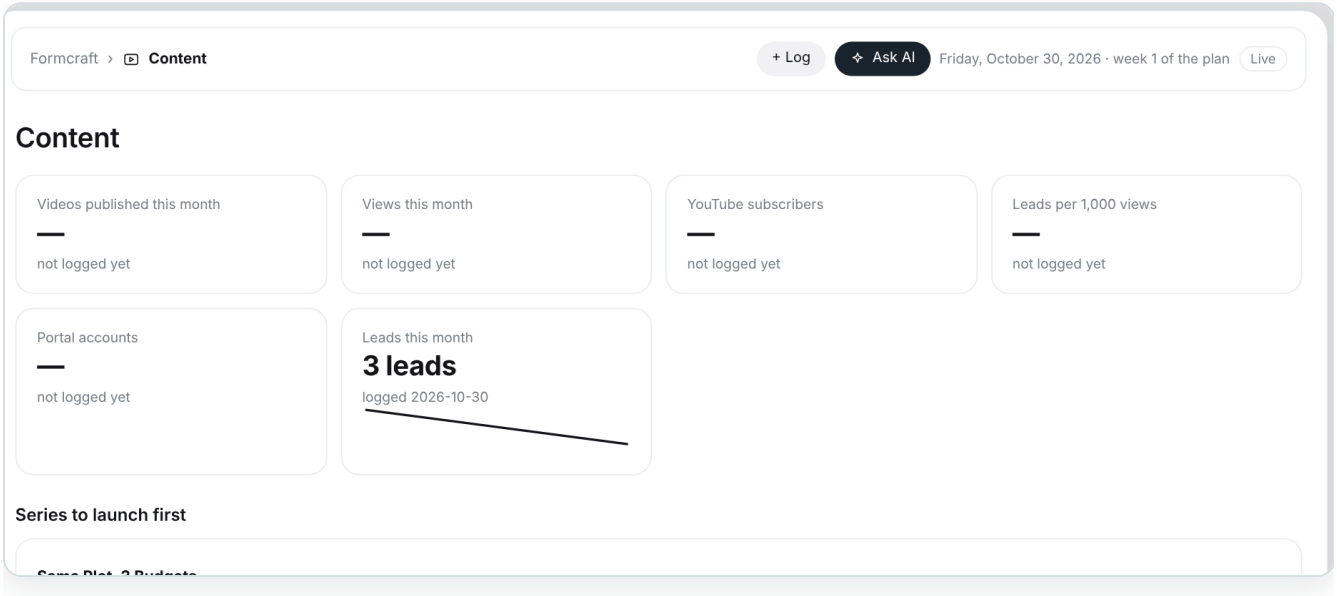

The content scoreboard: videos published, views, YouTube subscribers, leads per 1,000 views, portal accounts, and the series to launch first (Same Plot, 3 Budgets; Every Shilling; Plot to Permit Race).

HOW TO USE IT

1. Log the YouTube Studio numbers weekly.
2. Judge each video on click-through rate, average view duration and leads per 1,000 views.

UNDER THE HOOD

Metrics in the log collection: videos_month, views_month, yt_subs, leads_per_1000.

Content plan (year) BUSINESS

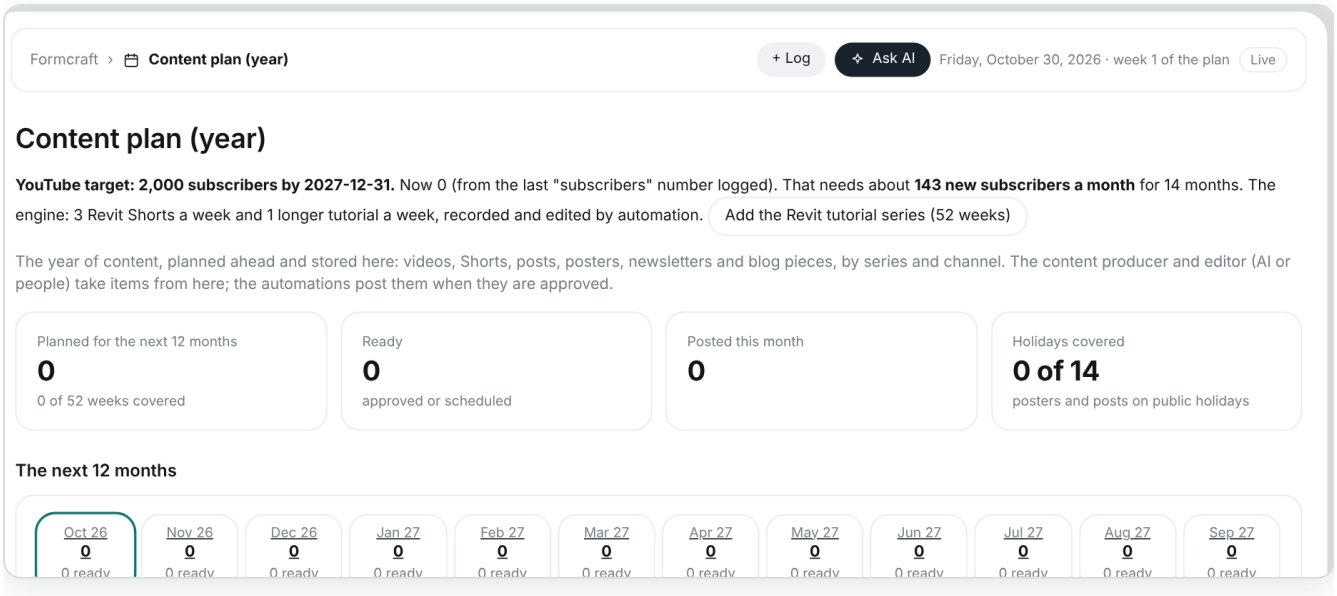

The year of content, planned ahead: videos, Shorts, posts, posters, newsletters and blog pieces, by channel and series, month by month. It also holds the Revit tutorial factory: a 52-week topic list plus tool guides, aimed at 2,000 YouTube subscribers by 31 December 2027 (about 143 new subscribers a month).

HOW TO USE IT

1. Press 'Add the Revit tutorial series (52 weeks)' once.
2. Fill each month; months with nothing ready show in amber.
3. Items move Idea, Planned, Scripted, In production, Approved, Scheduled, Posted. Esther approves; automations post.

UNDER THE HOOD

Collection: cplan {date, channel, series, title, status}. Channels: YouTube, Shorts and Reels, TikTok, Instagram, Facebook, X, LinkedIn, Newsletter, Blog, Poster, WhatsApp status. Automations VC-08 (tutorial recorder) and VC-09 (assembly) produce the videos.

Events to attend BUSINESS

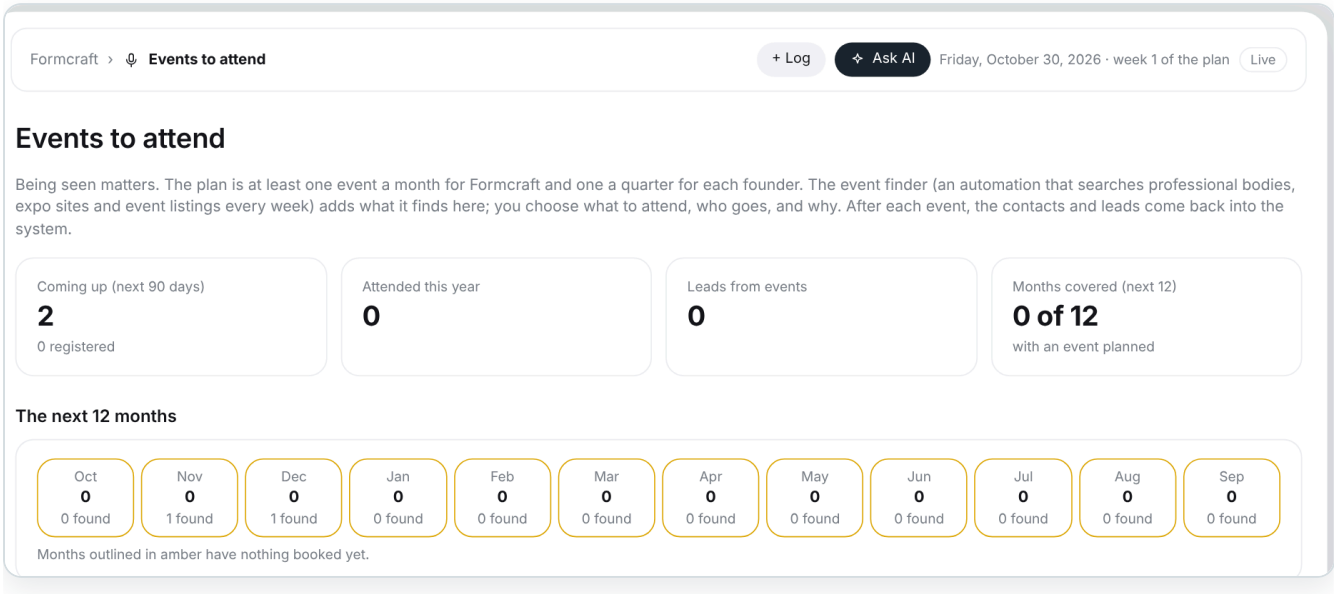

Events to attend: expos, conferences, CPD seminars, networking, awards. The plan is at least one event a month for Formcraft and one a quarter for each founder. The event finder (DD-14) searches every week and adds what it finds.

HOW TO USE IT

1. Review 'Found' events; set Considering, Registered or Skipped; choose who goes and why (leads, partners, CPD, hiring).
2. Paste an event listing and press 'AI: pull out the events'.
3. After the event mark Attended: a follow-up task is created to add the people you met to Sales and the directory.

UNDER THE HOOD

Collection: xevents {name, type, date, place, cost, status, who[], goals}. Registered events are copied to the calendar.

Website and SEO BUSINESS

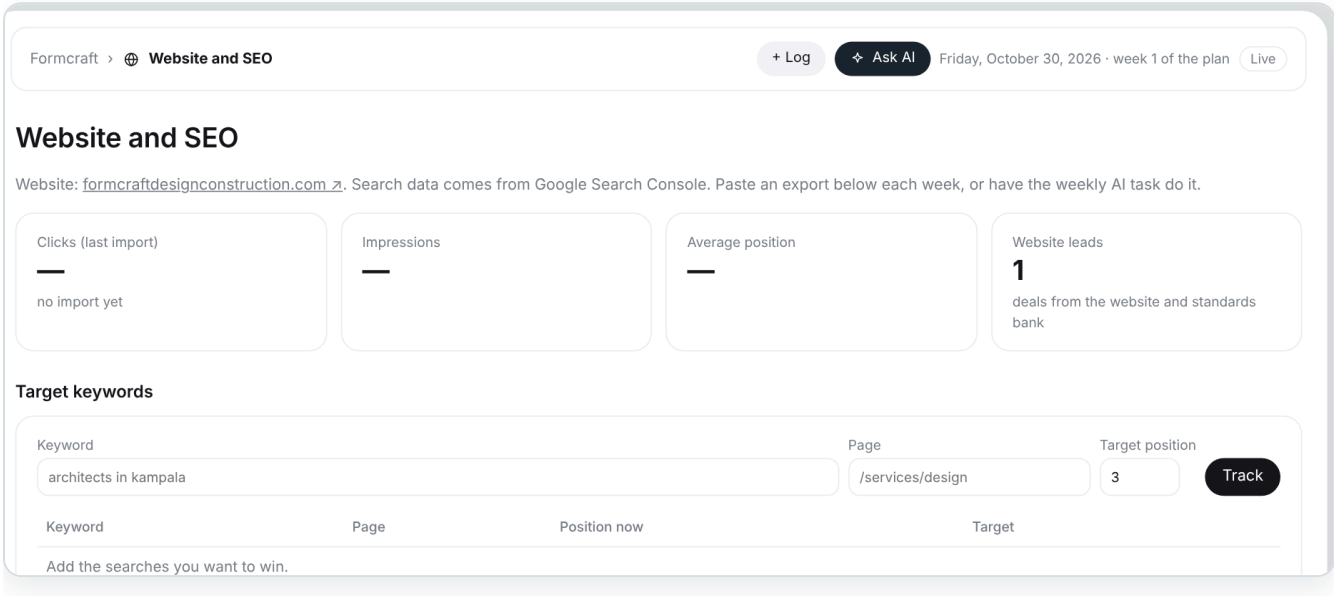

The website and search: target keywords, positions, clicks and impressions from Google Search Console, and website numbers (visits, visit-to-lead rate, pages indexed, page speed).

HOW TO USE IT

1. Add the searches you want to win and the page that should rank.
2. Paste the Search Console export weekly (or let the weekly AI task do it).

UNDER THE HOOD

Collection: seokw; imports are logged as web_clicks, web_impr, web_position metrics.

Leads and email BUSINESS

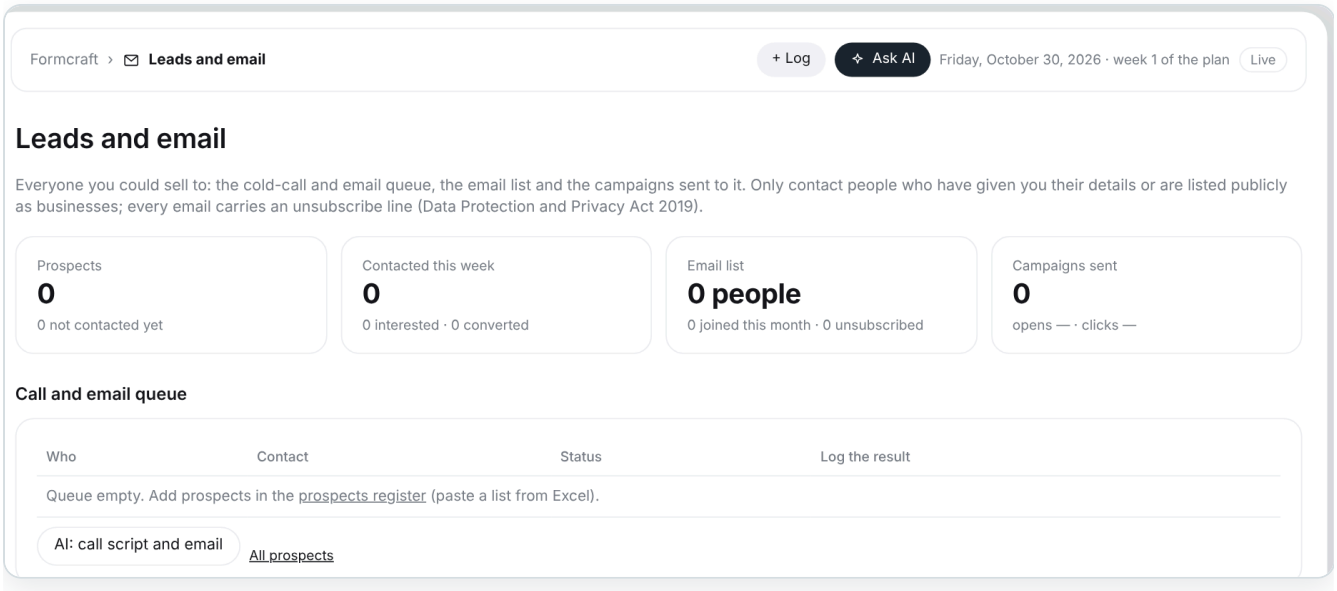

Everyone you could sell to: the call and email queue, the email list and the campaigns. Only contact people who gave their details or are listed publicly as businesses; every email has an unsubscribe line.

HOW TO USE IT

1. Paste prospects into the Prospects register from Excel.
2. Work the queue: log each result.
3. Use 'AI: call script and email' for a first draft.
4. Export the list as CSV for the email platform.

UNDER THE HOOD

Collections: reg_prospects, reg_subscribers, campaigns. Consent is a field on every prospect (Data Protection and Privacy Act 2019).

Licences and subscribers BUSINESS

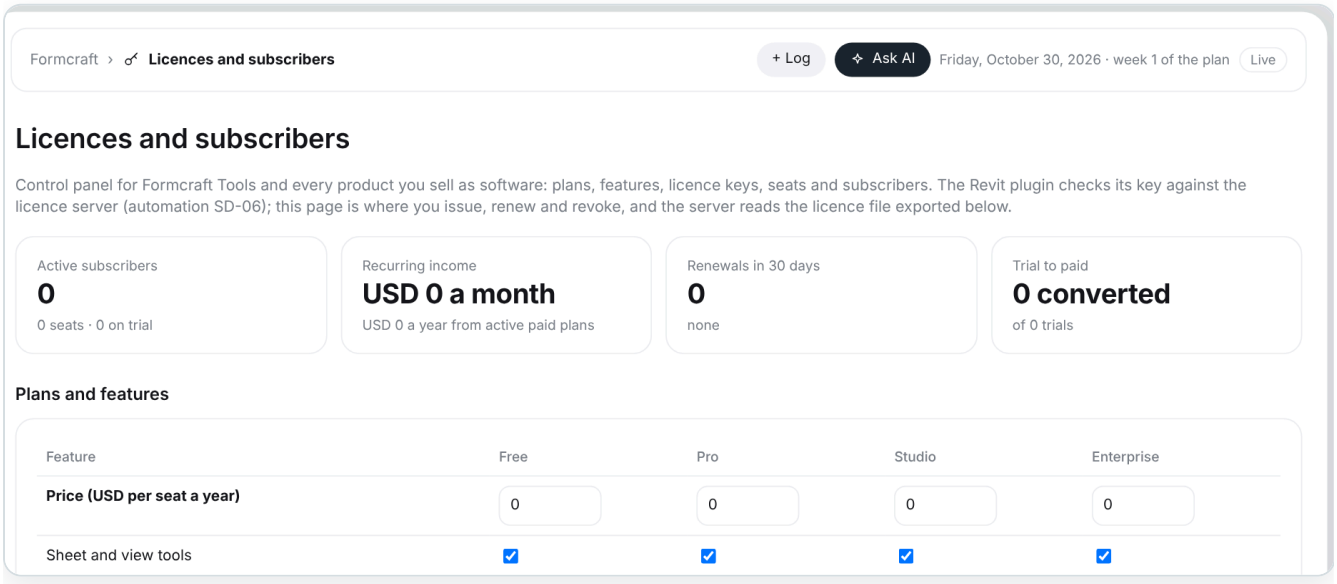

Control panel for Formcraft Tools as software: plans (Free, Pro, Studio, Enterprise), features per plan, licence keys, seats, subscribers, renewals and trials. The Revit plugin checks its key against the licence file exported here.

HOW TO USE IT

1. Set prices on Pricing and efficiency first, then here.
2. Issue a licence to a customer; export the licence file for the server.

UNDER THE HOOD

Collection: lic (admin-only). Automation SD-06 is the licence server check.

Pricing and efficiency BUSINESS

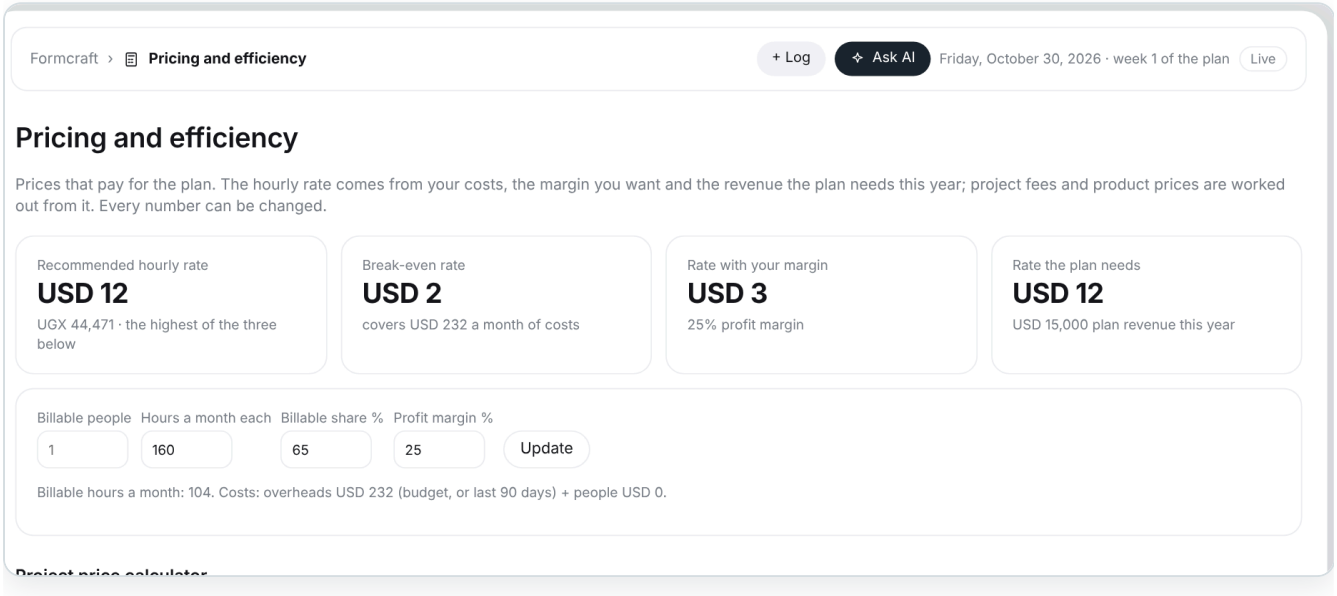

Prices that pay for the plan. It works out three hourly rates (break-even, with your margin, and what the plan's revenue needs) and recommends the highest, then prices projects by area, complexity, finish and RIBA stages.

HOW TO USE IT

1. Enter billable people, hours, billable share and margin.
2. Use the project price calculator for any quote.
3. Keep your own benchmarks (cost per m²) up to date.

UNDER THE HOOD

Reads overheads from the budget (or the last 90 days), people cost, and the plan's revenue target. The auto-quote on Enquiries uses this rate.

Feasibility studies BUSINESS

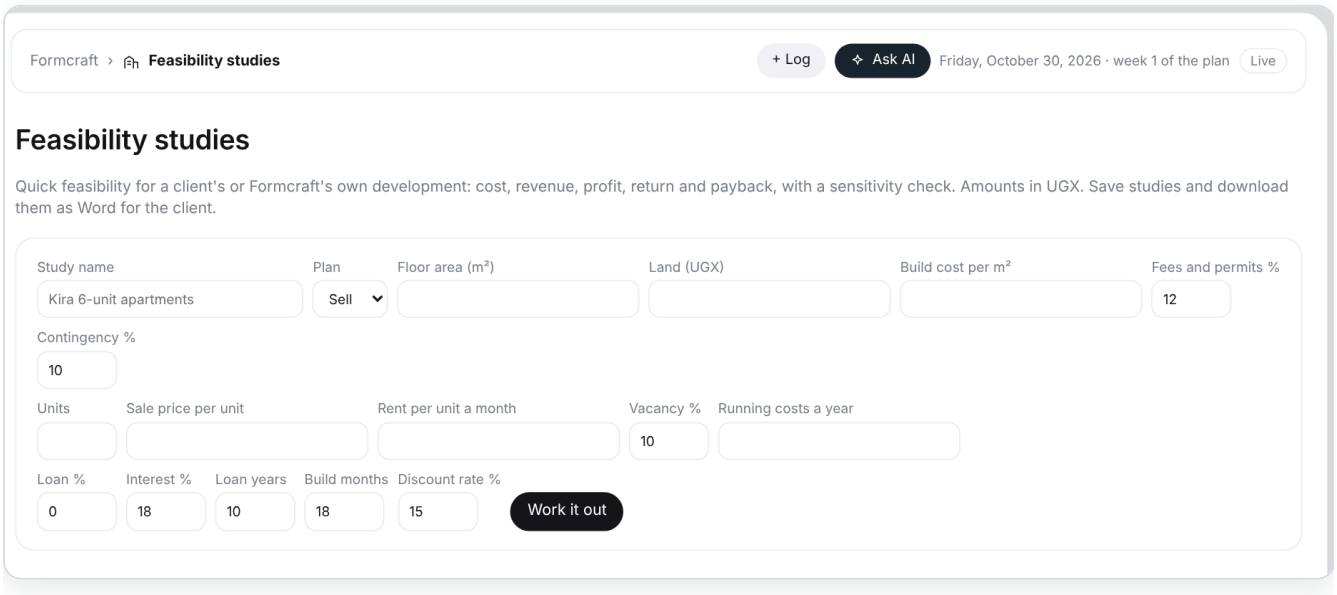

Quick feasibility for a client's or Formcraft's own development: cost, revenue, profit, return and payback, with a sensitivity check. Plan to sell or to rent. Amounts in UGX.

HOW TO USE IT

1. Enter area, land, build cost per m², fees, contingency, units and price.
2. Save the study and download it as Word for the client.

UNDER THE HOOD

Collection: feas. Sensitivity runs ±10% on cost and price.

Global reach BUSINESS

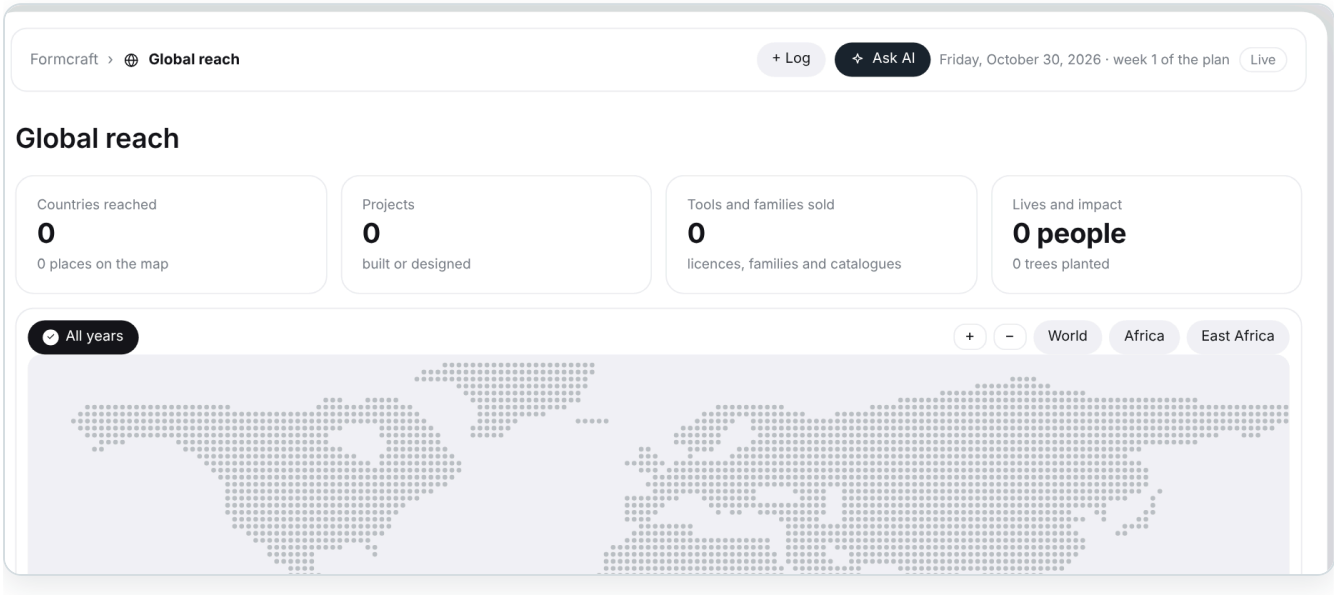

A world map of Formcraft's reach: projects, tools and family sales, website visitors, YouTube viewers, people trained and trees planted.

HOW TO USE IT

1. Add each item with a place and a number; dots grow with the number.

UNDER THE HOOD

Collection: reach {place, lat, lon, what, value, date}.

Incentives and funding BUSINESS

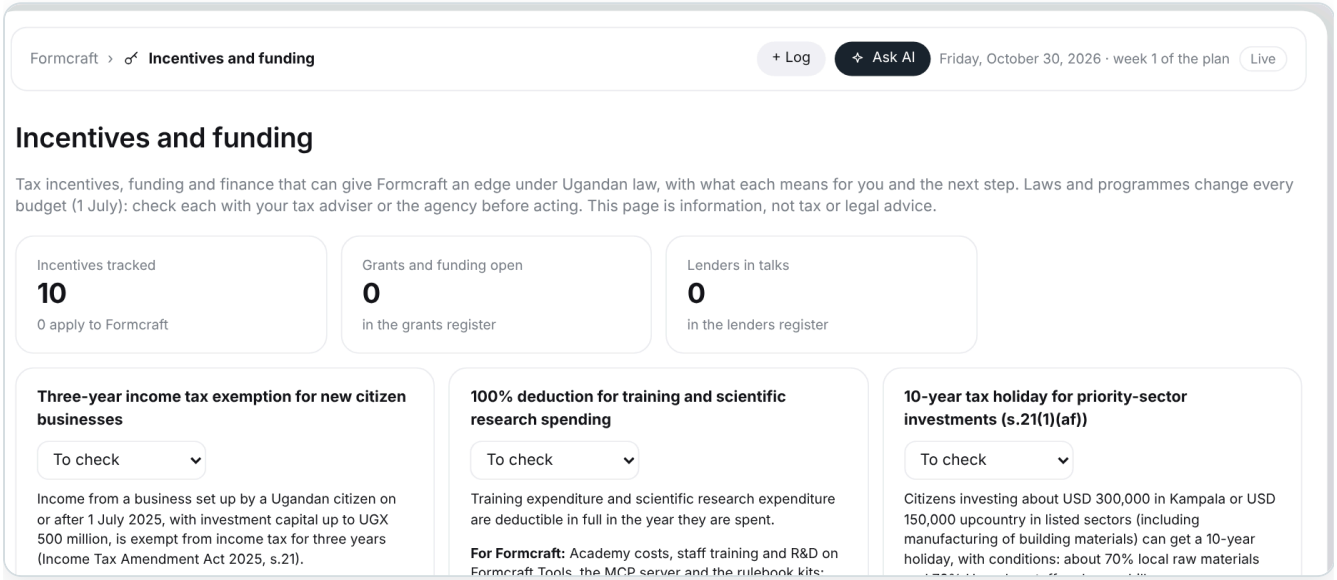

Tax incentives, funding and finance available under Ugandan law, with what each means for Formcraft and the next step. Information, not tax or legal advice: check with the adviser before acting.

HOW TO USE IT

1. Mark each incentive: To check, Applies to us, Applied, Not for us.
2. Track grants and lenders in their registers.

UNDER THE HOOD

Static guide in the app plus reg_grants and reg_lenders. Laws change every budget (1 July).

Building playbook BUSINESS

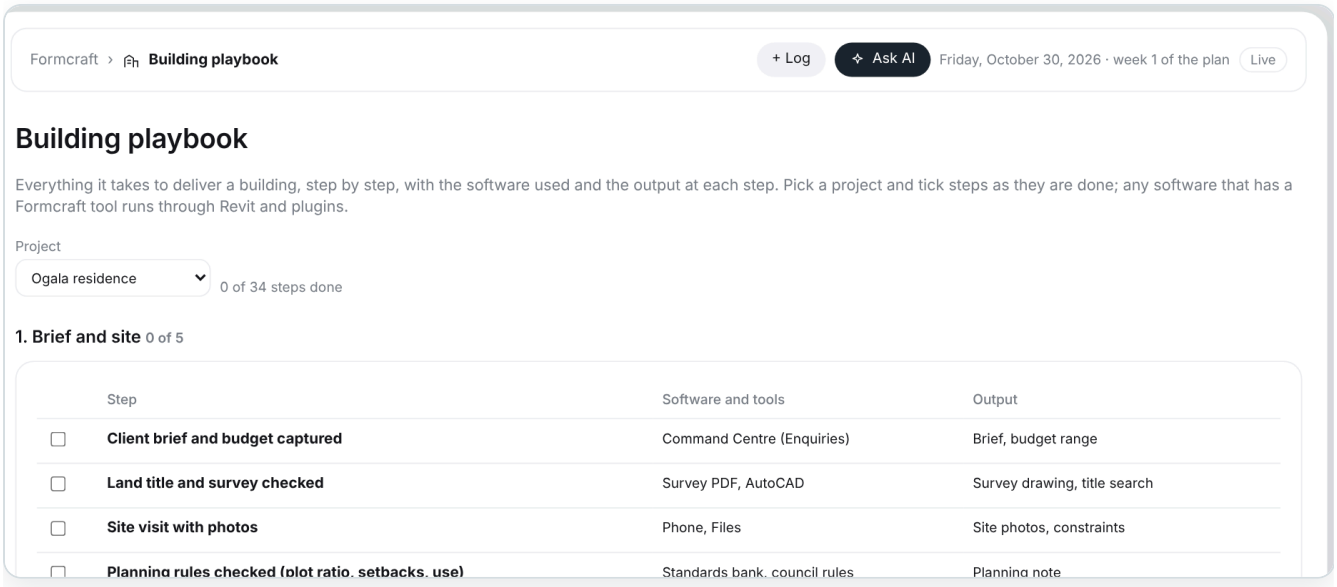

Everything it takes to deliver a building, step by step (34 steps in stages), with the software used and the output at each step.

HOW TO USE IT

1. Pick a project and tick steps as they are done.

UNDER THE HOOD

Ticks stored per project. Any step that has a Formcraft tool runs through Revit and plugins.

4.3 Build and AI pages

The machine room: agents, automations, AI cost, the standards bank, templates, files and the Revit link.

AI hub and memory BUILD AND AI

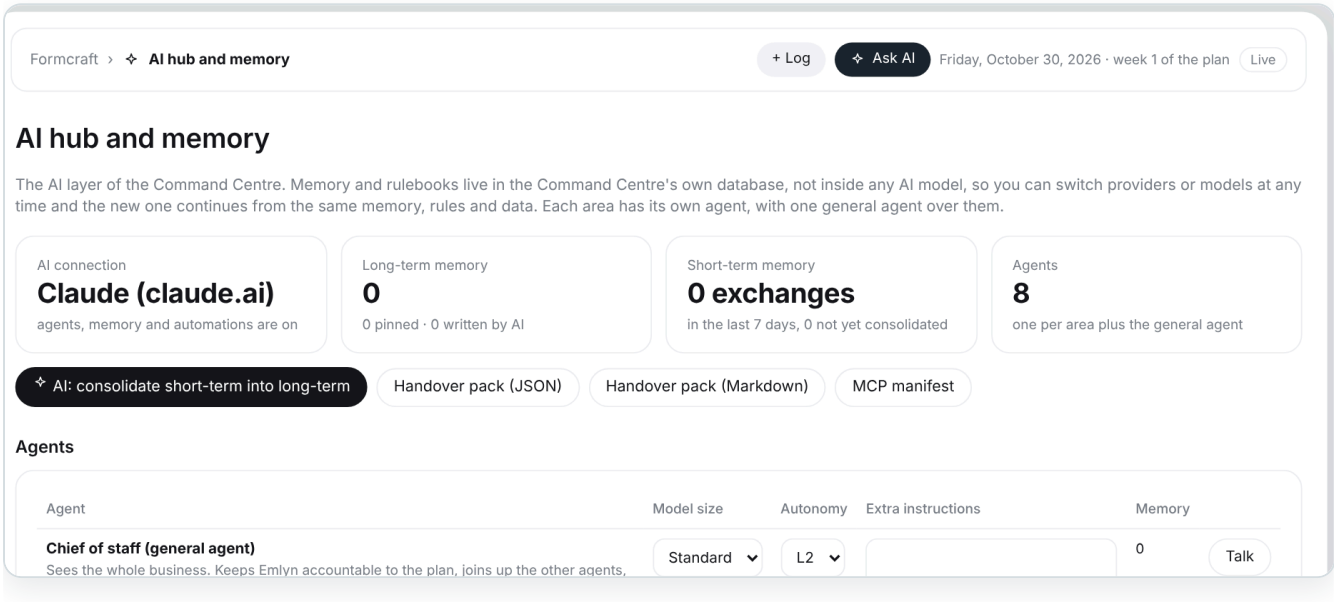

The AI layer. Memory and rulebooks live in Formcraft's own database, not inside any AI model, so you can switch provider or model at any time and the new one continues from the same memory, rules and data. Each area has its own agent with one general agent (Chief of staff) over them.

HOW TO USE IT

1. Set the AI connection and the model for each tier.
2. Set each agent's model size (Fast, Standard, Deep) and autonomy (L0 to L4).
3. Talk to an agent directly with Talk.
4. Weekly: 'AI: consolidate short-term into long-term' memory.
5. Download the handover pack (JSON or Markdown) to move to another AI tool.

UNDER THE HOOD

Collections: memory (long-term, pinned), ailog (short-term exchanges), aistaff, settings.ai. 8 agents: Chief of staff (general), Finance, Sales and marketing, Projects and site, Design and BIM, Software and automation, People and admin, Legal and risk. The MCP manifest lists the tools any outside AI can call (get_brief, read_data, query_register, propose_actions, list_pending, apply_approved, remember, recall, handover_pack, log_metric).

Automations and bots BUILD AND AI

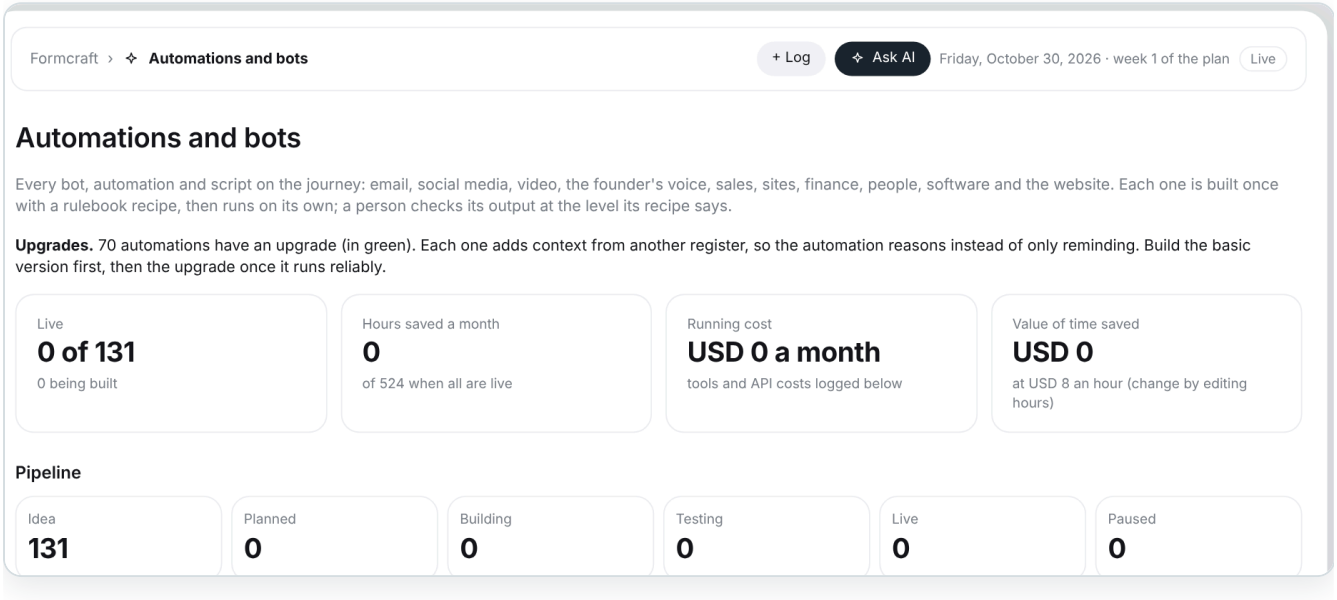

The catalogue of every bot and automation on the journey: 128 in 13 groups (email, social, video, founder voice, sales, clients, finance, people, software, website, operations, scrapers, alerts). Each has a trigger, what it is built with, hours saved and a phase. Many have an 'upgrade' that adds context from another register.

HOW TO USE IT

1. Move each through Idea, Planned, Building, Testing, Live, Paused.
2. Build the basic version first, the upgrade only once it runs reliably.
3. Watch 'Live of 131' and hours saved a month; they are the real automation score.

UNDER THE HOOD

AUTOS table in the app: A(code, group, name, description, trigger, built with, hours, phase). Status in settings. Today: 0 live. This is the most important number to move.

Dev and kits BUILD AND AI

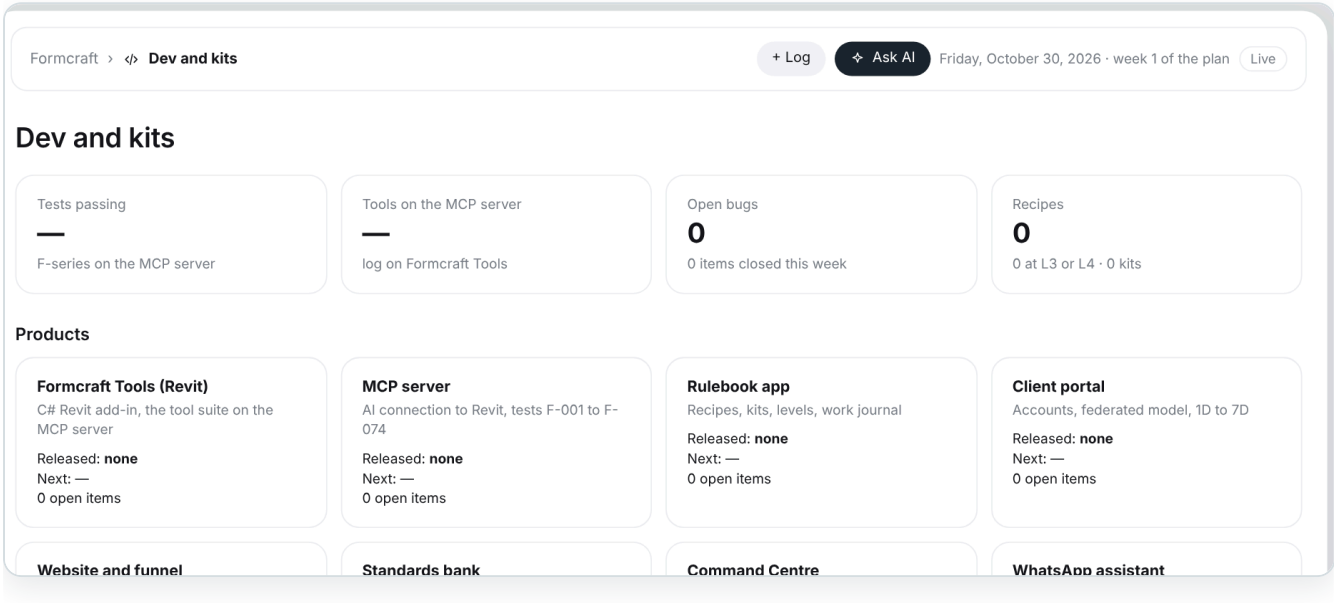

The development room for every product: Formcraft Tools (Revit add-in), the MCP server, the rulebook app, client portal, website and funnel, standards bank, Command Centre, WhatsApp assistant, family factory. Releases, next version, open items, tests passing and recipes.

HOW TO USE IT

1. Log each release; keep open items in the issue list.
2. The Windows hub's development room replaces this on the main PC (phase 6).

UNDER THE HOOD

Collections: issues, reg_releases, reg_recipes, reg_kits.

Systems map BUILD AND AI

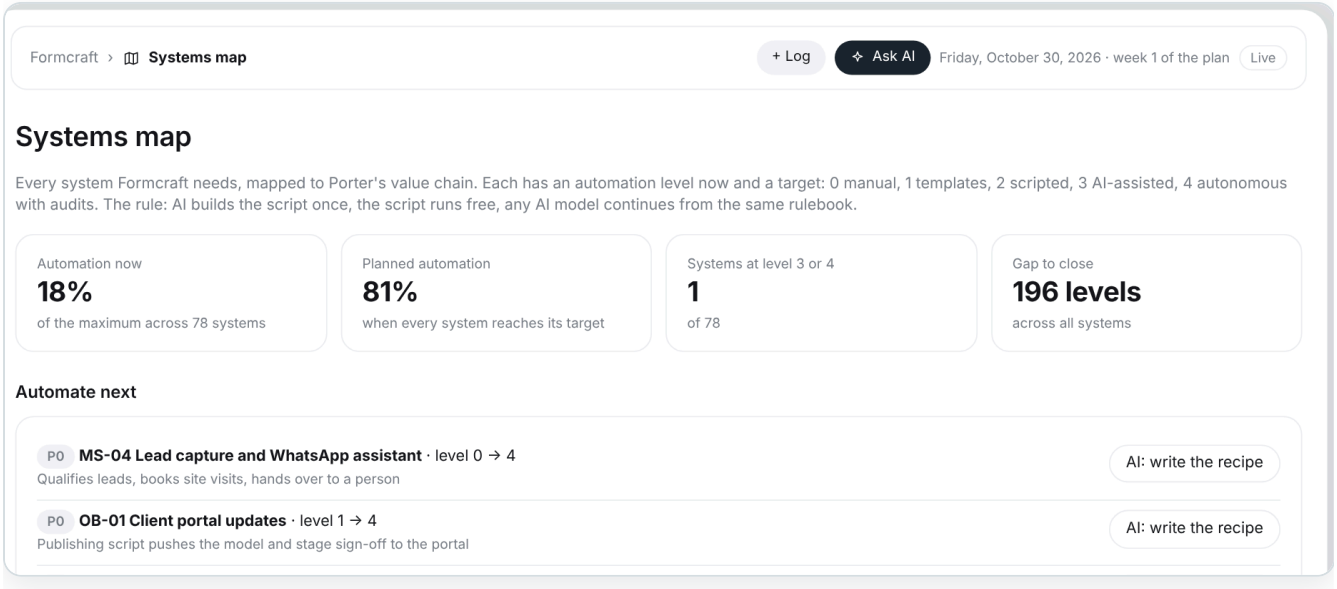

Every system Formcraft needs (78), mapped to Porter's value chain, each with its automation level now and its target: 0 manual, 1 templates, 2 scripted, 3 AI-assisted, 4 autonomous with audits. 'Automate next' lists the highest-priority gaps.

HOW TO USE IT

1. Use 'AI: write the recipe' on the top gap; build it; raise its level.

UNDER THE HOOD

Today 18% of the maximum; planned 81%. The rule: AI builds the script once, the script runs free.

AI workforce BUILD AND AI

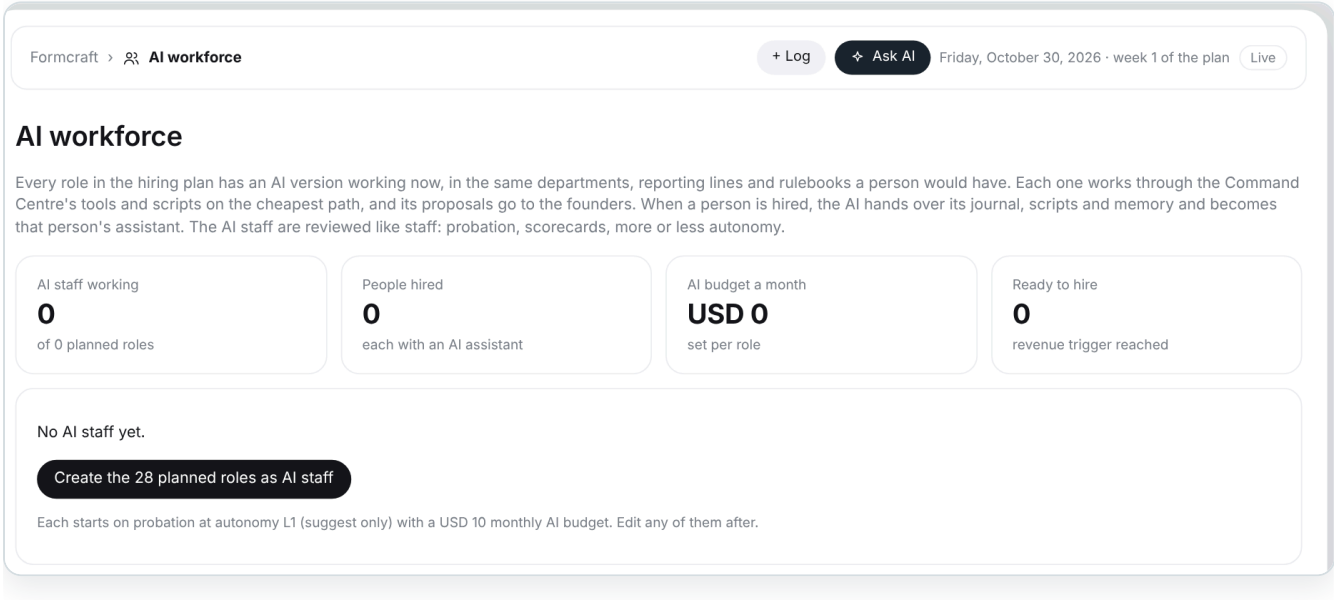

Every role in the hiring plan (28) has an AI version working now, in the same departments, reporting lines and rulebooks a person would have. AI staff are reviewed like staff: probation, scorecards, more or less autonomy. When a person is hired, the AI hands over its journal, scripts and memory and becomes that person's assistant.

HOW TO USE IT

1. Press 'Create the 28 planned roles as AI staff'. Each starts on probation at L1 (suggest only) with a USD 10 monthly budget.
2. Read each role's scorecard weekly; raise autonomy when errors stay under 2%.
3. When you hire, press Handover.

UNDER THE HOOD

Collection: aistaff {role, dept, reports_to, tier, budget, autonomy, score}. Roles from PLAN27; each reports to a founder (Emlyn: studio, BIM, software, product; Peter: engineering, construction, concrete, finance and HR; Esther: sales, content, stores, reception).

Data explorer BUILD AND AI

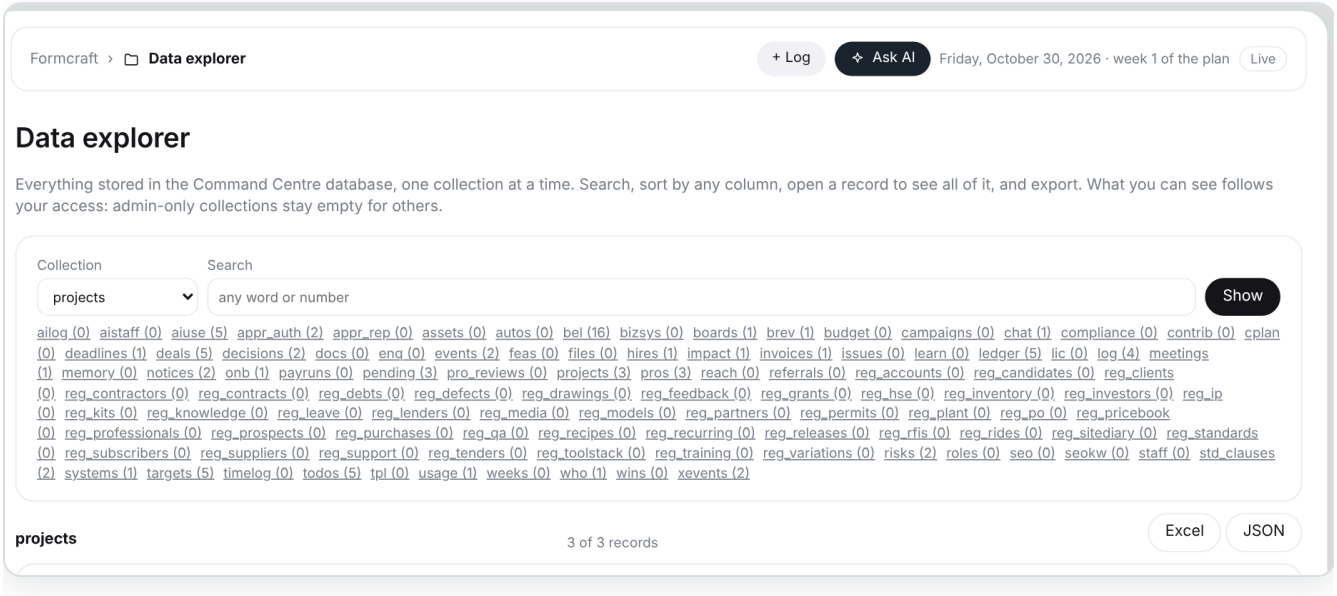

Every collection in the database, one at a time: search, sort by any column, open a record, export. What you can see follows your access.

HOW TO USE IT

1. Choose a collection; type to search; click a header to sort; export to Excel or JSON.

UNDER THE HOOD

Reads any collection by name. Admin-only collections stay empty for others because the database rules block them.

AI cost BUILD AND AI

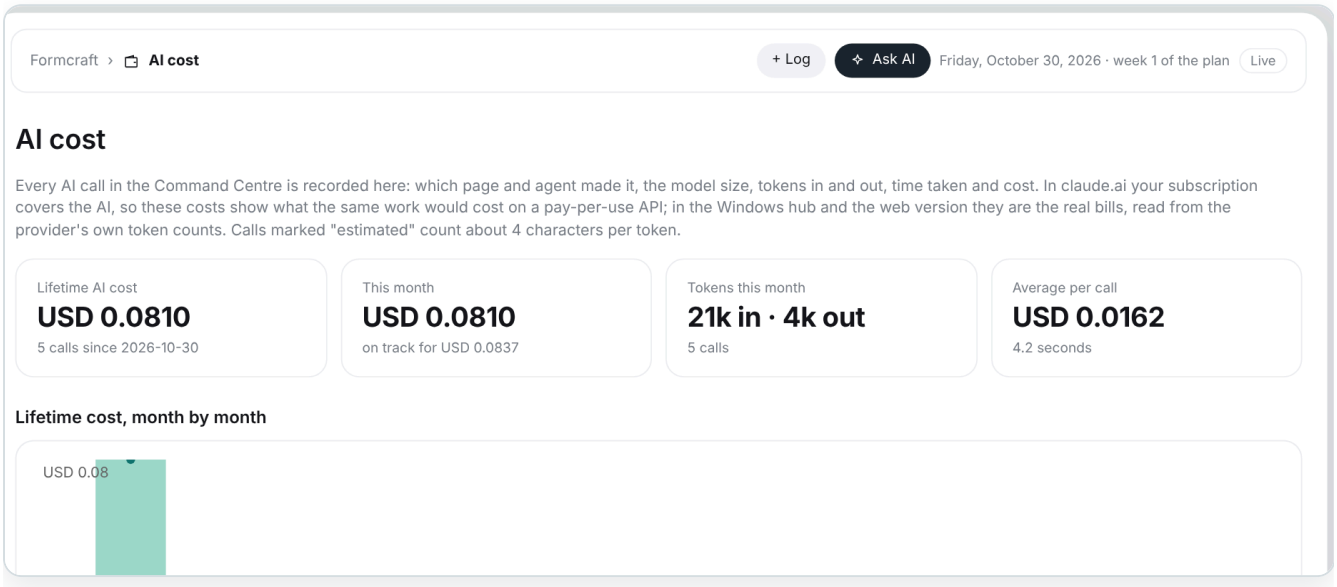

Every AI call is recorded: which page and agent made it, the model tier and provider, tokens in and out, time and cost. Lifetime cost, this month and projected month-end, and where the money goes by page, agent and model.

HOW TO USE IT

1. Set each provider's prices per million tokens.
2. Check monthly that the cheap tiers (scripts, offline, DeepSeek) carry most calls.

UNDER THE HOOD

Every call to the AI goes through wrapSample(), which writes aiuse {at, month, page, agent, tier, provider, inTok, outTok, est, cost, ms, ok}. In claude.ai the subscription pays, so costs show what the same work would cost on an API; in the hub and web version they are real bills from the provider's token counts.

Build list BUILD AND AI

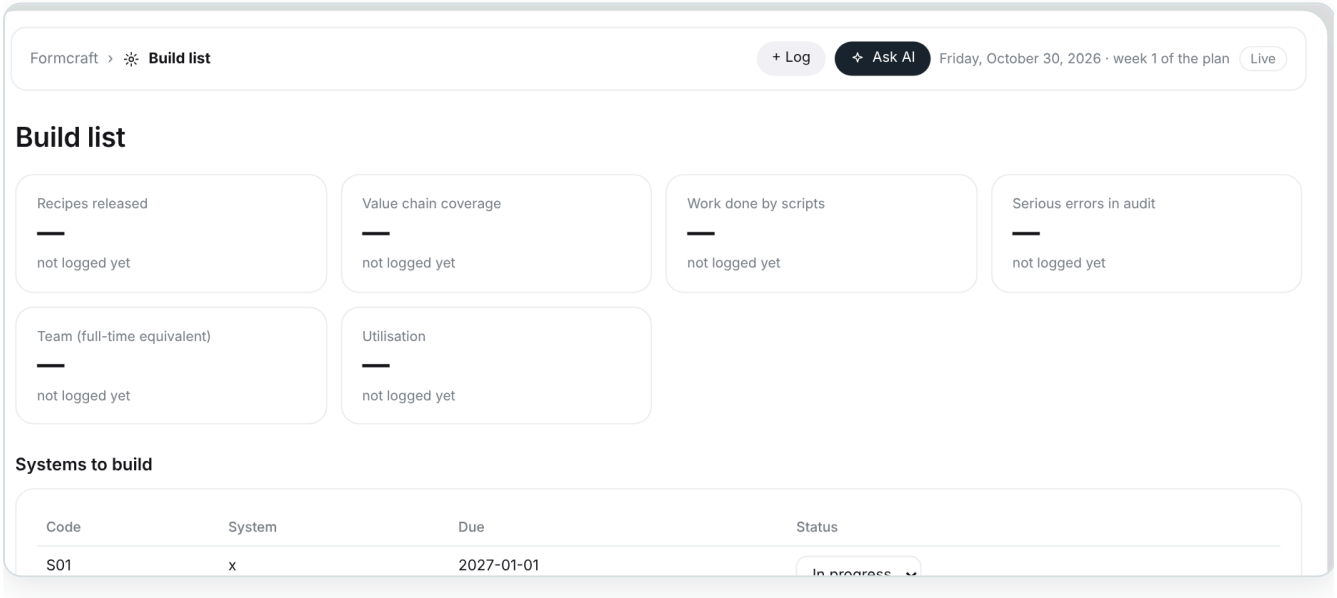

The build list: systems to build with due dates and status, and the AI and systems numbers (recipes released, value chain coverage, work done by scripts, serious errors in audit).

HOW TO USE IT

1. Keep it short: only what the next 90 days need.

UNDER THE HOOD

Collection: systems. Metrics in the log.

Standards bank BUILD AND AI

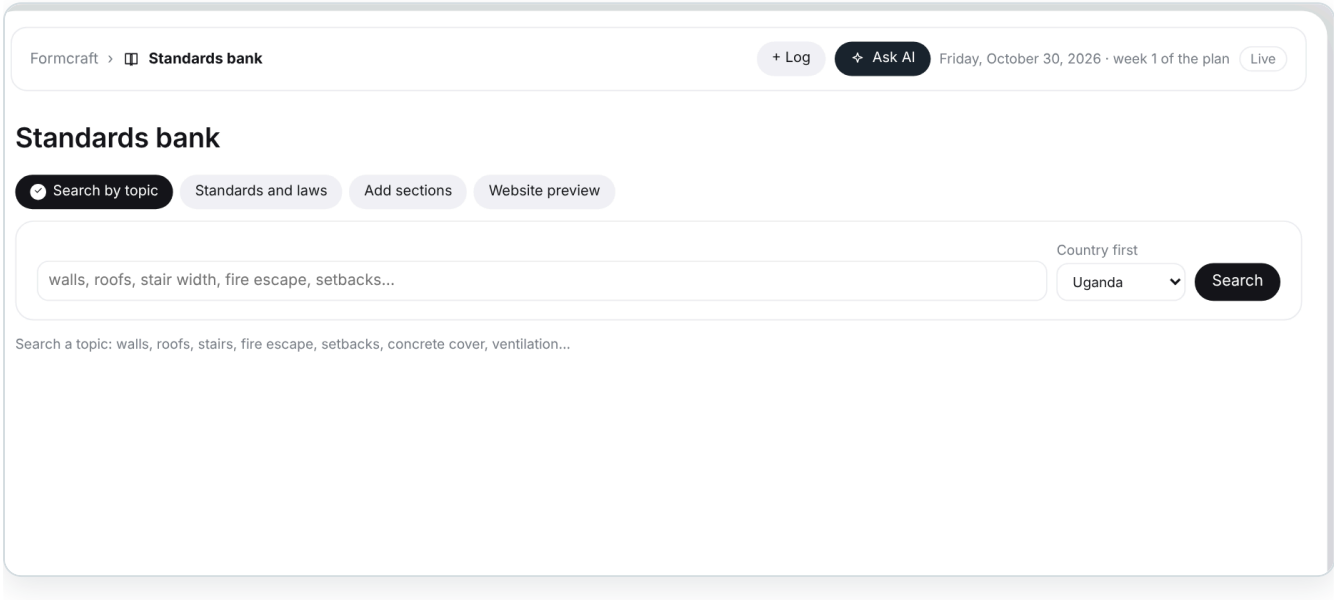

A searchable bank of building standards and laws by topic. Search 'walls' and you get every section about walls from every standard, your country first (Uganda first in Uganda, Kenya first in Kenya), each with its clause and page and a short summary. Formcraft never shares the standard's file: it says what the standard says on which page, then links to where to buy it.

HOW TO USE IT

1. Search by topic and choose the country first.
2. Add sections from a standard you own: clause, page, heading, topics, a short summary in your own words.
3. Mark which sections show on the website; check the website preview.

UNDER THE HOOD

Collection: std_clauses {std, source, link, kind, juris, ref, page, heading, topics, summary, lic}. searchClauses() expands the query with topic synonyms and ranks by jurisdiction (jurisRank). Licence rule in docs/windows-hub-plan.md §16: summaries and references only.

Enquiries and auto-quotes BUILD AND AI

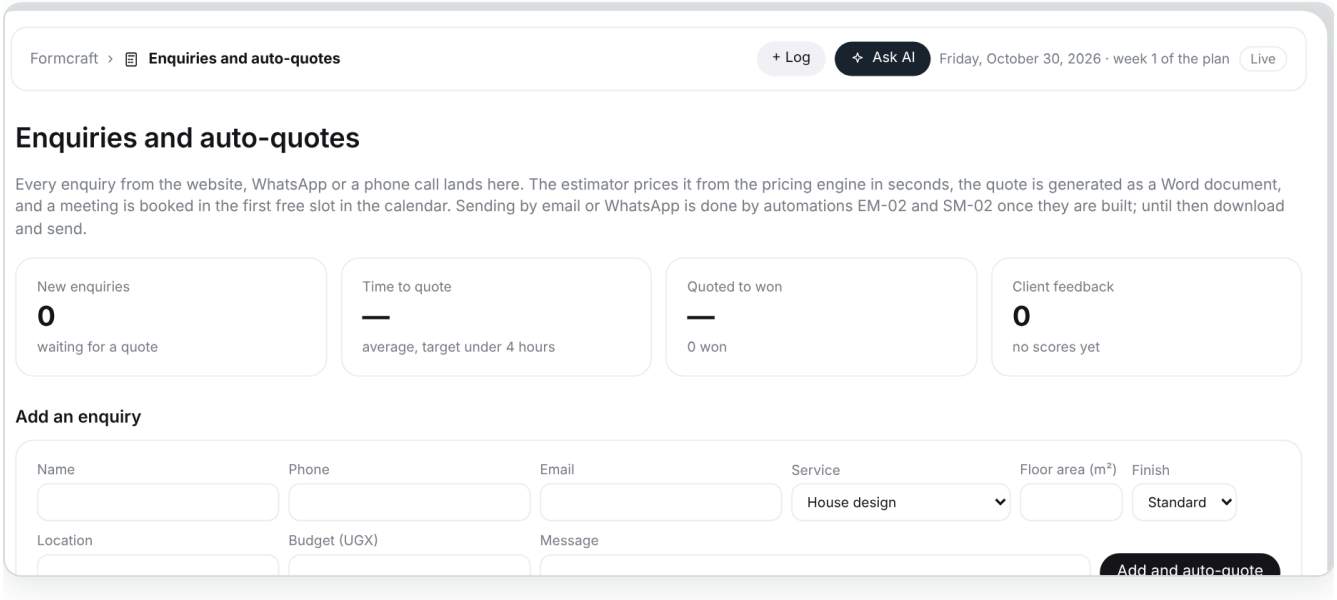

Every enquiry from the website, WhatsApp or a call lands here. The estimator prices it in seconds from the pricing engine, the quote is made as a Word document, and a meeting is booked in the first free calendar slot.

HOW TO USE IT

1. Add the enquiry (service, area, finish, location, budget) and press Add and auto-quote.
2. Check the estimate, download and send (until EM-02 and SM-02 send it for you).
3. Target: quote in under 4 hours.

UNDER THE HOOD

Collection: enq. Uses the pricing rate and benchmarks; a won quote becomes a deal.

Revit and plugins BUILD AND AI

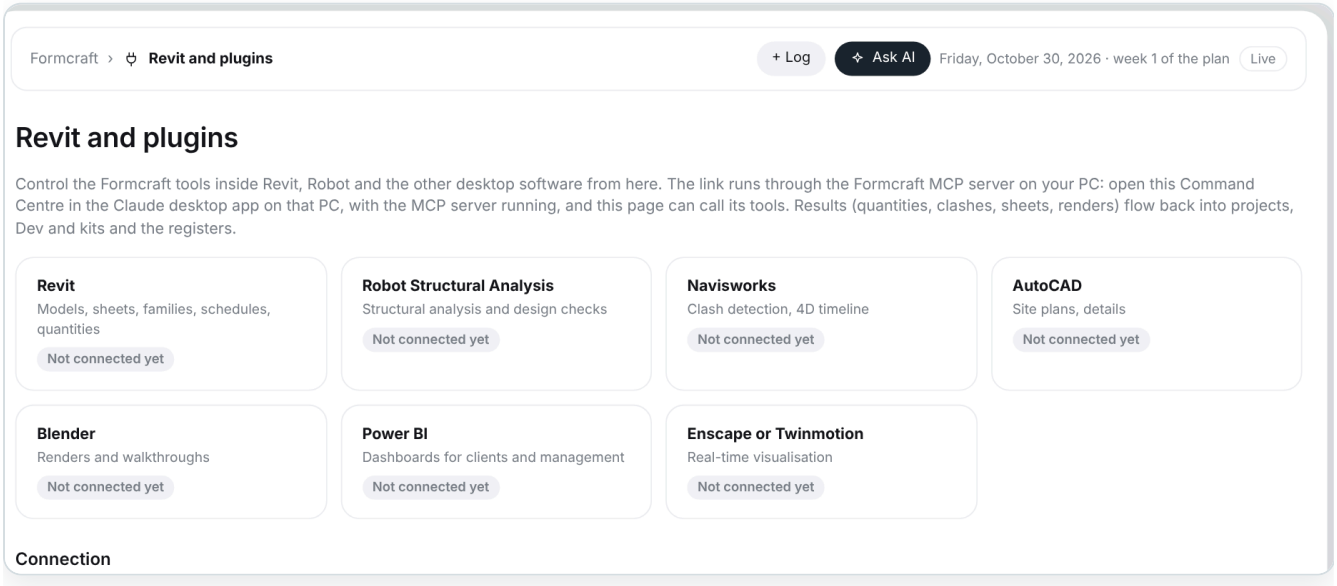

Control the Formcraft tools inside Revit, Robot, Navisworks, AutoCAD, Blender, Power BI and Enscape from here. The link runs through the Formcraft MCP server on the PC.

HOW TO USE IT

1. Start the MCP server on the PC; open the Command Centre in the Claude desktop app; set the server and tool names here.

UNDER THE HOOD

Each Revit window takes a port 8080 to 8089 and registers in %APPDATA%\Formcraft\instances; the hub keeps one job queue per window.

Templates BUILD AND AI

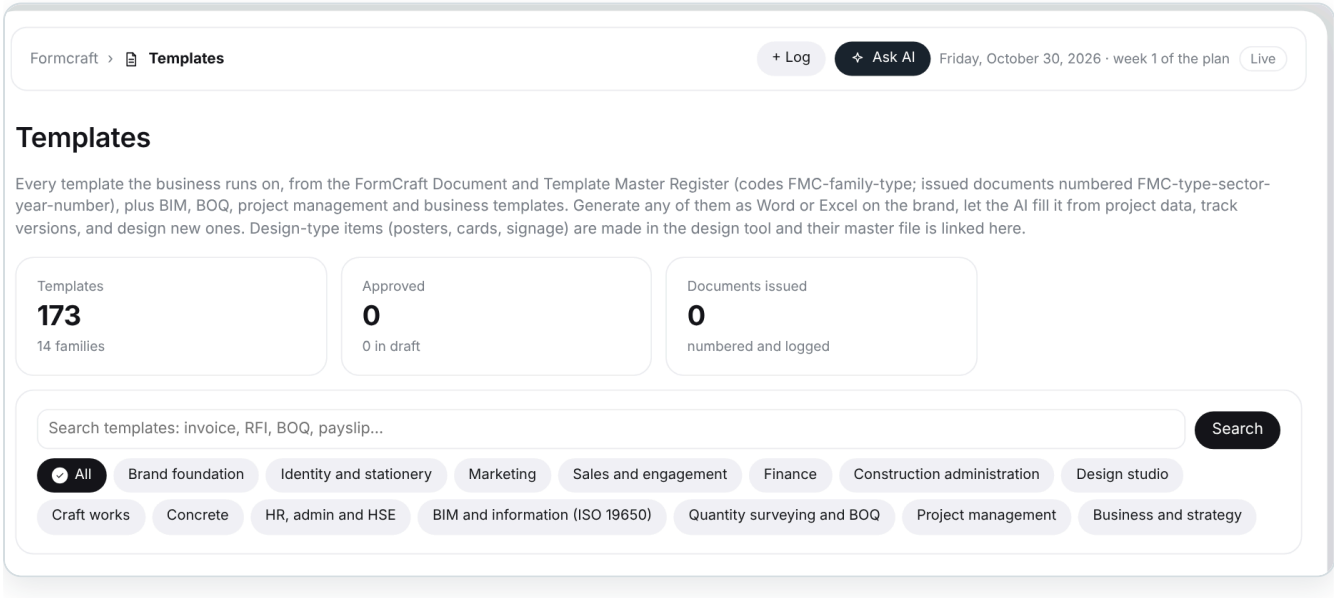

Every template the business runs on (173 in 14 families), from the FormCraft Template Master Register: codes FMC-family-type; issued documents numbered FMC-type-sector-year-number. Generate any as Word or Excel on the brand, let the AI fill it, track versions, design new ones.

HOW TO USE IT

1. Search, open, Use. Approve drafts before they go to clients.

UNDER THE HOOD

Template status: Not built, Draft, Approved. Automation SD-07 retires unused templates.

Documents BUILD AND AI

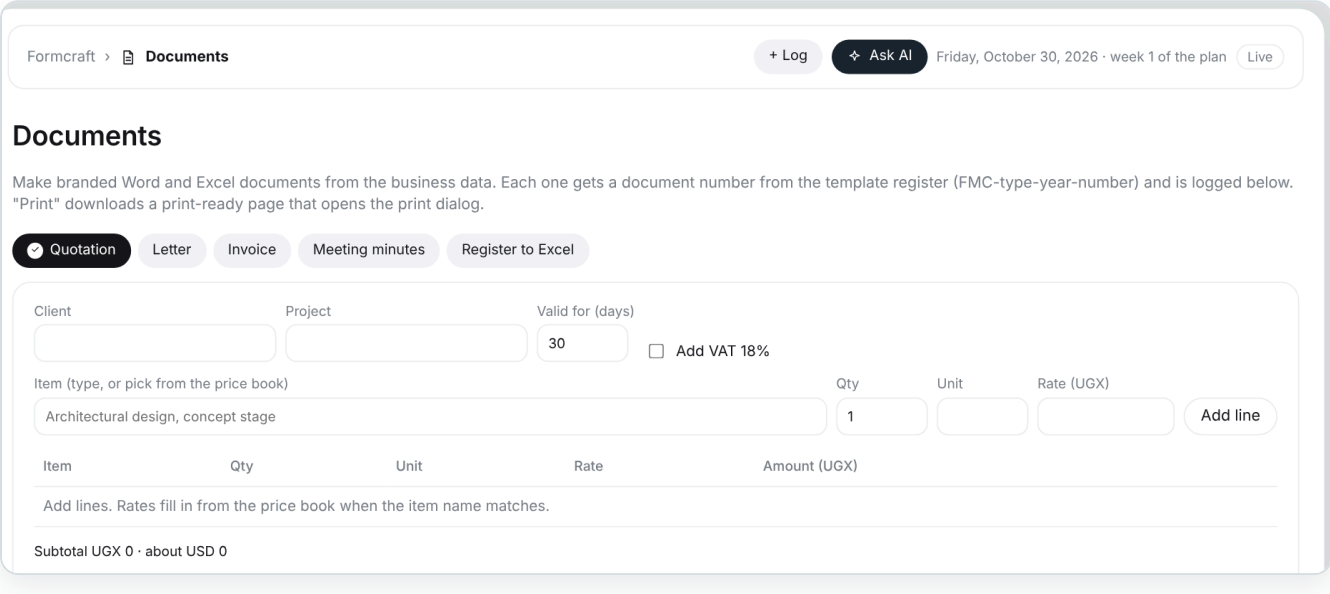

Make branded Word and Excel documents from the business data: quotation, letter, invoice, meeting minutes, register exports. Each gets a document number and is logged.

HOW TO USE IT

1. Pick the type, the client and project; add lines (rates fill from the price book).

UNDER THE HOOD

Collection: docs. Numbers follow the template register.

Files and media BUILD AND AI

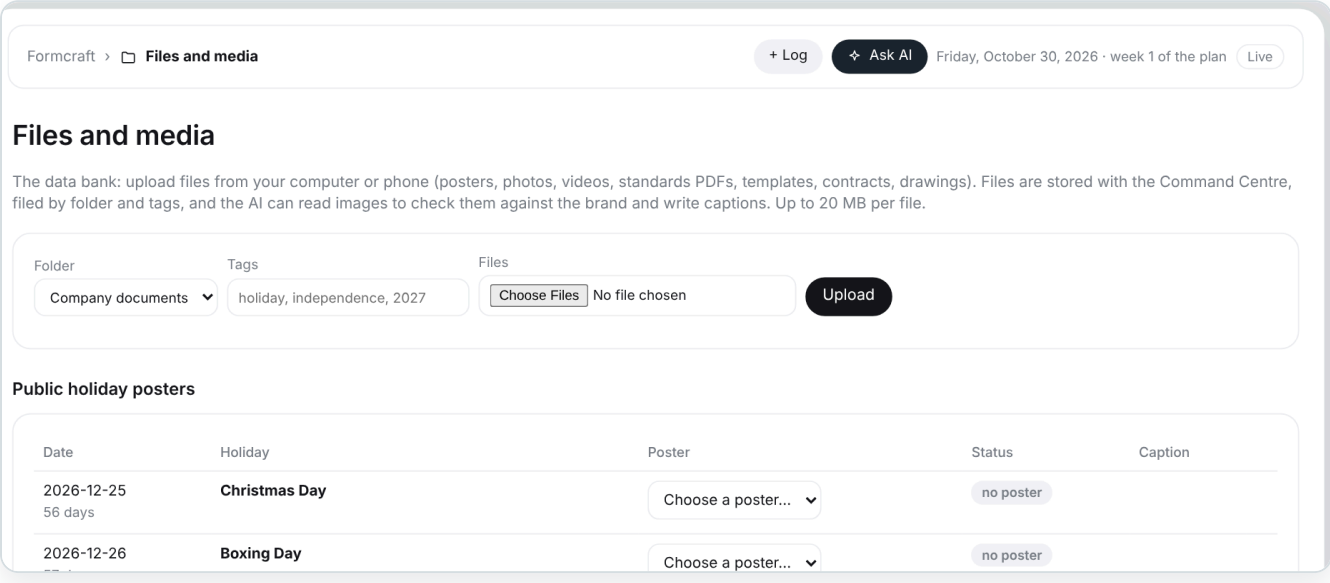

The data bank: upload files from computer or phone (posters, photos, videos, standards PDFs, contracts, drawings), filed by folder and tags. The AI can read images to check them against the brand and write captions. Also the public-holiday poster plan.

HOW TO USE IT

1. Choose a folder and tags, upload. Up to 20 MB a file.

UNDER THE HOOD

Collections: files, assets (stored with the Command Centre).

Live simulation BUILD AND AI

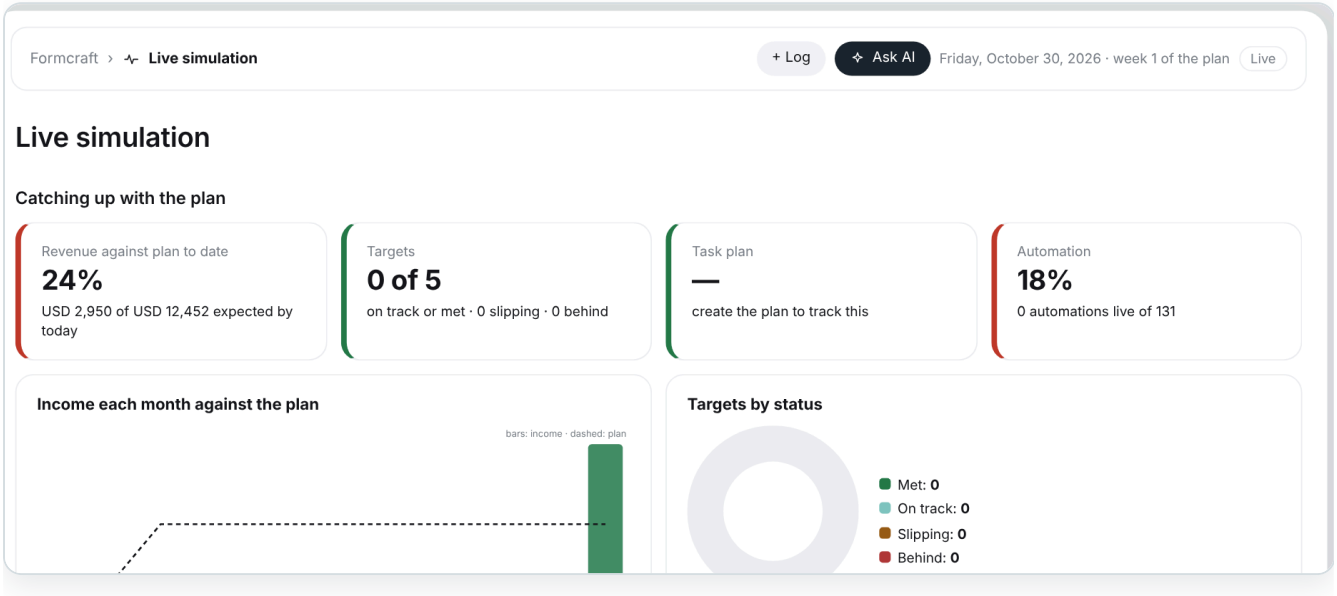

The live simulation: revenue against plan to date, targets on track, task plan progress, automation share, and the journey phases P0 to P5 with milestones done against time used.

HOW TO USE IT

1. Read it monthly with the founders: it is the plan's scoreboard.

UNDER THE HOOD

Plan curve from the feasibility model; actuals from ledger, targets and automations.

4.4 Registers

Registers are the lists the business runs on: 30 of them. Each one takes a paste from Excel or Google Sheets (copy the cells with the header row), exports to CSV or Excel, can be asked questions by the AI, and feeds its dates into the morning brief and the calendar. These nine are in the menu; All registers shows the rest (drawings, RFIs, variations, site diary, defects, permits, HSE, inventory, knowledge, training, leave, releases, recipes and more).

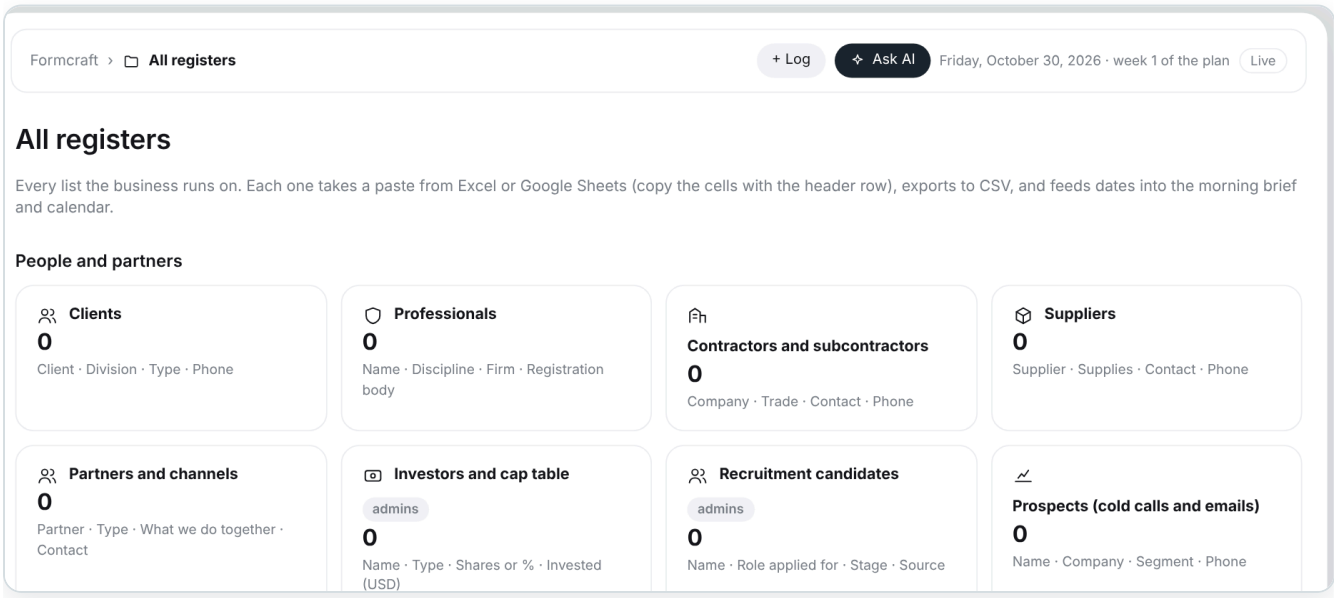

All registers. Example data.

Register	What it holds
Contracts	Every contract: type, value, dates, retention, signed or not, key terms. Admin-only.
Price book	Rates for materials, labour, plant and fees by region and date, with the source. Documents and quotes read rates from here.
Professionals	Architects and engineers Formcraft retains: registration body, number and expiry.
Contractors	Subcontractors by trade: insurance expiry, prequalification, rating.
Suppliers	Who supplies what, terms, on-time delivery, rating. Supplier price calls update the price book.
Clients	Every client with division, type, source and lifetime value.
Prospects	People you could sell to, with consent to be contacted.
Lenders	Banks, SACCOs, funds and grant bodies: what they offer and the next step. Admin-only.
Company assets	Computers, survey kit, formwork, vehicles: tag, holder, condition, next service.

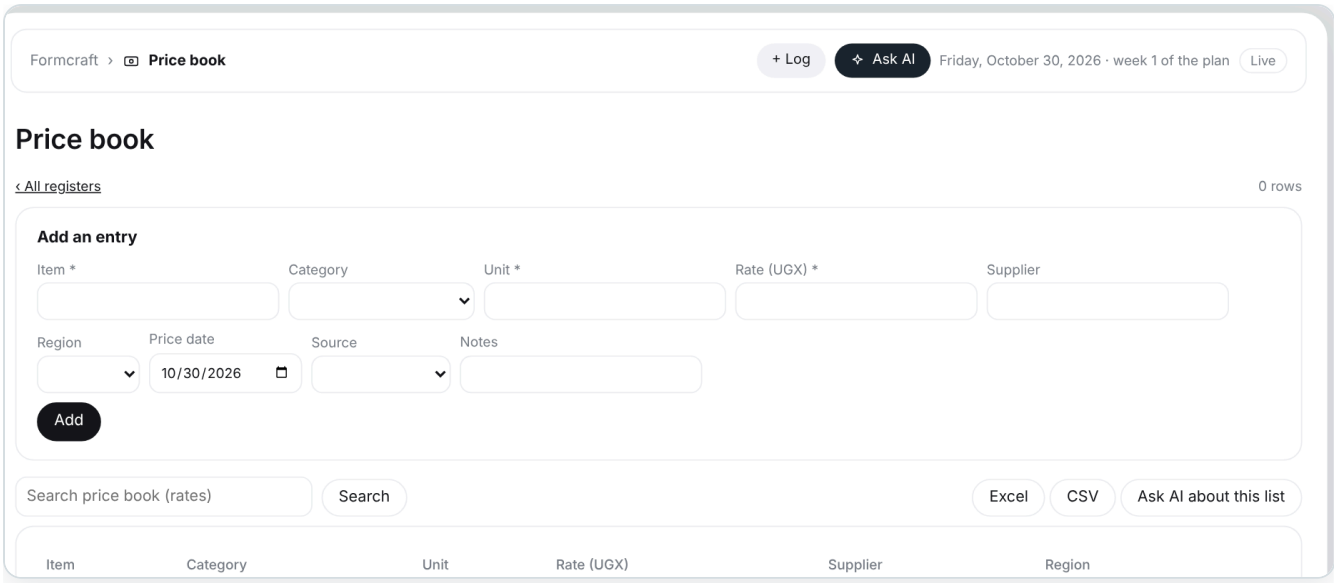

The Price book register: add an entry, paste from Excel, search, export, or ask the AI about the list.

UNDER THE HOOD

One generic register engine drives all of them from schema strings (`REGS`): each register is a collection `reg_<name>` with typed fields. Dates in any register (expiry, due, next service) become alerts in the brief. Admin-only registers are locked in the database rules.

4.5 Control pages

Targets, impact, legal and risk, numbers, wins, and who can see what.

Targets CONTROL

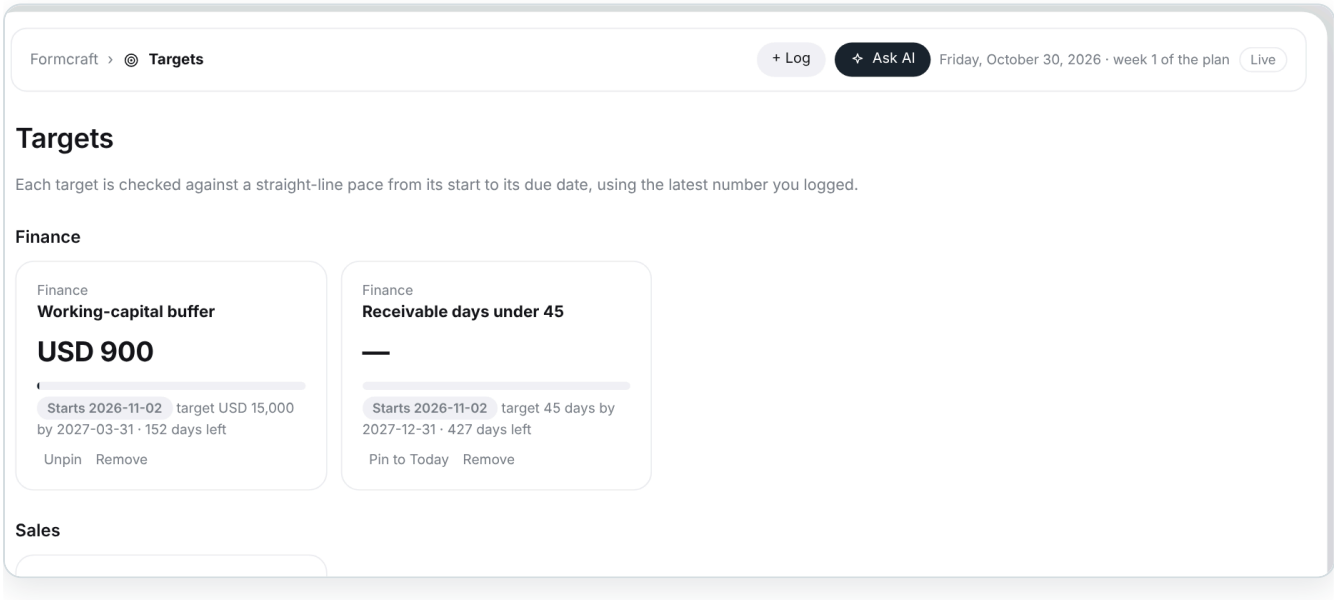

Each target is checked against a straight-line pace from its start to its due date, using the latest number logged. Pinned targets show on the brief.

HOW TO USE IT

1. Add a target with a metric, start, due and target value; pin the few that matter most.

UNDER THE HOOD

Collection: targets {metric, target, baseline, start, due, pinned}; status from log.

Impact CONTROL

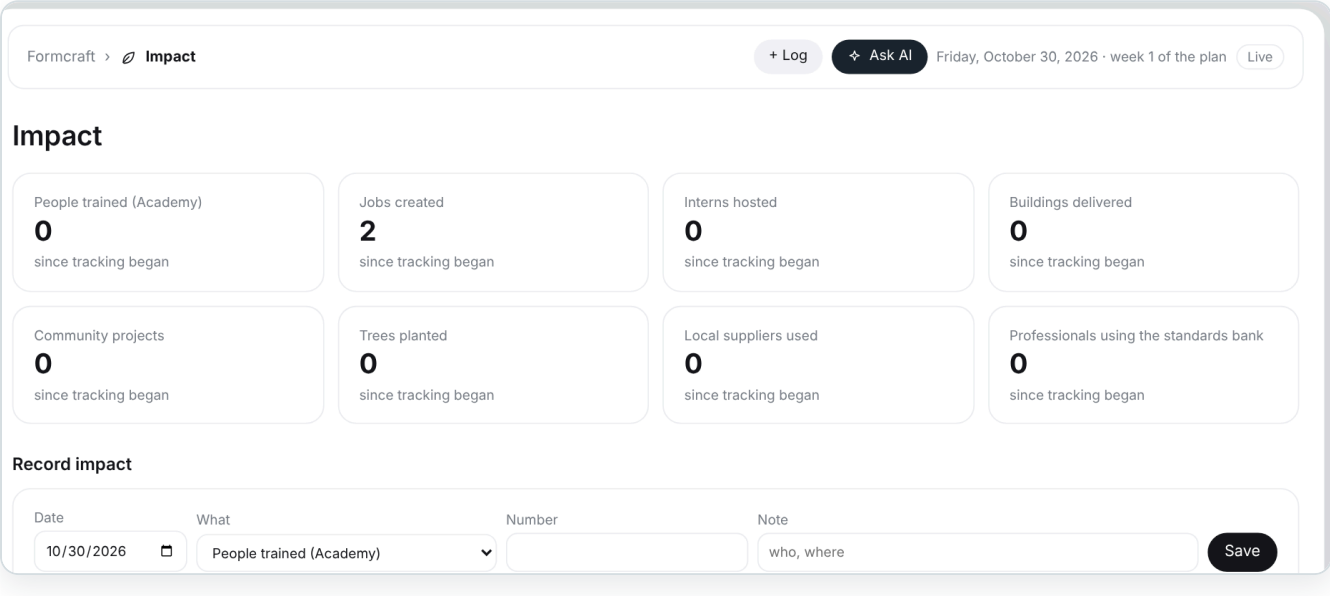

What Formcraft does for people and places: people trained, jobs created, interns, buildings delivered, community projects, trees planted, local suppliers used, professionals using the standards bank.

HOW TO USE IT

1. Log each as it happens.

UNDER THE HOOD

Collection: impact {date, type, value}.

Legal and risk CONTROL

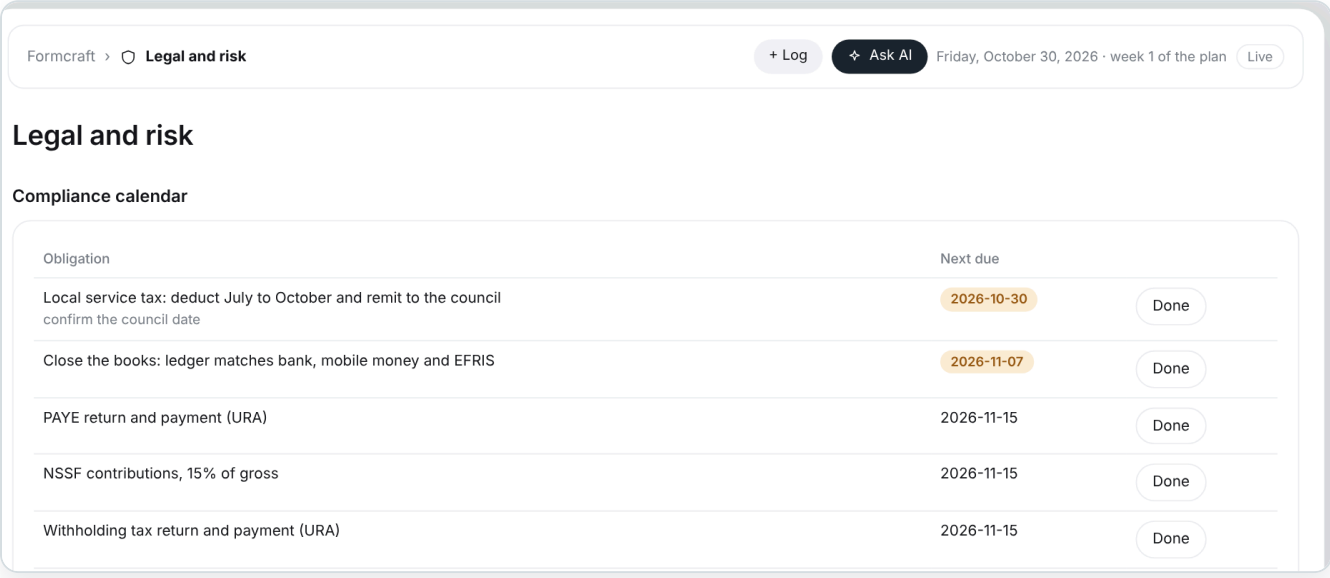

Legal and risk: the compliance calendar (PAYE, NSSF, WHT, VAT, books close, local service tax, provisional tax, URSB annual return, PDPO renewal, professional registrations) and the risk register with likelihood × impact.

HOW TO USE IT

1. Tick each obligation as done; it rolls to the next date.
2. Review the top risks monthly.

UNDER THE HOOD

Compliance dates from OBLIG; collection risks {t, area, l, i, m, owner, review}.

Log and deadlines CONTROL

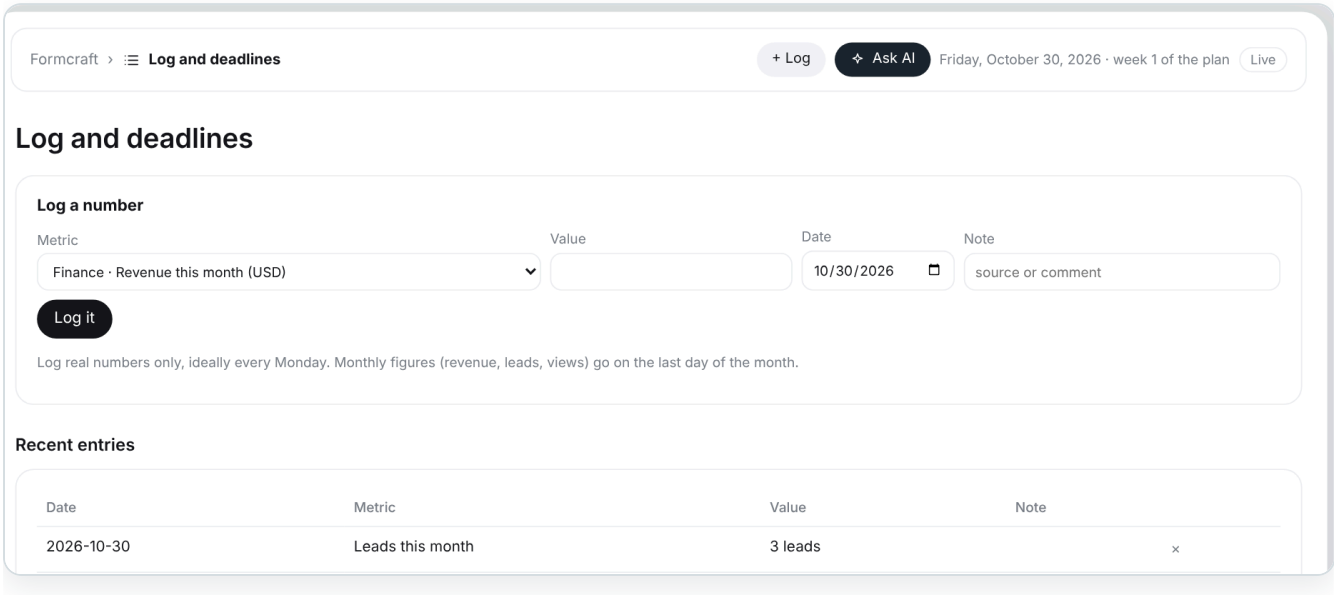

Log any number the business tracks (revenue, cash, leads, win rate, milestones on time, subscribers, recipes released...) and keep deadlines.

HOW TO USE IT

1. Pick the metric, enter the value. The + Log button in the header does the same from any page.

UNDER THE HOOD

Collections: log {metric, value, date, src} and deadlines. METRICS defines each metric's unit, direction and area.

Wins CONTROL

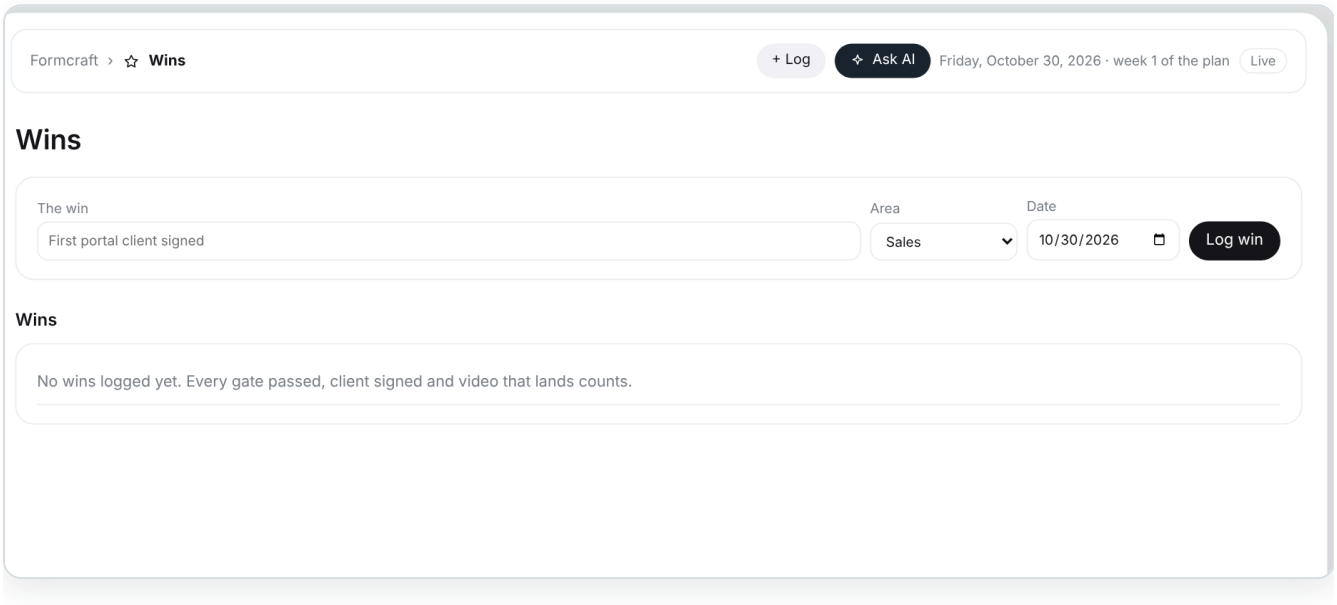

Every win logged: a gate passed, a client signed, a video that landed.

HOW TO USE IT

1. Log wins as they happen. Read them in the monthly review.

UNDER THE HOOD

Collection: wins.

Team and access CONTROL

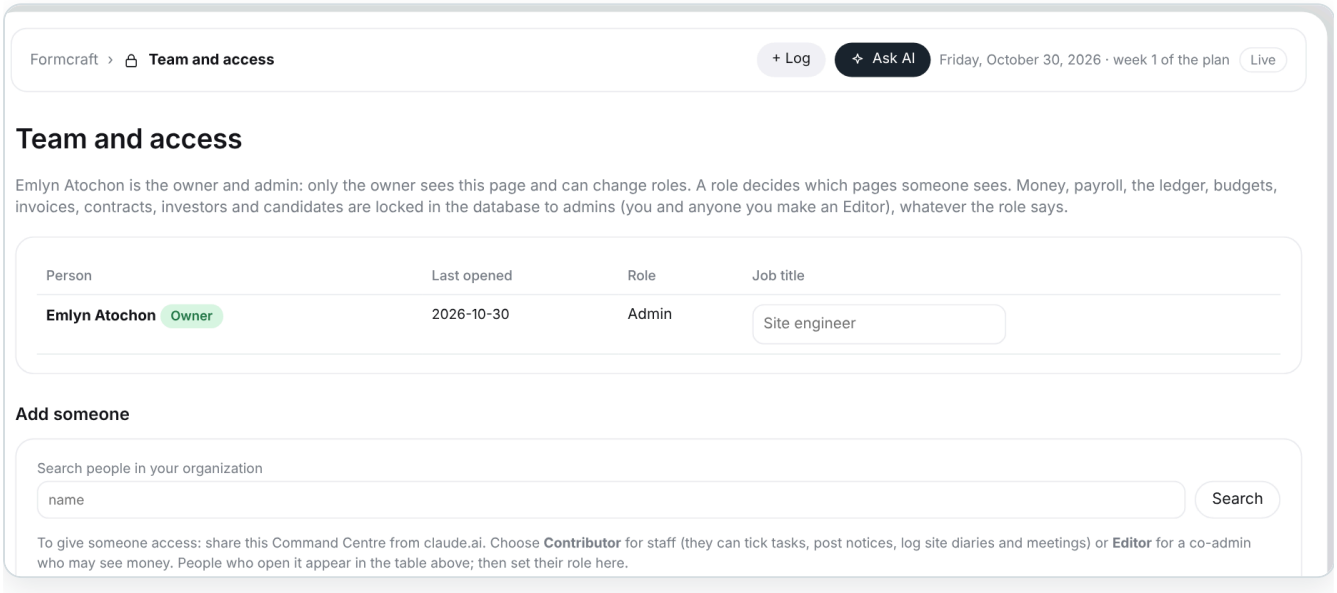

Who can see what. The owner sets each person's role (Admin, Manager, Finance, Design and BIM, Site, Sales and content, Staff, Partner) and which tabs each founder sees. Money, payroll, the ledger, budgets, invoices, contracts, investors and candidates are locked to admins in the database whatever the role. Also the full backup, restore and clean slate.

HOW TO USE IT

1. Share the Command Centre from claude.ai (Contributor for staff, Editor for a co-admin), then set the role here.
2. Download a full backup (JSON) every week.
3. Restore from a backup with Restore or move.

UNDER THE HOOD

ROLE_PAGES maps roles to pages; settings.tabs[uid] narrows a founder's tabs. Database rules enforce admin-only collections.

Standards bank: a search in action

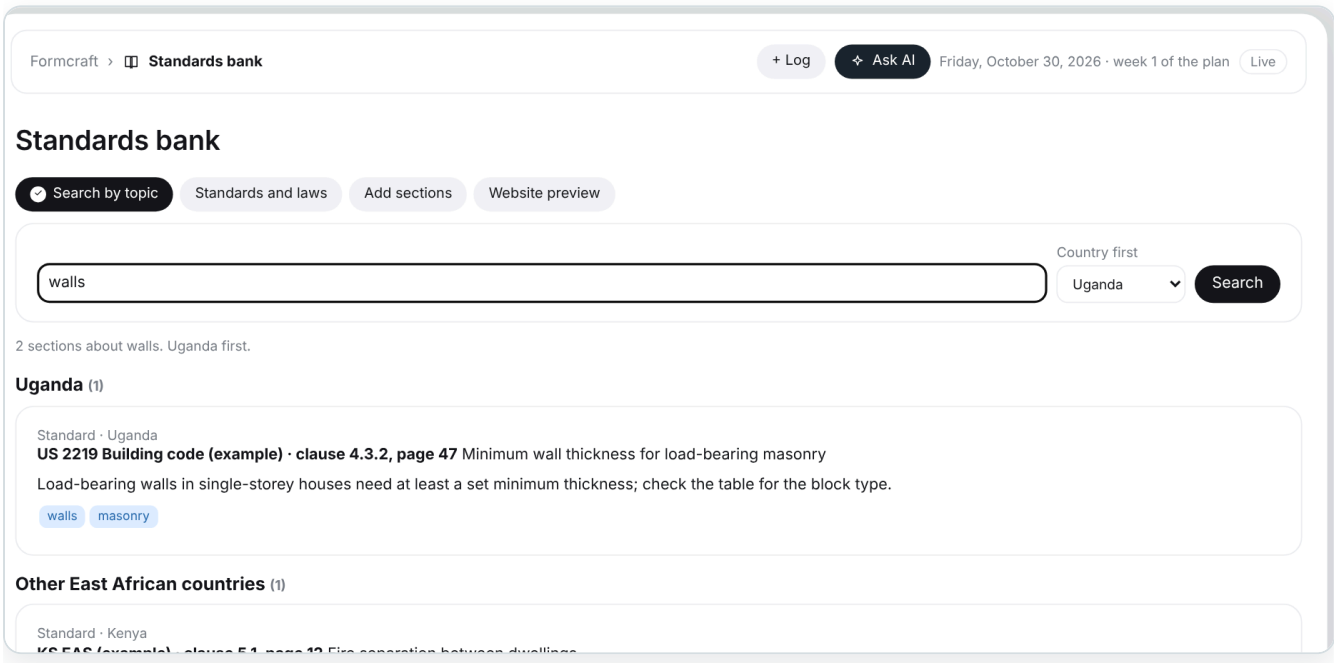

Searching "walls" with Uganda first: the clause, the page and a short summary in our own words. The standard itself is never shared.

PART 5

How the work flows

The main journeys through the system, step by step: from a lead to cash, from a sketch to a building, from a topic to a subscriber.

Formcraft
DESIGN & CONSTRUCTION

5 Lead to cash

The journey that pays for everything. Every arrow is measured on the Flowcharts page; the weakest one is where to work this week.

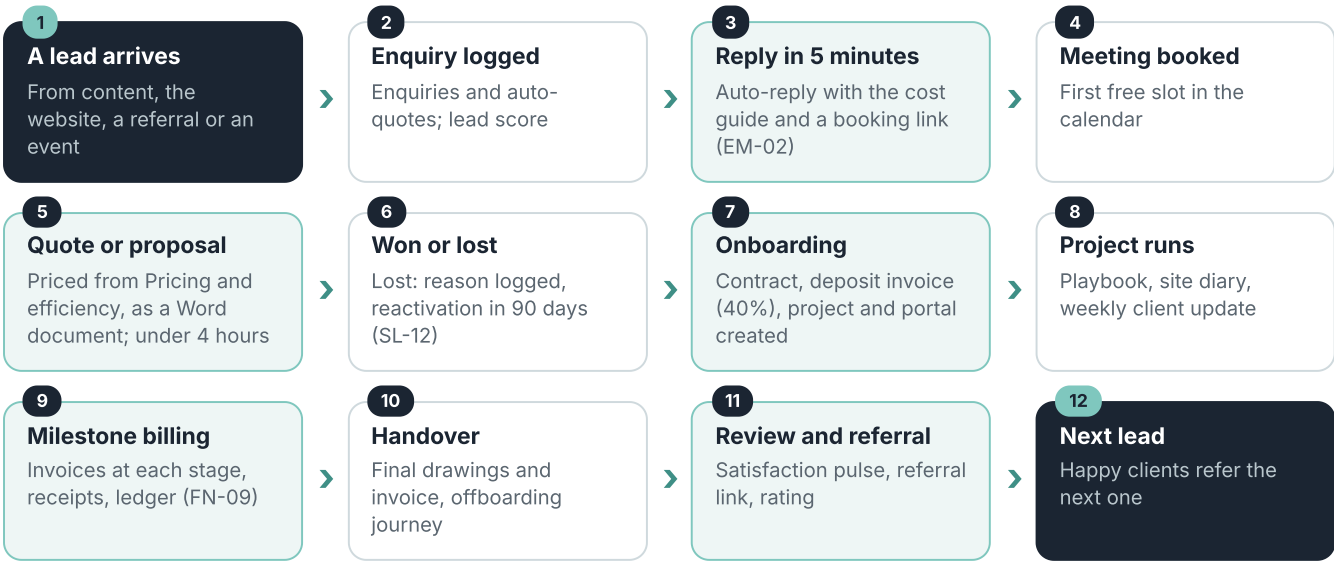

Client onboarding, step by step (Studio design)

Step	Owner	Day	Template or register	Automated
Log the enquiry, qualify it and send the auto-reply	Sales	0	Enquiries	Auto-reply and lead score
Book the discovery call or site visit from the free calendar slots	Sales	1	Calendar	Auto-booking
Send the design brief questionnaire	Studio lead	1	FMC-STU-BRF	Auto-send
Collect client details: ID or company papers, TIN, land title or lease copy, contacts	Admin	3	Clients register	Client form
Send the fee proposal and scope (RIBA stages, deliverables, revisions included)	Studio lead	3	FMC-SLS-PRP	AI drafts from the brief
Sign the design services agreement (fees, stages, IP and licence of drawings, data consent)	Director	5	Contracts register	by hand
Issue the deposit invoice and confirm payment and receipt	Finance	7	Invoice, receipt	Payment confirmation and auto-receipt
Create the project, its folder and the client portal access	Studio lead	7	Project hub	Auto-create on payment
Send the welcome pack: team, timeline, how we communicate, meeting rhythm, what we need from the client	Studio lead	7	Welcome pack	AI drafts

Hold the kick-off meeting and send the minutes	Studio lead	10	Meetings	AI minutes
Order the survey and soil test where needed	Studio lead	14	Purchase orders	by hand

The same kind of journey, with its own steps, exists for Construction and design-and-build, Concrete, Stores, BIM services, Formcraft Tools and families, and Advisory, each with an offboarding journey.

Sketch to building

Design moves from a fast 2D sketch, which the client can see and comment on, to a Revit model, checked drawings and the authority approval, without retyping anything.

1. **Brief and site** — Questionnaire, survey, planning rules
2. **Sketch in the studio** — Walls, rooms with target areas, doors, windows, dimensions
3. **Client comments** — On the same board, as pins
4. **Design assistant** — "Move the kitchen wall 300 mm left": edits are logged and undoable
5. **Revision sheets** — Rev A, B, C with a decision log
6. **Hand-off file** — fmc-cis/0.2: outline, walls, openings, decisions
7. **Revit builds it** — The plugin creates walls and rooms (planned command)
8. **BIM model** — Families from the factory; Gate A model check
9. **Standards check** — Clauses from the standards bank
10. **Approval guide** — Steps, documents, fees for the authority
11. **Approval** — Real approval times reported back
12. **Construction** — Playbook and site diary

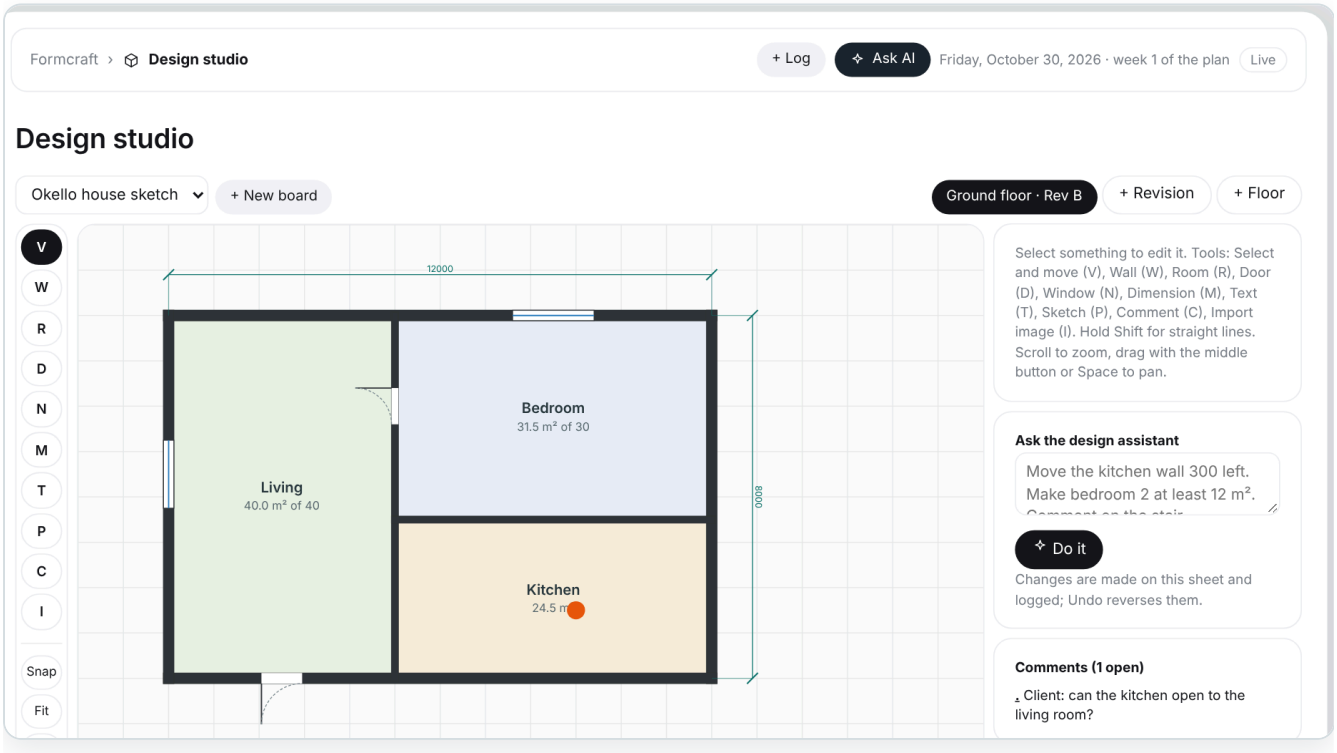

The Design studio: a sketch at Rev B with a client comment pinned in the kitchen. Example data.

The content factory

The goal: **2,000 YouTube subscribers by 31 December 2027**, about 143 new subscribers a month. The engine is three Revit Shorts and one longer tutorial a week, produced mostly by automation, with Esther approving.

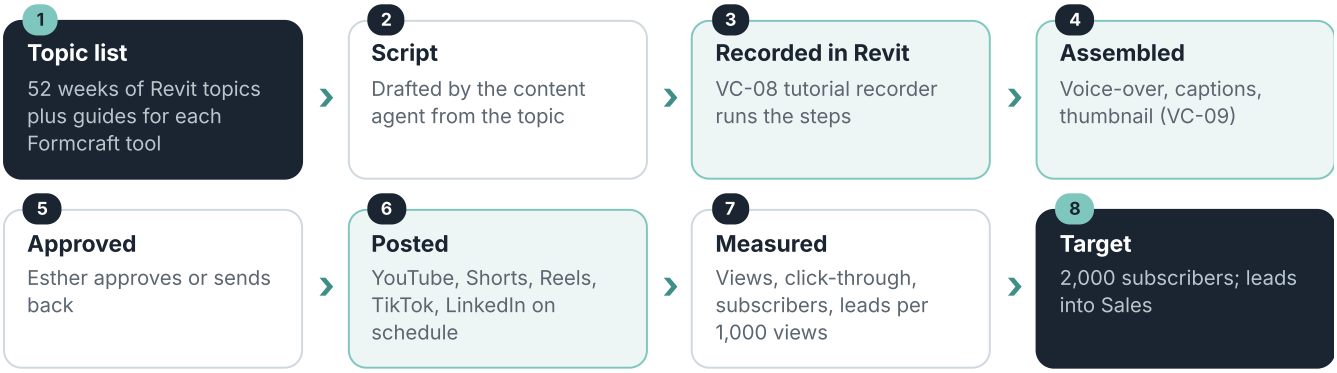

Events

One event a month for Formcraft, one a quarter for each founder. The event finder (DD-14) searches weekly; you pick, go, and mark Attended; a follow-up task makes sure the people you met reach Sales and the directory.

Standards bank

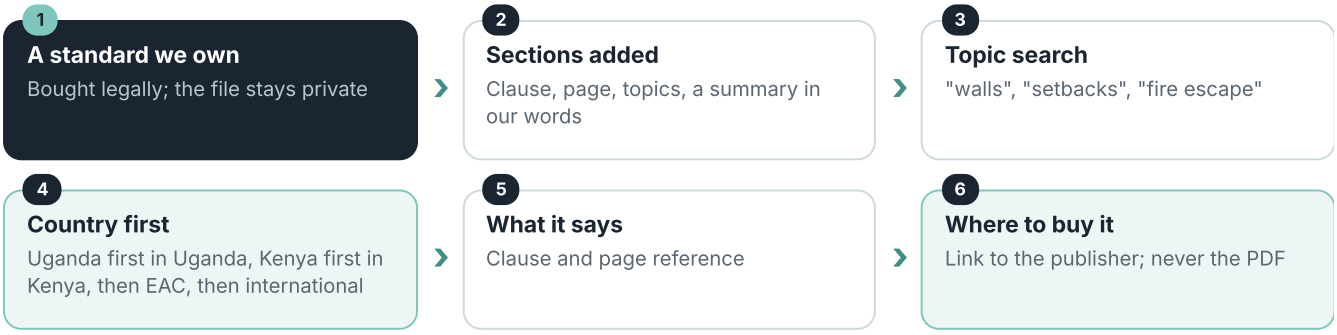

Professionals directory

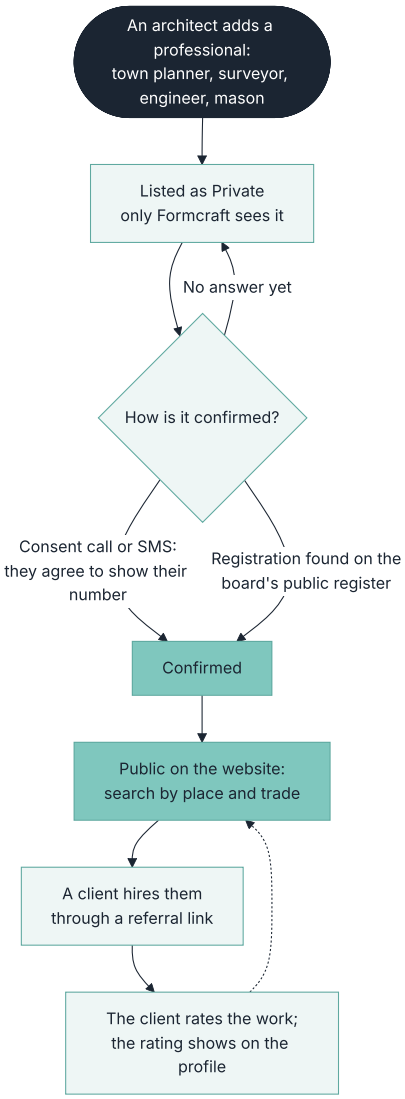

Figure 5.1 · Confirm first: nobody is public until they agree or their registration is checked.

The money cycle

1. **Price** — Pricing sets the rate the plan needs
2. **Quote** — Auto-quote, deposit 40%
3. **Invoice** — Numbered from the template register
4. **Paid** — Mobile money or bank; receipt sent
5. **Ledger** — Income and expenses with receipts
6. **Forecast** — 12 months; USD 15,000 buffer
7. **Tax** — PAYE, NSSF, WHT by the 15th; VAT once registered
8. **Report** — Monthly pack; profit and cash

How AI work becomes scripts

1. **AI does a job** — Logged with its intent, inputs and result
2. **Third time** — Same intent, similar inputs, three times
3. **Script written** — Developer agent writes it with tests
4. **Approved** — Emlyn approves in the development room
5. **Runs free** — Level 0 from now on
6. **Watched** — A failed check pauses it; AI takes over until fixed

PART 6

Automations and bots

All 128 automations on the journey, by group, and how each one moves from an idea to live.

Formcraft
DESIGN & CONSTRUCTION

6 The automation catalogue

Each automation is written once as a recipe (trigger, steps, checks, who reviews), then built, tested and switched on. Seventy of them have an upgrade that adds context from another register, so they reason instead of only reminding. Build the basic version first.

1 **Idea** — Described with a trigger and hours saved

2 **Planned** — Recipe written; phase set

3 **Building** — Script or flow made

4 **Testing** — Runs alongside a person

5 **Live** — Runs on its own; sampled weekly

6 **Paused** — Stopped after a failed check

Group	Automations (code and name)
Email 12 automations	**CJ-01** Client onboarding · **CJ-02** Client offboarding · **CJ-03** Journey step reminders · **EM-01** Inbox triage · **EM-02** Lead reply in 5 minutes · **EM-03** Lead nurture sequence · **EM-04** Weekly client update · **EM-05** Invoice and payment reminders · **EM-06** Supplier quote requests · **EM-07** Monthly newsletter · **EM-08** Recruitment replies · **EM-09** Tools customer emails
Social media 6 automations	**SM-01** Comment replies · **SM-02** DM and WhatsApp assistant · **SM-03** Scheduled posting · **SM-04** Repurpose long videos · **SM-05** Trend and competitor watch · **SM-06** Social reports
Video and content 9 automations	**VC-01** Video topic generator · **VC-02** Title and thumbnail packaging · **VC-03** Script writer · **VC-04** B-roll from the model · **VC-05** Edit assembly · **VC-06** Captions and translations · **VC-07** Upload and metadata · **VC-08** Revit tutorial recorder · **VC-09** Tutorial assembly
Founder voice and brand 5 automations	**FV-01** Founder voice profile · **FV-02** Voice-over from script · **FV-03** Founder posts and articles · **FV-04** Brand guideline checker · **FV-05** Document generator
Sales and leads 15 automations	**CS-01** Voice receptionist bot · **CS-02** Call notes to CRM · **CS-03** Customer service chat · **SL-01** Lead capture to CRM · **SL-02** Follow-up reminders · **SL-03** Instant estimate · **SL-04** Quote builder · **SL-05** Referral and review requests · **SL-06** Tender finder · **SL-07** Proposal builder · **SL-08** Meeting scheduler · **SL-09** Review collector · **SL-10** Win and loss reasons · **SL-11** Client touchpoint cadence · **SL-12** Lost deal reactivation
Clients and projects 6 automations	**CJ-04** Satisfaction pulse · **CP-01** Portal model publishing · **CP-02** Site diary from WhatsApp · **CP-03** Weekly site report · **CP-04** RFI and variation drafts · **CP-05** Handover pack
Finance 14 automations	**FN-01** Bank and mobile money import · **FN-02** EFRIS invoice issue · **FN-03** Receipt capture · **FN-04** Monthly close and pack · **FN-05** Tax payment preparation · **FN-06** Payment confirmation · **FN-07** Receipts to clients · **FN-08** Receipt chaser for staff spending · **FN-09** Milestone billing · **FN-10** Budget burn and overrun forecast · **FN-11** Year-end close · **FN-12** Subcontractor payment check · **FN-13** 8-week cash forecast · **FN-14** Mobile money float alert
People 7 automations	**PP-01** Payroll run · **PP-02** Daily stand-up digest · **PP-03** Meeting minutes · **PP-04** Onboarding kit · **PP-05** CV screening · **PP-06** Utilisation and load forecast · **PP-07** Certificate and induction expiry
Software and data 11 automations	**PL-01** Revit and desktop plugin bridge · **SD-01** GitHub to Command Centre · **SD-02** Test runner and alerts · **SD-03** Family factory night run · **SD-04** Model-swap drill · **SD-05** Backups · **SD-06** Licence server · **SD-07** Template usage and retirement · **SD-08** Model health check (Gate A) · **SD-09** System health and AI check · **SD-10** Product idea scout

Website and SEO 8 automations	**WS-01** Search Console feed · **WS-02** SEO page writer · **WS-03** Standards bank indexer · **WS-04** Uptime and speed watch · **WS-05** Professional confirmation sender · **WS-06** Approval times digest · **WS-07** Public data publish · **WS-08** Referral follow-up for ratings
Operations 10 automations	**OP-01** Tender deadline tracker · **OP-02** RFI ageing and chase · **OP-03** HSE incident clock · **OP-04** Permit expiry watch · **OP-05** QA checklist at milestones · **OP-06** Drawing revision control · **OP-07** Stock reorder · **OP-08** Standards change impact · **OP-09** Defect close-out check · **OP-10** Plant and tool maintenance
Data, scrapers and documents 14 automations	**DD-01** Price scraper · **DD-02** Tender scraper · **DD-03** Market and competitor scraper · **DD-04** Standards catalogue scraper · **DD-05** PDF digester: standards · **DD-06** PDF digester: quotes, invoices and receipts · **DD-07** PDF digester: tender documents · **DD-08** PDF digester: contracts · **DD-09** Client sketch and survey reader · **DD-10** File bank auto-tagger · **DD-11** Holiday poster scheduler · **DD-12** Document generator · **DD-13** Weekly data backup · **DD-14** Event finder
Alerts and accountability 11 automations	**AL-01** Morning accountability brief · **AL-02** Task start and due alerts · **AL-03** Phone call for missed P1 tasks · **AL-04** Weekly report and coaching · **AL-05** Monthly board pack · **AL-06** Reports by email · **AL-07** Decision review · **AL-08** Risk register refresh · **AL-09** KPI snapshot against the plan · **AL-10** Project lessons to standards · **AL-11** Event follow-up

Total: 128. The full description, trigger, tools and hours saved for each are on the Automations and bots page.

The first ten to switch on

The automations that bring in or protect cash come first: they pay for the rest.

Code	Automation	Why first
EM-02	Lead reply in 5 minutes	Speed wins leads
SL-01	Lead capture to CRM	No lead is lost
SM-02	DM and WhatsApp assistant	Where Ugandan clients write
EM-01	Inbox triage	Frees founder hours every day
FN-09	Milestone billing	Cash arrives on time
SM-03	Scheduled posting	Content goes out without a person
VC-08	Revit tutorial recorder	The subscriber engine
AL-09	KPI snapshot against the plan	The founders see the truth weekly
SD-09	System health and AI check	Catches failures early
DD-01	Price scraper	Quotes on current prices

PART 7

The development plan

What is built, what comes next, and the rules for building it: from the Command Centre today to the Formcraft Hub for Windows.

Formcraft
DESIGN & CONSTRUCTION

7 Where we are

Part	State	What it is
Command Centre	Running	The app in this guide: one file, running in claude.ai with its own database. Tested with automated browser tests before every release.
Web version	Built, not deployed	The same app on Firebase (Firestore, Auth, Storage) with an AI adapter for any provider, installable on phones and PCs. For employees.
Formcraft MCP server	Built, not in daily use	Lets Claude Desktop or any AI tool read the brief, query registers, propose actions and keep memory, with approvals.
Formcraft Tools for Revit	In development	C# add-in plus its own MCP server; supports several Revit windows.
Website	Live	React and Firebase; will host the standards bank, approvals guides and directory.
Formcraft Hub for Windows	Planned	The founders' app and the MCP hub for everything (below).
Automations	0 of 128 live	All designed with recipes; none switched on yet.

The roadmap

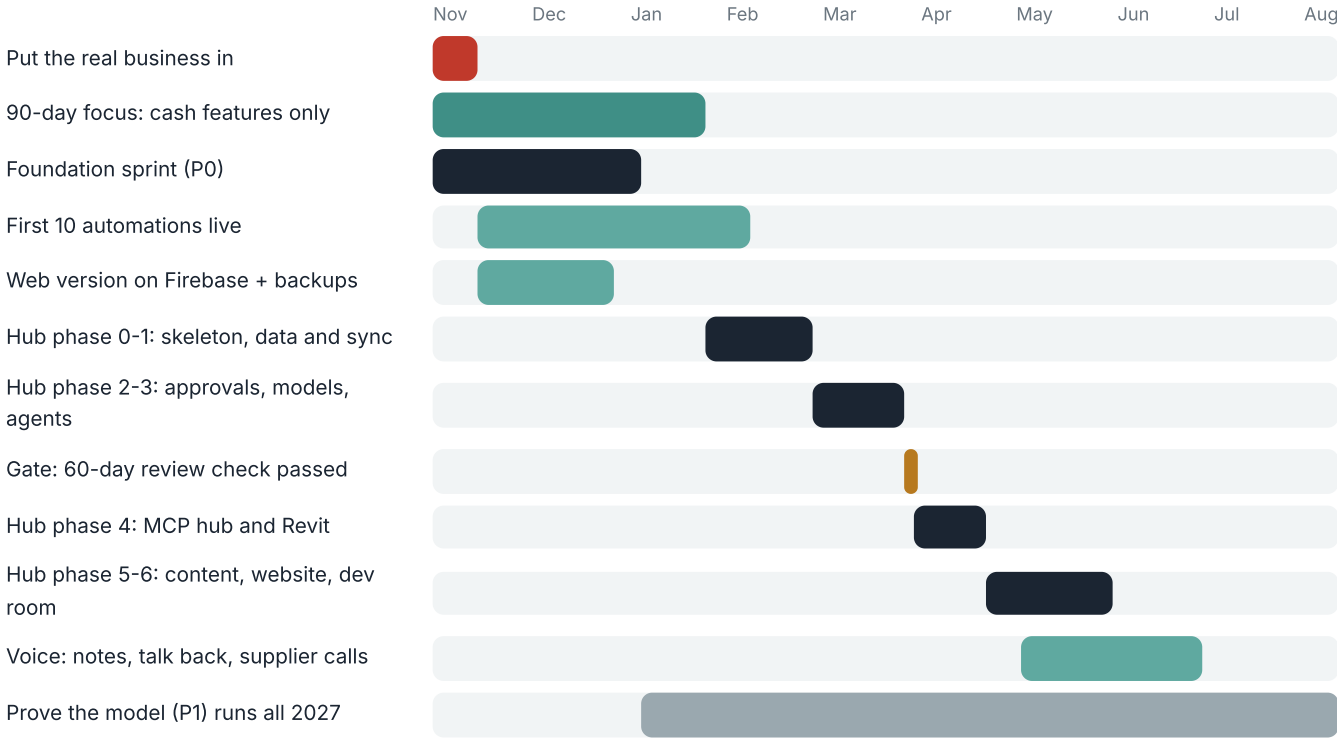

November 2026 to August 2027. The hub is about 18 weeks of part-time work for one developer; it starts after the 90-day focus, and phase 4 waits for the review gate.

The 90-day focus rule

> For the next 90 days we build **only what brings in or protects cash**: the proposals and pricing engine, the first ten automations, the Revit tutorials for the channel, the family store, backups and the Firebase move. Everything else waits. The audit found the plan's biggest risk is building tools instead of selling.

Foundation sprint, week by week

Week of	Work
2 Nov	Server tests, rulebook data model, IP and accounts
9 Nov	Server tests, journal and handover, standards register
16 Nov	Server release, funnel pages, first recipes
23 Nov	WhatsApp assistant, CRM, standards bank model
30 Nov	Client portal v1: accounts, project page, sign-off
7 Dec	Portal model viewer, content scripts, standards catalogue
14 Dec	Finance automation, script library, edge tests
21 Dec	Kit 1 release and swap drill
28 Dec	Gate review and plan Q1 2027

The Formcraft Hub for Windows

The Hub is the founders' app: the Command Centre inside a Windows program built the same way as Revit, holding all Formcraft data, connecting to AI models offline or in the cloud, and acting as the MCP hub every app connects through. Only the three founders have it; employees use the web version.

Area	Decision	Why
App	C# .NET 8 with WPF on `Formcraft.Shell`; Command Centre pages inside WebView2	One language and one look with the Revit tools; official C# MCP SDK
Online data	Firebase: Firestore, Auth, Storage, Functions, Hosting	The website and the web version already use it
Local data	PostgreSQL on each hub	Years of history, SQL reports, change log, recovery
Offline AI	7-8B model (Q4) for the default tier, 3-4B for quick, on the main PC	Fits 16 GB RAM and a 4 GB graphics card
Cloud AI	Any provider through one adapter, by tier	Swapping is a setting
Jobs	Hangfire queues, YARP routing, Polly retries	Load balancing, retries, health checks every 30 s
Revit	Existing add-in; each window on a port 8080-8089	Two or more Revit windows run jobs in parallel
Updates	Velopack installer and auto-update	All three hubs stay on the same version

Phase	Weeks	Delivers	Done when
0 Skeleton	1-2	Solution, service and tray app, PostgreSQL, Firebase sign-in, Command Centre in WebView2	Starts on boot; restarts after a crash; all three founders sign in
1 Data and sync	3-5	Firestore ↔ PostgreSQL mirror, change log, outbox, roles, nightly backups	An edit shows on the others in 5 s; 50 offline edits sync in order; a restore drill passes
2 Approvals and monitor	6-7	Shared approval queue with risk rules, the monitor screen, review sampling, purpose and context packs	A high-risk action waits for two founders
3 Models and agents	8-9	Level router, escalation, answer cache, budgets, the 8 agents, memory and handover	Works with no internet; falls back to the cloud; unloads the model when Revit starts
Gate		Founders decide every proposal within 24 hours, nothing waits over 48 (the 60-day review check)	
4 MCP hub and Revit	10-12	Connection registry, the hub's MCP server, per-window Revit queues, lease and failover	Jobs run on both Revits; a frozen Revit's jobs move; the standby takes over

5 Content and website	13-15	Social calendar and posting, newsletters, website publishing, enquiries, orders	A post goes from draft to posted with metrics
6 Dev room and installer	16-18	GitHub, test runs, builds and releases, script promotion, installer and auto-update	An update reaches all three hubs

UNDER THE HOOD

Solution `Formcraft.Hub.sln` : `Hub.Core` (types, roles, risk policy) · `Hub.Data` (Npgsql + EF Core, change log, outbox) · `Hub.Sync` (Firestore listeners, lease and heartbeat) · `Hub.Jobs` (Hangfire, router, Polly) · `Hub.Mcp` (MCP client registry and server) · `Hub.Models` (Ollama and cloud adapters, keys in Credential Manager) · `Hub.Revit` (instances, per-window queues, guard rules) · `Hub.Content` · `Hub.Dev` · `Hub.Service` (background host) · `Hub.App` (WPF). Main hub writes a heartbeat to `hub/lease` every 30 s; if it is 5 minutes old the standby founder PC takes the lease and runs cloud-only jobs. Payment confirmations and website auto-replies run in Firebase Functions so they never wait for a PC. Full plan: `docs/windows-hub-plan.md`.

Revit, voice and the rules for building

A simpler Revit plugin

The plugin keeps only what needs the live model: the open document, the current view or selection, or a one-click action while modelling. Settings, data, queues, reports and work across apps move to the Hub. Designers get a lighter plugin; the Hub controls development and testing of the tools.

Voice

- **Transcription and voice notes:** speak a site note or a meeting; it becomes text, tasks and log entries.
- **Talk to the system:** ask aloud, hear the answer.
- **Founder voices:** cloned only with the founder's written consent, used for tutorials and voice-overs.
- **Supplier price calls:** an automated call asks today's price; the answer updates the price book.
- **Directory checks:** a call asks a professional to confirm their details and consent to show their number.
- **Rules:** every automated call says it is an automated assistant for Formcraft, and recordings follow the data protection law.

Rules for building

Build only what gets used

A feature is built when someone will use it this month. Otherwise it waits in the Build list.

Test every change

Every release of the app passes the syntax check and the browser tests (no page errors) before it is published.

One source of rules

Rulebooks and guard rules live in one place; every app reads them, none keeps a copy.

Write it down

Every request and decision is logged (`docs/requests-log.md`, Decisions and learning), so the next person, or the next AI, knows why.

PART 8

The honest gaps

What is missing between the plan and the system, and the next 30 days that close the most important ones.

Formcraft
DESIGN & CONSTRUCTION

8 The gaps, ranked

An honest audit of the live system on 30 October 2026, ranked by how much each gap could stop the plan.

#	Gap	What we found	Fix
1	**The system holds no real business yet**	No deals, projects, ledger entries or logged numbers. Every dashboard and simulation runs on nothing.	One week: put the real business in (Part 3).
2	**More is being built than sold**	About 65 pages, 128 automations and 28 AI roles designed; none live; one developer who also runs Revit tools, the website and client work.	The 90-day focus rule.
3	**Legal papers not proven done**	IP assignment to the company, shareholders' agreement with vesting, registration confirmed, Personal Data Protection Office registration.	Sign and upload them; tick them on Legal and risk.
4	**No professional sign-off workflow**	AI drafts layouts, BOQs and checks, but nothing records who signs drawings; no professional indemnity or contractor's all-risks insurance recorded.	Add a sign-off step for drawings; buy the insurance.
5	**One account, one PC**	All data under one claude.ai account; backups not routine yet.	Weekly backup; move to Firebase.

Real, but not plan-stopping

- **Revenue engine:** the USD 1M target is not yet turned into weekly numbers per division (leads, quotes, wins, job size); the proposals engine is not built; family pricing and checkout are not decided.
- **Cash:** no real 13-week cash forecast and no funding pipeline entered.
- **Construction capacity:** AI cannot pour slabs: crews, foremen, subcontractors and equipment for a second site are not planned.
- **The founders' review rhythm:** roles not confirmed, standby PC not chosen, and the review queue needs decisions within 24 hours.
- **Clients:** the client portal, client access to the studio and after-sales follow-up are planned, not built.
- **The app's size:** one large file; a feature freeze and tests on every change are now in place. (This guide's own checks found and fixed a bug that blanked the money totals.)

The next 30 days

1. **Real data in** — Pipeline, projects, cash, this month's money, leads and subscribers
2. **Legal papers** — IP assignment, shareholders' agreement, registration, data protection
3. **Sales numbers** — Weekly targets per division from the USD 1M goal; build the proposals engine
4. **Backups and Firebase** — Weekly backup; move the data
5. **Founders reviewing** — Confirm roles; agree a daily review time
6. **Feature freeze** — Only what feeds cash until February

Decisions we need from the founders

1. Confirm each founder's role and the USD 500 two-founder threshold.
2. Choose the standby PC (Peter's or Esther's).
3. Choose the newsletter email service (for example Brevo, Mailchimp or Resend).
4. Agree the daily review time and who covers when someone travels.
5. Agree family and Formcraft Tools pricing (subscriptions and checkout).
6. Agree what the design studio shows clients (their own boards only).

A Appendix: glossary and technical reference

Term	Meaning
Agent	An AI given one area (finance, sales…), its rulebook and tools. It proposes; founders approve.
Approval	A founder's yes or no to something an agent proposed. Stored in the pending queue.
Automation	A job that runs by itself on a trigger: an email, a date, a form. Built from a recipe.
BIM	Building Information Modelling: a 3D model that carries data (quantities, cost, time).
Collection	One kind of record in the database, like one sheet in a workbook.
Context pack	What the hub gives an AI before a job: the scripts, memory lines and rules it needs, nothing more.
Family	A Revit component (a door, a bed, a clinic fitting). The family factory makes them in batches.
Firebase	Google's online database and sign-in service, used by the website and the web version.
Gate A	The model check every Revit model and family passes before it is used.
Handover pack	Memory, rules and state in one file, so another AI or a new hire continues from it.
MCP	Model Context Protocol: the standard way AI tools connect to apps. Our MCP server gives AIs Formcraft's tools.
Offline model	An AI that runs on our own PC, free and without internet (7-8B parameters).
Recipe	A written rule for a job: trigger, steps, checks, reviewer. Every automation starts as one.
Register	A list the business runs on: clients, suppliers, price book, contracts…
RIBA stages	The standard design and construction stages 0 to 7 used for projects.
Rulebook	An agent's written rules, kept in our repository so any model can follow them.
Tier	Which AI model size does a job: offline, quick, default, complex, second opinion.
Token	The unit AI providers charge by: about four characters of text.

Where everything is

Path (repository formcraft_pioneer)	What it is
`command-centre/index.html`	The Command Centre app (one file)
`command-centre/standalone/`	Web version: Firebase runtime, AI adapter, rules, installable app files
`mcp-server/server.js`	The Formcraft MCP server
`rulebooks/agents/*.md`	Each agent's rulebook
`rulebooks/client-onboarding-offboarding.md`	The 7 client journeys

`docs/command-centre.md`	Feature reference for every page
`docs/windows-hub-plan.md`	The Hub plan (sections 1-17)
`docs/architecture-ai-hub.md`	AI hub architecture and the offline model
`tools/test_*.js`, `tools/check_syntax.sh`	Browser tests and the syntax check run before each release
`simulations/`, `feasibility/`	The simulations and the feasibility report

Design studio keys

Key	Tool	Key	Tool
V	Select and move	**M**	Dimension
W	Wall	**T**	Text
R	Room	**P**	Sketch
D	Door	**C**	Comment
N	Window	**I**	Import image
Shift	Straight lines	**Space**	Pan (or middle button)

Formcraft
DESIGN & CONSTRUCTION

Formcraft Design and Construction · Kampala · 30 October 2026
This guide is updated with each release of the Command Centre.
